

Fond du Lac Line 4 Project

Application for Pipeline Routing Permit and Partial Exemption

Minnesota Public Utilities Commission

Appendix B

Enbridge Environmental Protection Plan



Environmental Protection Plan

Enbridge Energy, Limited Partnership • Fond du Lac Line 4 Project

This page intentionally left blank

TABLE OF CONTENTS

INTRODUCTION 1

1.0 GENERAL MITIGATION MEASURES 3

1.1 IDENTIFICATION OF AVOIDANCE AREAS..... 3

1.2 CONSTRUCTION LINE LIST AND PERMITS 3

1.3 WET WEATHER SHUTDOWN 3

1.4 RIGHT-OF-WAY ACCESS..... 3

1.5 RIGHT-OF-WAY REQUIREMENTS..... 4

1.6 CONTROLLING SPREAD OF UNDESIRABLE SPECIES..... 5

 1.6.1 Prevention and Control Measures 5

 1.6.2 Pesticide Use and Application 6

1.7 POTHOLING/HYDROVAC SLURRY 7

1.8 UPLAND CLEARING 7

 1.8.1 Disposal of Non-Merchantable Timber 7

 1.8.2 Disposal of Merchantable Timber 7

 1.8.3 Upland Grading and Stump Removal..... 7

1.9 TEMPORARY EROSION AND SEDIMENT CONTROLS 7

 1.9.1 Temporary Stabilization 8

 1.9.2 Erosion Control Blanket 8

 1.9.3 Mulch 8

 1.9.4 Cat Tracking 9

 1.9.5 Temporary Slope Breakers..... 9

1.10 UPLAND TOPSOIL SEGREGATION 10

1.11 UPLAND TRENCHING 11

 1.11.1 Timing..... 11

1.12 FOAM PILLOW INSTALLATION 11

1.13 TRENCH BREAKERS 11

1.14 DRAIN TILE INLET PROTECTION AND TILE REPAIRS 12

1.15 UPLAND BACKFILLING 12

1.16 CLEANUP AND ROUGH/FINAL GRADING..... 12

 1.16.1 Timing..... 13

1.17 PERMANENT EROSION AND SEDIMENT CONTROLS 13

1.18 SOIL COMPACTION TREATMENT 13

1.19 STONE REMOVAL 14

1.20 REPAIR OF DAMAGED CONSERVATION PRACTICES..... 14

1.21 LAND LEVELING FOLLOWING CONSTRUCTION 14

2.0 STREAM AND RIVER CROSSING GENERAL REQUIREMENTS..... 15

2.1 TIME WINDOW FOR CONSTRUCTION..... 15

2.2 CLEARING AND GRADING 15

 2.2.1 Beaver Dam Removal and Prevention of Dam Rebuilding..... 16

 2.2.2 Impaired Waters 16

2.3 ADDITIONAL TEMPORARY WORKSPACE 16

2.4 BRIDGES 16

 2.4.1 Types of Bridges..... 17

 2.4.2 Bridge Design and Maintenance..... 17

2.5 STREAM AND RIVER CROSSING CONSTRUCTION METHODS..... 17

 2.5.1 Wet Trench Method 17

 2.5.2 Dam and Pump Method..... 18

 2.5.3 Flume Method..... 20

2.5.4	Directional Drill and/or Guided Bore Method	21
2.6	PERMANENT RESTORATION	22
2.6.1	Vegetative Bank Restoration	22
2.6.2	Supplemental Bank Stabilization	22
2.6.3	Bridge Removal	22
2.6.4	Swales	23
3.0	WETLAND CROSSING GENERAL REQUIREMENTS.....	24
3.1	WETLAND ACCESS	24
3.2	CLEARING	24
3.3	ADDITIONAL TEMPORARY WORKSPACE IN WETLANDS	24
3.4	GRADING IN A WETLAND	25
3.5	RIGHT-OF-WAY STABILIZATION	25
3.6	TRENCHING	25
3.6.1	Topsoil Segregation.....	26
3.6.2	Trench Breakers	26
3.7	PIPELINE INSTALLATION.....	26
3.7.1	Push/Pull Method.....	26
3.7.2	Temporary Erosion and Sediment Controls.....	26
3.7.3	Concrete Coating.....	26
3.8	BACKFILLING	27
3.9	ROUGH GRADING, CLEANUP, AND TEMPORARY RESTORATION	27
3.9.1	Timing.....	27
3.9.2	Temporary Stabilization	27
4.0	HIGHWAY, ROAD AND RAIL CROSSINGS.....	28
4.1	ADDITIONAL WORKSPACE.....	28
4.2	MAINTENANCE	28
4.3	TEMPORARY EROSION AND SEDIMENT CONTROLS	28
5.0	CONSTRUCTION DEWATERING.....	29
5.1	TRENCH DEWATERING	29
5.1.1	Flow Measurement and Water Sampling.....	30
5.1.2	Regulatory Notification and Reporting	30
5.2	HYDROSTATIC TEST DISCHARGES.....	30
5.2.1	Refueling	30
5.2.2	Siting of Test Manifolds	30
5.2.3	Water Sampling	31
5.2.4	Best Management Practices.....	31
5.2.5	Flow Measurement	31
6.0	WATER APPROPRIATION	32
6.1	GENERAL	32
6.2	WATER SOURCES.....	32
6.3	FLOW MEASUREMENT	32
6.4	WATER SAMPLING	32
6.5	REGULATORY NOTIFICATION AND REPORTING	32
7.0	REVEGETATION & MONITORING.....	33
7.1	PROJECT SEED SPECIFICATIONS.....	33
7.2	TEMPORARY REVEGETATION.....	33
7.3	TIMING FOR TEMPORARY VEGETATION	34
7.4	MULCH.....	34
7.5	PERMANENT REVEGETATION.....	35
7.6	UPLAND CONSTRUCTION AREAS.....	35

7.7	PERMANENT SEEDING OF WETLAND AREAS	35
7.7.1	Unsaturated Wetland Areas.....	35
7.7.2	Saturated/Standing Water Wetlands	35
7.7.3	Forested Wetland Restoration	35
7.8	PERMANENT SEEDING OF WATERBODY BANKS	35
7.9	SPECIALIZED SEED MIXES	36
7.10	CONSERVATION RESERVE PROGRAM PROPERTIES	36
7.11	SEED BED PREPARATION AND SEEDING PROCEDURES	36
7.12	SEEDING METHODS	37
7.12.1	Drill Seeding	37
7.12.2	Broadcast Seeding	37
7.12.3	Hydroseeding.....	37
7.13	COMPANION CROPS.....	37
7.14	SOIL AMENDMENTS.....	38
7.15	SEEDING PERIODS	38
7.16	TIMING OF FINAL SEEDING.....	38
7.17	EROSION AND SEDIMENT CONTROL	38
7.18	DORMANT SEEDING	39
7.19	MANAGEMENT AND MONITORING.....	39
8.0	WINTER CONSTRUCTION	40
9.0	WASTE MANAGEMENT	41
9.1	HAZARDOUS WASTES.....	41
9.2	ABRASIVE BLAST DEBRIS.....	41
10.0	SPILL PREVENTION, CONTAINMENT, AND CONTROL MEASURES	42
10.1	PLANNING AND PREVENTION	42
10.2	ROLES AND RESPONSIBILITIES.....	42
10.2.1	Spill Coordinator	42
10.2.2	Environmental Inspector	43
10.2.3	Authorized Personnel	43
10.2.4	Construction Superintendent	43
10.2.5	Construction Personnel	43
10.3	TRAINING	43
10.4	EQUIPMENT	43
10.5	SUPERVISION AND INSPECTION	44
10.6	STORAGE AND HANDLING OF FUELS/HAZARDOUS LIQUIDS	44
10.6.1	Fuel Storage - General	44
10.6.2	Refueling	45
10.6.3	Refueling, Maintenance, and Fuel Storage Near Wetlands and Waterbodies	45
10.6.4	Overnight parking	45
10.6.5	Concrete Washout Handling.....	45
10.7	INITIAL SPILL MANAGEMENT.....	46
10.7.1	Immediate Response.....	46
10.7.2	Mobilization.....	46
10.8	SPILL NOTIFICATION RESPONSIBILITIES	47
10.8.1	Notification Volumes	47
10.8.2	Spill Report Form.....	47
10.8.3	Agency Notification	47
10.9	SPILL CONTAINMENT AND CLEANUP	47
10.9.1	Spill Control - Upland Areas	47

10.10 SPILL CONTROL - WETLANDS AND WATERBODIES..... 48
 10.11 STORAGE AND DISPOSAL OF CONTAMINATED MATERIALS 48
11.0 DRILLING FLUID RESPONSE, CONTAINMENT, AND NOTIFICATION PROCEDURES50
 11.1 ON-SITE OBSERVATION DURING CONSTRUCTION..... 50
 11.2 CONTAINMENT, RESPONSE, AND CLEAN-UP EQUIPMENT 51
 11.3 RESPONSE 51
 11.3.1 Upland Locations..... 51
 11.3.2 Wetland and Waterbody Locations..... 52
 11.4 NOTIFICATION AND RESUMPTION OF SUSPENDED HDD OPERATIONS... 52
 11.5 CLEAN-UP 53
 11.6 RESTORATION AND POST-CONSTRUCTION MONITORING..... 53

FIGURES

Figure 1 Typical Topsoil Segregation – Full Right-of-Way
 Figure 2 Typical Topsoil Segregation – Trench Line Only
 Figure 3 Typical Topsoil Segregation – Modified Ditch Plus Spoil Side
 Figure 4 Typical Temporary or Permanent Berms – Perspective View
 Figure 5 Typical Temporary or Permanent Berms – Elevation View
 Figure 6 Typical Silt Fence Installation
 Figure 7 Typical Straw Bale Installation
 Figure 8 Typical Erosion Control Blanket Installation
 Figure 9 Typical Staple Pattern for Erosion Control Fabric
 Figure 10 Typical Biolog Installation
 Figure 11 Typical Cat Tracking
 Figure 12 Typical Trench Breakers – Perspective View
 Figure 13 Typical Trench Breakers – Plan & Profile Views
 Figure 14 Permanent Slope Breakers – Perspective View
 Figure 15 Typical Waterbody Crossing – Open-Cut Wet Trench Method
 Figure 16 Typical Waterbody Crossing – Dam and Pump Method
 Figure 17 Typical Waterbody Crossing – Flume Method
 Figure 18 Typical Waterbody Crossing – Directional Drill Method
 Figure 19A Typical Span Type Bridge With and Without Instream Support (Flume Support)
 Figure 19B Typical Span Type Bridge With and Without Instream Support (Timber Matted Support)
 Figure 20 Typical Rock Flume Bridge
 Figure 21 Typical Dewatering Measures
 Figure 22A Typical Straw Bale Dewatering Structure
 Figure 22B Typical Straw Bale Dewatering Structure
 Figure 22C Typical Straw Bale Dewatering Structure
 Figure 23 Typical Final Stream Bank Stabilization – Rip Rap & Erosion Control
 Figure 24 Typical Wetland Crossing Method
 Figure 25 Typical Improved Road Crossing Directional Bore Method
 Figure 26 Typical Stream Bank Stabilization Biolog
 Figure 27 Typical Root Wad
 Figure 28 Typical Natural Material Revetment

APPENDICES

Appendix A	Noxious and Invasive Weed Species
Appendix B	Equipment Cleaning Log
Appendix C	Seed Mixes
Appendix D	Enbridge Environment Hydrostatic Test Discharge Authorization & Documentation
Appendix E	Emergency Response Contractors/Disposal and Treatment Facilities
Appendix F	Spill Report Form
Appendix G	Spill Reporting-Agency Contacts

ACRONYMS AND ABBREVIATIONS

ATWS	additional temporary workspace
BMP	best management practices
CLL	Construction Line List
Contactora	construction Contractor
CRP	Conservation Reserve Program
DOT	Department of Transportation
ECD	erosion and sediment control device
EI	environmental inspector
Enbridge	Enbridge Energy, Limited Partnership
EPP	Environmental Protection Plan
HDD	horizontal directional drilling
NFPA	National Fire Protection Association
NRCS	Natural Resources Conservation Service
OHWL	ordinary high water level
OHWM	ordinary high water mark
PLS	Pure Live Seed
ROW	right-of-way
TWS	temporary workspace
UFC	Unified Facilities Criteria

This page intentionally left blank

INTRODUCTION

This Environmental Protection Plan (“EPP”) outlines construction-related environmental policies, procedures, and protection measures Enbridge Energy, Limited Partnership (“Enbridge”) developed as a baseline for construction. This EPP was developed based on Enbridge’s experience implementing Best Management Practices (“BMPs”) during construction as well as the Federal Energy Regulatory Commission’s Upland Erosion Control, Revegetation, and Maintenance Plan (May 2013 Version) and Wetland and Waterbody Construction and Mitigation Procedures (May 2013 Version). It is intended to meet or exceed federal, state, tribal, and local environmental protection and erosion control requirements, specifications and practices. The EPP is designed to address typical circumstances that may be encountered along the Project. Project-specific permit conditions and/or landowner agreements may supersede the general practices described in this document.

This document includes the following sections:

- Section 1.0 describes general mitigation measures, including soil erosion and sedimentation control procedures, to be implemented during upland construction and upland restoration;
- Section 2.0 describes stream and river construction, crossing, and restoration;
- Section 3.0 describes practices for wetland construction, crossings, and restoration;
- Section 4.0 describes highway, road, and rail crossings;
- Section 5.0 describes construction dewatering;
- Section 6.0 outlines water appropriation practices;
- Section 7.0 addresses revegetation measures;
- Section 8.0 addresses winter construction issues;
- Section 9.0 addresses waste management issues;
- Section 10.0 addresses construction equipment-related spill prevention, containment and controls; and
- Section 11.0 addresses containment, response, and notification procedures for inadvertent releases of drilling fluid.

Alternative construction procedures implemented in lieu of this EPP will provide an equal or greater level of protection to the environment, and will be approved in writing by Enbridge.

Unless otherwise specified, the construction Contractor (“Contractor”) is responsible for implementing the requirements of this EPP.

Enbridge will provide appropriate construction oversight to confirm and document compliance with the measures of this EPP and requirements of applicable federal, state, tribal, and local permits. Enbridge’s Environmental Inspectors (“EIs”) will assist the Contractor in interpreting and implementing the requirements of the EPP, and verify compliance with these procedures for Enbridge. Enbridge will employ experienced EIs to manage unforeseen situations that are not directly addressed by project documents. Enbridge relies on the experience and judgment of the

EIs, through coordination and consultations with project management staff, to address unforeseen situations should they occur in the field. The EIs will be expected to use judgment in the field to interpret environmental conditions and requirements, but will not be authorized to make major modifications or changes without the prior written approval of Enbridge. The EI, in consultation with Enbridge Environment staff, will have the authority to stop activities and order corrective mitigation for actions that are not in compliance with the measures in this EPP, landowner agreements, or environmental permit requirements. The EI will maintain appropriate records to document compliance with these and other applicable environmental permit conditions.

Enbridge has also committed to applicable agencies to fund a comprehensive third-party monitoring program to be deployed during Project construction. Enbridge has constructed numerous projects with the oversight of third-party monitors and accepts the recommendation by state agencies regarding their use. Enbridge will work with the agencies to define the role and qualifications of proposed third-party monitors to ensure they are experienced in the type of construction they will be observing and knowledgeable regarding the resources that may be impacted.

1.0 GENERAL MITIGATION MEASURES

1.1 IDENTIFICATION OF AVOIDANCE AREAS

The EI will post signs for environmental features such as wetlands, waterbodies, drainages/drain tiles, buffer zones, rare plant or ecological community sites, invasive species and noxious weed locations, regulated wildlife habitat, cultural resources, and erosion-prone or steep slopes.

1.2 CONSTRUCTION LINE LIST AND PERMITS

Enbridge will provide the Contractor with a Construction Line List (“CLL”) that describes special requirements (e.g., timber salvage, topsoil segregation, restoration measures, fencing requirements) as agreed upon with landowners provided the special requirements conform to project permits. The Contractor will comply with these special requirements and/or permit conditions.

The CLL identifies requirements and comments provided by landowners; however, it is not a comprehensive list of construction requirements. The CLL will be considered in conjunction with other project documents and permits.

1.3 WET WEATHER SHUTDOWN

During construction, certain activities may be suspended in wet soil conditions, based on consideration of the following factors:

- extent of surface ponding;
- extent and depth of rutting and mixing of soil horizons;
- areal extent and location of potential rutting and compaction (i.e., can traffic be rerouted around wet area); and
- type of equipment and nature of the construction operations proposed for that day.

The Contractor will cease work in the applicable area until Enbridge determines that site conditions are such that work may continue. The EIs, in collaboration with Enbridge construction management, will ultimately decide if wet weather shutdown is necessary in a given location.

1.4 RIGHT-OF-WAY ACCESS

Access to the right-of-way (“ROW”) will be from public roadways and Enbridge-approved private access roads only. Existing roads are generally in a condition that can accommodate construction traffic without modification or improvement. Some roads will require improvements such as widening and/or grading and the placement of timber mats or gravel.

Enbridge is responsible for posting signs or other methods to identify approved access roads in the field and to ensure that access is confined to only the approved roads. Vehicle tracking of soil from the construction site will be minimized by installation and implementation of BMPs such as stone pads, timber mats, reducing equipment/vehicle access to the construction ROW

where practicable (off-ROW parking), or equivalent. Installation of stone or timber mat access pads will be in accordance with applicable permits and state/federal specifications. If such BMPs are not adequately preventing sediment from being tracked onto public roads, street sweeping, or other equivalent means of collecting sediment, will be used. If soil is tracked onto a roadway, the contractor will remove accumulated material from the road and return it to the construction ROW within an upland area as soon as possible, but in no circumstances more than 24 hours after discovery. In addition, soil on roadways cannot be broomed, washed, and/or graded into the road ditch or onto the shoulder.

After construction, Enbridge will return improved roads to their pre-construction condition unless the landowner or land-managing agency requests that the improvements be left in place. Enbridge will maintain permanent access roads to aboveground facilities (e.g. pump stations, mainline valves) throughout project operation.

1.5 RIGHT-OF-WAY REQUIREMENTS

All construction equipment and vehicles will be confined to the approved construction ROW and additional temporary workspace ("ATWS"). Prior to commencement of clearing operations, the outer limits of the construction ROW and ATWS areas will be marked with distinctive stakes and flagging by Enbridge. Construction activities are restricted to the approved designated areas.

The construction ROW (i.e., construction workspace) for the Project will vary and may include a portion of Enbridge's existing corridor, new permanent corridor, permitted temporary workspace ("TWS"), and site-specific extra workspaces as defined below and shown in Figures 1 through 3. The construction ROW width will be reduced in selected locations (e.g., wetlands, waterbodies, and forested shelterbelts), in accordance with applicable permit conditions, as indicated on the Project construction alignment sheets and in the field by the use of staking.

(a) ROW (Permanent)

Enbridge's existing permanent ROW varies in width. Additional footage may be added, depending on the location of the new pipeline(s) in relation to the existing pipelines. The permanent ROW is maintained to facilitate access and aerial inspection of the pipeline system.

(b) TWS

In addition to the ROW/permanent corridor, construction will require TWS. The TWS will be located adjacent to and contiguous with the proposed ROW/permanent corridor and will be identified on the construction alignment sheets and by distinctive staking of construction limits prior to clearing.

(c) ATWS

Site-specific ATWS locations, (construction work areas beyond the permanent corridor and TWS previously described), will be required at select locations such as steep slopes, road, waterbody, railroad, some wetland crossings, and where it is necessary to cross under the existing pipelines or foreign utilities. ATWS will typically be located in uplands adjacent to the construction ROW and set at least 50-feet back from sensitive resource boundaries where site-specific field conditions allow. However, to complete

work safely, Enbridge may need to locate ATWS within a wetland or within the 50-foot setback from a wetland or waterbody based on site-specific conditions. ATWS adjacent to waterbodies and/or wetlands is addressed further in Sections 2.0 and 3.0, respectively.

1.6 CONTROLLING SPREAD OF UNDESIRABLE SPECIES

It is Enbridge's intent to minimize the potential introduction and/or spread of undesirable species (i.e., invasive species, noxious weeds, or crop diseases) along the construction ROW due to pipeline construction activities. However, it is not practicable for Enbridge to eradicate undesirable species that are adjacent to the construction ROW. Enbridge will minimize the potential for the establishment of undesirable species by minimizing the time duration between final grading and permanent seeding.

In consultation with the applicable agencies, Enbridge will identify plant species that are considered noxious weeds and/or invasive plants that may occur within the counties being crossed by the pipeline corridor (refer to Appendix A).

1.6.1 Prevention and Control Measures

To prevent the introduction of identified noxious weeds and invasive species into the Project areas from other construction sites, construction equipment and mats will be cleaned prior to arriving on site. This cleaning consists of removing visible dirt from the equipment and mats and blowing loose material from equipment using compressed air. Equipment designated for use within waterbodies will be washed and dried prior to use. Purge and clean all pumps before proceeding from one location to the next if designated noxious weeds or invasive plants or infested waters (e.g. zebra mussels, Eurasian milfoil) are known to be present in the area. Known locations of noxious or invasive plant infestations and infested waters will be identified in the appropriate permits. If the EI identifies aquatic invasive species in an area not previously identified as an infested water, the EI will contact the Minnesota Department of Natural Resources. The Contractor(s) will keep logs documenting the cleaning history of each piece of equipment and make the logs available to the EI upon request. Contractors may use the equipment cleaning log provided in Appendix B or an equivalent form approved by Enbridge. Equipment found to be in non-compliance with the cleaning requirement will not be allowed on the Project sites until it has been adequately cleaned.

Prior to clearing and grading of the construction ROW and pending landowner permission, major infestation areas identified during surveys or by Enbridge's EIs may be treated with the herbicides. All proposed herbicides will be reviewed and approved by Enbridge's Environment Department through consultation with Minnesota Department of Agriculture and U.S. Environmental Protection Agency and as recommended through consultation with local authorities prior to use. Selective foliage or basal application will be used when practicable. Alternatively, full construction ROW topsoil segregation may be implemented for weed control to allow equipment to work through the area after topsoil has been stripped, as long as equipment stays on the subsoil (clearing, grading, and restoration equipment will still be cleaned). The Contractor(s) will obtain necessary permits and/or certifications for the use of the applicable herbicides, is responsible to limit off-ROW overspray, and will comply with state laws regarding the use of those herbicides. Contractor(s) will keep proper documentation of the locations where the herbicides have been used and provide such documentation to Enbridge within 3 days of

completing the work. Weed control spraying will be restricted near certified organic farms and prohibited on certified organic farms.

Treatment of known infestation areas will be completed in accordance with applicable chemical contact times (as specified by the manufacturer) in advance of clearing and grading within the construction ROW. Treatment may be restricted in areas that are not readily accessible, such as areas where access is limited by topography or other site conditions such as saturated/inundated soils. In the event that an area is determined to be inaccessible, the EI will be notified and a site-specific alternative treatment method will be developed.

If additional noxious weed infestations are identified subsequent to herbicide applications, mechanical means (scrape down/blow down) may be used to remove weeds from tracked equipment and mats prior to leaving the infested area. High pressure water wash stations may be established in select areas if the above measures do not adequately remove soil and vegetation debris from construction equipment. Enbridge will determine where this practice will be implemented. The Contractor(s) will keep logs documenting the cleaning history of each piece of equipment and make the logs available to the EI or other Enbridge Representative upon request. Any equipment found to be in noncompliance with the cleaning requirement will be removed from the Project sites until it has been adequately cleaned.

To prevent the spread of noxious weeds and invasive species during construction, mulch used on the Project will be composed of weed-free material. Certified weed-free mulch may also be required at site-specific locations. The Contractor(s) will be responsible for identifying and acquiring sources of weed-free and certified weed-free mulch. Sources will be approved by Enbridge prior to purchase. As discussed further in Section 1.8.3, tree stumps outside the ditch line will be ground below normal ground surface or completely removed and hauled off to an approved disposal facility. Stumps within the ditch line will be completely removed, ground, and/or hauled off to an approved disposal facility. Enbridge will consult with the appropriate agency to determine the appropriate treatment for felled infested and diseased trees.

In the case that a healthy oak tree adjacent to the construction ROW is damaged or wounded during construction activities in counties where the oak wilt fungus is present, Enbridge will treat the cut surface with water-based paint, a pruning/wound sealer, or shellac to prevent further spread of the disease. Treated trees will be inspected by the EI.

1.6.2 Pesticide Use and Application

Enbridge does not typically authorize use of pesticides on the construction or permanent ROW or at Enbridge facilities. However, should pesticide use be required to control the spread of undesirable pests and/or at the request of an agency, Enbridge will only utilize those pesticides and methods of application approved by the Minnesota Department of Agriculture, Minnesota Department of Natural Resources, and the U.S. Environmental Protection Agency in the state of Minnesota. Selective foliage or basal application will be used when practicable. All pesticides will be applied in a safe and cautious manner so as not to damage adjacent properties including crops, orchards, tree farms, apiaries, or gardens. Enbridge will contact the landowner or designee to obtain approval for the use of pesticide at least 14 days prior to any application on their property. The landowner may request that there be no application of pesticides on any part of the site within the landowner's property. Enbridge will provide notice of pesticide application to affected landowners and known beekeepers operating apiaries within three miles of the site at least 14 days prior to such application.

1.7 POTHOLING/HYDROVAC SLURRY

Hydrovac excavation is used to positively identify pipelines and other buried utilities. The Contractor will construct an unlined but bermed containment area or identify comparable containment (e.g., open top tank) to hold the hydrovac slurry in an Enbridge and landowner-approved upland area within the construction workspace or dispose of the material off-site at a licensed disposal facility. Once the slurry is drained and dry, it may be incorporated with the subsoil in an Enbridge and landowner-approved upland area within the construction workspace. Discharging hydrovac slurry on to topsoil is not permitted as the material will degrade the quality of the topsoil and potentially affect revegetation.

1.8 UPLAND CLEARING

The initial stage of construction involves the clearing of brush, trees, and tall herbaceous vegetation from the ROW. Clearing may be accomplished with chain saws, mowers, and hydraulic tree-cutting equipment.

1.8.1 Disposal of Non-Merchantable Timber

Unless otherwise directed by Enbridge, non-merchantable timber and slash will be disposed of by mowing, chipping, grinding, and/or hauling off site to an approved disposal facility or used in stabilizing erodible slopes or construction entrances. In non-agricultural, non-wetland areas, chips, mulch, or mechanically cut woody debris may be uniformly broadcast across the ROW where the material would ultimately be incorporated into the topsoil layer during grading activities, with landowner approval (coordinated through Enbridge ROW agents). Burning of non-merchantable wood may be allowed only where the Contractor has acquired all applicable permits and approvals (e.g. agency, tribal, and landowner) and in accordance with all tribal, state, and local regulations. The Contractor will provide Enbridge with copies of these permits and/or approvals prior to initiating burning.

1.8.2 Disposal of Merchantable Timber

All merchantable timber will be managed in accordance with Enbridge contract specifications.

1.8.3 Upland Grading and Stump Removal

To facilitate proper cleanup and restoration in upland areas, tree stumps outside the ditch line will be ground below normal ground surface or completely removed and hauled off to an approved disposal facility. Stumps in the ditch line will be completely removed, ground, and/or hauled off to an approved disposal facility.

1.9 TEMPORARY EROSION AND SEDIMENT CONTROLS

Temporary erosion and sediment control devices (“ECDs”) include, but are not limited to, slope breakers, sediment barriers (silt fence, straw bales, bio-logs, etc.), stormwater diversions, trench breakers, mulch, and revegetation subsequent to seeding of exposed soils (refer to Figures 4 through 11). The Contractor will maintain erosion and sediment control structures as required in the Project construction documents and as required by all applicable permits. Non-functional erosion and sediment controls will be repaired, replaced, or supplemented with functional materials within 24 hours after discovery, or as otherwise specified in project permits. ECDs will

be installed after initial clearing but before grading activities and will be replaced by permanent erosion controls as restoration is completed.

Temporary ECDs will be installed after clearing and prior to grubbing and grading activities at the base of sloped approaches to streams, wetlands, and roads. Temporary ECDs will also be installed at the edge of the construction ROW as needed, and/or in other areas determined by the EI to slow water leaving the site and prevent siltation of waterbodies and wetlands down slope or outside of the construction ROW (e.g., swales and side slopes). Temporary ECDs will be placed across the entire construction ROW at the base of slopes greater than 5 percent where the base of the slope is less than 50 feet from tile line inlets, drainage ways, wetlands, and/or waterbodies until the area is revegetated and there is no potential scouring or sediment transport to surface waters. Adequate room will be available between the base of the slope and the sediment barrier to accommodate ponding of water and sediment deposition.

If silt fence is used, when the depth of sediment reaches about one-third of the height, the sediment will be removed. Non-functional ECDs will be repaired, replaced, or supplemented with functional structures within 24 hours after discovery, or as otherwise specified in project permits.

Temporary ECDs installed across the travel lane may be removed during active daytime construction; however, ECDs will be properly reinstalled after equipment passage, or activities in the area are completed for the day. These ECDs will also be repaired and/or replaced prior to inclement weather when forecasted.

1.9.1 Temporary Stabilization

Installation of temporary seeding, mulch (straw or hydromulch), and erosion control mats may be required by Enbridge in certain locations (including topsoil piles) if there are construction delays within a spread of at least 14 days. The Contractor may be required by Enbridge to install temporary stabilization materials sooner based on site conditions, or as required in project permits.

1.9.2 Erosion Control Blanket

The appropriate class of erosion control blanket will be installed in accordance with manufacture recommendations and/or state Department of Transportation (“DOT”) specifications on slopes greater than 5 percent that would be exposed over the winter and drain to surface waters (refer to Figures 8 and 9). The Contractor will attempt to install erosion control blankets on the exposed slopes prior to snowfall; however, construction progress and/or seasonal weather variations may prevent installation prior to the first snowfall. Installation of erosion control blankets and additional BMPs, as applicable based on site conditions, is required after the first snowfall to protect slopes prior to spring melt and runoff. Erosion control blankets will be installed running parallel (up and down) with the direction of the slope (not perpendicular).

1.9.3 Mulch

Mulch (weed-free straw, wood fiber hydromulch, or a functional equivalent) will be applied to disturbed areas (except for actively cultivated land and wetlands) if requested by the landowner or land managing agency, if specified by the applicable permits or licenses, or as required by Enbridge. Mulch will specifically be required on:

- slopes greater than 5 percent; and
- dry, sandy areas that can blow or wash away (field decision).

Mulch will be free of noxious weeds as listed in applicable state laws. Certified weed-free mulch may also be required at site-specific locations. The Contractor will be responsible for identifying and acquiring sources of weed-free and certified weed-free mulch. Sources will be approved by Enbridge prior to purchase.

Mulch will be applied at a rate of 2 tons per acre to cover at least 75 percent of the ground surface unless otherwise stipulated by permit conditions. Mulch will be uniformly distributed by a mechanical mulch blower, or by hand in areas not accessible to the mulch blower. Mulch will be anchored/crimped using a mulch-anchoring tool or disc set in the straight position to minimize loss by wind and water, as site conditions allow. In areas not accessible to a mulch-anchoring tool or too steep for safe operation, the mulch may be anchored by liquid tackifiers, with advance written approval from Enbridge. The manufacturer's recommended method and rate of application will be followed.

Hydro-mulch and liquid tackifier can be used in place of straw or weed-free hay mulch with prior approval from Enbridge. All hydromulch and liquid tackifier products used will be on the applicable state DOT product list. Application rates will be at the manufacturer's recommended rate, equal to or greater than 2 tons per acre of straw mulch.

1.9.4 Cat Tracking

Cat tracking, also known as horizontal slope grading, may be implemented based on site conditions (sandy or silt soils) to reduce erosion potential. Cat tracking is achieved by driving a bulldozer vertically up and down the slope which results in the tracks being oriented horizontally; creating small speed bumps for water (refer to Figure 11).

1.9.5 Temporary Slope Breakers

Temporary slope breakers will be installed to minimize concentrated or sheet flow runoff in disturbed areas in accordance with the following maximum allowable spacing unless otherwise specified in permit conditions.

<u>Slope (%)</u>	<u>Approximate Spacing (ft)</u>
3-5	250
5-15	200
15-25	150
>25	<100

If the length of the slope is less than the distance of the required spacing, slope breakers are not required unless a sensitive resource area (e.g., wetland or public roadway) is located immediately down slope, or as requested by the EI. Temporary slope breakers may be constructed using earthen subsoil material, silt fence, straw bales, or in non-agricultural land, rocked trenches may be used. On highly erodible slopes, slope breakers in the form of earthen berms will be used whenever possible.

Temporary slope breakers will be constructed according to the following specifications (refer to Figures 4 and 5):

- straw bales used as slope breakers will be trenched in and staked so as to not allow spacing between bales or allow flow underneath the bales;
- the outfall of temporary slope breakers will be directed off the construction ROW into a stable well-vegetated upland area or into an appropriate energy-dissipating sediment control device (e.g., silt fence, straw bales, rock aprons) to prevent the discharge of sediments (refer to Figure 4);
- proper slope breaker outfalls will be established where topsoil segregation and/or grading has created a barrier at the edge of the construction workspace; and
- gaps will be created through spoil piles where necessary to allow proper out letting of temporary berms.

1.10 UPLAND TOPSOIL SEGREGATION

Upland areas where topsoil will be stripped includes cropland, hay fields, pasture, residential areas, and other areas as requested by the landowner or as specified in the project plans, commitments, and/or permits. Topsoil will not be used to construct berms, trench breakers, temporary slope breakers, improving or maintaining roads, or to pad the pipe. Berms used for stacking pipe in pipe yards may be constructed using topsoil if landowner permission and necessary approvals are obtained. Gaps will be left and ECDs installed where stockpiled topsoil and spoil piles intersect with water conveyances (i.e., ditches, swales, and waterways) to maintain natural drainage.

Topsoil Segregation Methods

The following topsoil segregation methods may be employed during construction:

- Full Construction ROW (refer to Figure 1)
- Trench-Line-Only (refer to Figure 2)
- Modified Ditch-Plus-Spoil Side (refer to Figure 3)

The Full Construction ROW topsoil segregation technique will typically be used in active cropland, which will consist of stripping topsoil from the spoil storage area, ditch line, and the primary travel lane. The Trench-Line-Only topsoil segregation method may be used where Enbridge determines that the width of the construction ROW is insufficient for other methods to be used. Enbridge may also use the Trench-Line-Only topsoil segregation method in areas where there is a thick sod layer such as in hay fields, pastures, golf courses, and residential areas, unless otherwise requested by the landowner. Alternative topsoil segregation methods, such as Modified Ditch-Plus-Spoil Side, may be used on a site-specific basis or as requested by the landowner. Topsoil is not typically segregated in standing water wetlands unless specifically requested by the landowner and/or managing land agency in accordance with applicable permit conditions.

Depth of Upland Topsoil Stripping

In deep soils (more than 12 inches of topsoil), topsoil will be stripped to a minimum depth of 12 inches, unless otherwise specified/requested by other plans, permit conditions, or the landowner. Additional space may be needed for spoil storage if more than 12 inches of topsoil are segregated. If less than 12 inches of topsoil are present, the Contractor will attempt to segregate to the depth that is present.

1.11 UPLAND TRENCHING

Trenching in uplands is typically accomplished with a backhoe excavator or a rotary wheel ditching machine. Excavated material will be side cast (stockpiled) within the approved construction ROW separate from topsoil, and stored such that the area subject to erosion is minimized. Enbridge will coordinate with landowners to minimize disruption of access caused by the trench during construction. Where deemed appropriate by Enbridge, the Contractor will leave plugs of subsoil in the ditch or will construct temporary access bridges across the trench for the landowner to move livestock or equipment. Trenches may also be sloped where started and ended to allow ramps for wildlife to escape. Spacing of plugs and ramps will be determined in the field.

1.11.1 Timing

The length of time a trench is left open will be minimized to ensure that installation of the pipe and restoration of the construction ROW occurs in a timely fashion. Therefore, unless otherwise specified by project permits or Enbridge, the Contractor will limit the amount of excavated open trench to a maximum of 3 days of anticipated welding production per spread. This timeframe may be decreased at the discretion of Enbridge based on site conditions. Site-specific activities such as horizontal directional drilling (“HDD”), guided bores, road bores, tie-in points, and valve work may be performed independent of a spread.

1.12 FOAM PILLOW INSTALLATION

Use of foam pillows for pipe protection in the trench will be approved by Enbridge in advance and installed in accordance with applicable project permits, local/state/federal regulations, and manufacturer’s recommendations.

1.13 TRENCH BREAKERS

Trench breakers will be installed as deemed necessary by Enbridge in sloped areas after the pipe has been lowered into the trench. Trench breakers protect against subsurface water flow along the pipe after the trench is backfilled. Trench breakers will be constructed with bags filled with rock-free subsoil or sand. Topsoil will not be used to construct trench breakers.

Use of foam trench breakers will be approved by Enbridge in advance and installed in accordance with applicable project permits, local/state/federal regulations, and manufacturer’s recommendations. Trench breakers will be placed from the bottom of the trench to near the top of the trench, completely surrounding the pipe and will be properly keyed into the undisturbed trench walls (refer to Figures 12 and 13). The location for trench breakers will be based on field conditions including the degree and length of slope, presence of down slope sensitive resource areas such as wetland and waterbodies, and proximity to other features such as roads and/or

railroads. The following conditions apply to the placement and installation of trench breakers unless otherwise directed by Enbridge:

- Trench breakers will be installed on slopes greater than 5 percent adjacent to streams, wetlands, or other waterbodies.
- Where the pipeline exits a wetland towards areas of lower relief, trench breakers will be installed (within the upland) where there is a potential for underground drainage along the pipe in order to prevent wetland or waterbody drainage.
- At all waterbody crossings, as necessary, to prevent diversion of water into upland portions of the pipeline trench and to keep accumulated trench water out of the waterbody.

The actual location of each trench breaker will be selected through coordination between Enbridge's EIs, Enbridge's Craft Inspectors, and the Contractor's Foreman for backfilling activities.

1.14 DRAIN TILE INLET PROTECTION AND TILE REPAIRS

Enbridge will attempt to locate existing drain tile inlets that are located near the construction work area prior to construction. Drain tile inlets will be marked using flags. The Contractor will protect located drain tile inlets with the potential to receive stormwater from construction of the Project using the appropriate ECDs until sources with the potential to discharge have been stabilized. The determination of the specific ECD will be made based on the location of an inlet with respect to the project area, drainage area from the construction work area to the inlet, topography, vegetation, soils, and accessibility to the inlet. Where drain tile inlets are located off of Enbridge's construction ROW, Enbridge may not have authorization to install ECDs at the inlet site. In these cases, sediment control measures (typically silt fence) will be installed along the edge of the construction work area that drains to the inlet structure to minimize sedimentation.

If underground drainage tile is damaged by pipeline construction, it will be repaired in a manner that assures proper tile line operation at the point of repair in accordance with the Agricultural Protection Plan.

1.15 UPLAND BACKFILLING

Backfilling follows pipe installation and consists of replacing the material excavated from the trench. In areas where topsoil has been segregated, the subsoil will be replaced first, and the topsoil will be spread uniformly over the area from which it was removed. Prior to backfilling, the trench will be dewatered in accordance with the methods discussed in Section 5.0 if water obscures the trench bottom.

1.16 CLEANUP AND ROUGH/FINAL GRADING

All waste materials, including litter generated by construction crews, will be disposed of daily by the Contractor. Initial cleanup and rough grading activities may take place simultaneously. Cleanup involves removing construction debris (including litter generated by construction crews and excess rock) and large woody debris. Rough and final grading includes restoring disturbed

areas as near as practicable to preconstruction conditions, returning the topsoil where topsoil has been stripped, preparing a seedbed and de-compacting subsoil (where applicable) for permanent seeding, installing or repairing temporary erosion control measures, repairing/replacing fences, and installing permanent erosion controls.

1.16.1 Timing

The Contractor will begin cleanup and rough grading (including installation of temporary erosion and sediment control measures) within 72 hours after backfilling the trench. The Contractor will attempt to complete this rough cleanup within one week. The Contractor will initiate final grading, topsoil replacement, seeding, and installation of permanent erosion control structures within 14 days after backfilling the trench. If seasonal or other weather conditions prevent compliance with these timeframes, temporary erosion controls will be maintained until conditions allow completion of cleanup.

1.17 PERMANENT EROSION AND SEDIMENT CONTROLS

During final grading, slopes in areas other than cropland will be stabilized with erosion control structures. With exception for actively cultivated areas, permanent berms (diversion dikes or slope breakers) will be installed on all slopes, according to the following maximum spacing requirements unless otherwise specified in permit conditions:

<u>Slope (%)</u>	<u>Approximate Spacing (ft)</u>
3-5	250
5-15	200
15-25	150
>25	<100

Permanent berms will be constructed according to the following specifications:

- Permanent berms will be constructed of compacted earth, stone, or functional equivalent as approved in advance by Enbridge.
- The outfall of berms will be directed toward appropriate energy-dissipating devices, and off the construction ROW if possible.
- Permanent berms will be inspected and repaired as deemed necessary by Enbridge to maintain function and prevent erosion.
- Erosion control blankets (curlex, jute, or equivalent) will be placed on slopes over 30 percent or that are a continuous slope to a sensitive resource area (e.g., wetland or waterway).

1.18 SOIL COMPACTION TREATMENT

Cultivated fields and compacted or rutted areas will be tilled prior to topsoil replacement with a deep tillage device or chisel plowed to loosen compacted subsoils. If subsequent construction and cleanup activities result in further compaction, additional measures will be undertaken to alleviate the soil compaction.

1.19 STONE REMOVAL

A diligent effort will be made to remove excess stones equal to or larger than 4 inches in diameter from the upper 8 inches of subsoil or as specified in permit conditions, contract documents, or landowner agreements. After the topsoil is replaced, stone removal efforts will cease when the size and density of stones on the construction ROW are similar to undisturbed areas adjacent to the construction ROW as determined by the EI. Excess rock will be piled in upland areas where landowner permission has been obtained or will be hauled off-site to an Enbridge approved disposal site.

1.20 REPAIR OF DAMAGED CONSERVATION PRACTICES

The Contractor will restore all soil conservation practices (such as terraces, grassed waterways, etc.) that are damaged by the pipeline construction to preconstruction conditions to the extent practicable.

1.21 LAND LEVELING FOLLOWING CONSTRUCTION

Following the completion of the pipeline, the construction ROW will be restored to its pre-construction conditions as practical. Should uneven settling or documented surface drainage problems occur following the completion of pipeline construction and restoration, Enbridge will take appropriate steps to remedy the issue.

2.0 STREAM AND RIVER CROSSING GENERAL REQUIREMENTS

The procedures in this section apply to streams, rivers, and other waterbodies such as jurisdictional ditches, ponds, and lakes. These procedures require that judgment be applied in the field and will be implemented under the supervision of Enbridge.

Stream crossing requirements, including construction methods, timing, erosion control, and restoration are described in this section and in the stream crossing permits issued by state and federal agencies and by tribal authorities (as applicable). If the contractor considers certain parts of these procedures to be technically impractical due to site-specific engineering constraints, they may submit an on-site modification request to Enbridge for consideration of alternative measures that would provide an equal or greater level of protection to the stream and river ecosystems. Enbridge will review the contractor's alternatives and consult with appropriate regulatory agencies and tribal resource specialists (as applicable). The contractor will receive written approval from Enbridge prior to implementing the alternatives. During wet and high runoff conditions, the EI will determine whether conditions warrant additional considerations for construction activities.

2.1 TIME WINDOW FOR CONSTRUCTION

All in-stream work activities (installation of dams, sheet piling, etc.) will be minimized to the extent practicable on an area and time duration basis. In-stream trenching will be conducted during periods permitted by the appropriate regulatory agencies and applicable permits. Unless otherwise specified in applicable permits and with exception to blasting and other rock breaking measures and directional drill, in-stream construction activities (specifically trenching, pipeline installation, backfill, and restoration of the streambed contours) for wet crossing methods will occur within the following timeframes:

- Minor Waterbodies (all waterbodies less than or equal to 10 feet wide at the water's edge at the time of crossing): 24 hours
- Intermediate Waterbodies (all waterbodies greater than 10 feet wide but less than 100 feet wide at the water's edge at the time of crossing): 48 hours
- Major Waterbodies (all waterbodies greater than 100 feet wide at the time of crossing): As specified by Enbridge or in the applicable permits.

These timeframes apply regardless of the presence or absence of flow. These timeframes also apply to dry crossing methods as a guideline and can be extended based on site-specific conditions with approval from Enbridge Environment staff, Construction Management, and the EI.

Stream crossings will be designed as close to perpendicular to the axis of the stream channel as engineering and routing constraints allow, creating the shortest crossing length.

2.2 CLEARING AND GRADING

The construction ROW width will consist of a 25-foot-wide neck down beginning 20 feet from the ordinary high water mark ("OHWM") / ordinary high water level ("OHWL") on the working side of the ROW (refer to Figures 15 through 17).

2.2.1 Beaver Dam Removal and Prevention of Dam Rebuilding

With landowner approval and in accordance with necessary permits obtained, the Contractor may trap beavers, alter or remove beaver dams in order to attempt to lower the water level prior to construction. For alterations, the Contractor will insert a 12-inch minimum diameter, 20-foot long minimum perforated steel culvert, or an equivalent device, through the dam to allow the water to continually drain. The perforations should be a minimum of 1.5-inch diameter, encompassing the entire circumference and extend for the full length of the culvert.

2.2.2 Impaired Waters

Where discharges of stormwater may occur to waters designated under Section 303(d) of the Clean Water Act as Impaired Waters, additional BMPs will be implemented as specified in the applicable project permits.

2.3 ADDITIONAL TEMPORARY WORKSPACE

ATWS includes work areas outside the boundary of the typical construction ROW. These spaces are typically used to assemble pipe segments and for temporary spoil storage. Clearing of forested and brushy areas for ATWS will be avoided as much as possible. Woody vegetation in wetlands and riparian areas will typically not be cleared for the purpose of ATWS unless approved by appropriate regulatory agencies as stipulated in permits issued for the Project. ATWS will be constructed as follows:

- ATWS will be located at least 50 feet away from the OHWM/OHWL if topographic or other physical conditions such as stream channel meanders allow, except where the adjacent upland consists of cultivated or rotated cropland or other disturbed land (refer to Figures 15 through 17).
- If safe work practices or site conditions do not allow for a 50-foot setback, ATWS should be located no closer than 20 feet from the OHWM/OHWL, subject to site-specific approval by Enbridge.
- ATWS will be limited to the minimum size needed to construct the stream crossing.

2.4 BRIDGES

Temporary equipment bridges will be used on most waterways (upon approval by the appropriate agency), including small waterways such as ditches and intermittent streams, where there is a potential for stormwater runoff or rain events to transport sediment downstream from equipment crossing the waterway. Bridges will be constructed as described below and will be removed as soon as possible during final restoration. Bridges will not typically be installed at directionally drilled waterbodies, unless there is no reasonable alternative that provides an efficient, economical way to transport heavy construction equipment around the waterbody by truck.

With exception to clearing-related equipment, fording of waterways is prohibited (i.e. civil survey, potholing, or other equipment are not permitted to ford waterways prior to bridge placement). Clearing equipment and equipment necessary for installation of equipment bridges

will be allowed a single pass across waterbodies prior to bridge installation, unless restricted by applicable permits.

2.4.1 Types of Bridges

Equipment bridges will be constructed using one of the following techniques:

- Typical Span Type Bridge (timber mats - refer to Figure 19)
- Rock Flume (refer to Figure 20)
- Railroad flat cars
- Flexi-float or other pre-fabricated portable bridges
- Other methods as approved by Enbridge and appropriate agencies

2.4.2 Bridge Design and Maintenance

Bridges will be designed as close to perpendicular to the axis of the stream channel, creating the shortest crossing length and will be built and maintained in accordance with applicable permits. Equipment bridges will be designed to withstand the maximum foreseeable flow of the stream with headers and support structures being placed above the OHWM of the feature. In the event that local jurisdictions require stricter guidelines associated with bridge placement, Enbridge will design the bridge to comply with these requirements. Bridges will not restrict flow or pool water while the bridge is in place, and will be constructed with clean materials. Bridges will be designed and maintained to prevent soil from entering the waterbody. Soil that accumulates on the bridge decking will be removed as needed, or as deemed necessary by the EI.

2.5 STREAM AND RIVER CROSSING CONSTRUCTION METHODS

The following stream and river crossing methods are typically used, subject to further restrictions by Enbridge and applicable permits and subject to modifications as approved by appropriate regulatory agencies and tribal resource specialists (as applicable) during construction.

2.5.1 Wet Trench Method

Installation

The wet trench method will be used to cross streams and rivers not permitted to be flumed, dam and pumped, or directionally drilled (refer to Figure 15). The following procedures will be used during wet trench crossings:

- Sediment control measures will be installed before grading from the 20-foot vegetative buffer left on each stream bank. Spoil containment structures will be installed back from the stream bank so that spoil does not migrate into the stream.

- Grading will be directed away from the waterbody to minimize the potential for sediment to enter the stream. Grading of stream banks will be restricted to the trench line and areas necessary for safe bridge installation.
- After grading, backhoes or draglines will be used to excavate the trench. Where possible, excavating equipment will operate from one or both banks, without entering the stream. If equipment must encroach into the stream, it will operate on clean construction mats. Streambed material will be segregated (e.g., upper one foot and the remaining trench spoil will be stored separately) and placed within a spoil containment structure in approved construction work area limits. Storage of streambed spoil within the stream will only be allowed if expressly approved in the applicable permits.
- Earthen trench plugs (hard plugs) between the stream and the upland trench will be left undisturbed during excavation of the in-stream trench to prevent diversion of the stream flow into the open trench and to prevent water that may have accumulated in the adjacent upland trench from entering the waterbody. Trench plugs will be removed immediately prior to pipe placement, and then replaced when the pipe is in place. Trench water accumulated upslope of trench plugs will be dewatered appropriately prior to trench plug removal.
- Water within the trench will be managed in accordance with Section 5.0
- Backfilling will begin after the pipe is positioned in the trench at the desired depth. Backfill material will consist of the spoil material excavated from the trench and parent streambed unless otherwise specified in state or federal permits. The in-stream trench will be backfilled so that the stream bottom is as near as practicable to its pre-construction condition, with no impediments to normal water flow.

Temporary Stabilization

The Contractor will restore the stream banks as near as practicable to pre-construction conditions unless that slope is determined to be unstable. If Enbridge determines the slope is considered unstable, the Contractor will reshape the banks to prevent slumping. Once the banks have been reshaped, ECDs will be installed within 24 hours of backfilling the crossing. Temporary slope breakers will be installed on all sloped approaches to streams in accordance with the spacing requirements previously specified.

A temporary seed mix (e.g., annual rye or annual oats) and mulch and/or erosion control blankets will be installed within a 50-foot buffer on either side of the stream, with exception to actively cultivated land. Silt fence or functional equivalent as approved in advance by Enbridge will be installed upslope of the temporary seeding area.

2.5.2 Dam and Pump Method

Installation

The dam and pump method is a dry crossing technique that is suitable for low flow streams and is generally preferred for crossing meandering channels. The dam and pump method involves damming of the stream upstream and downstream of the proposed trench before excavation

(refer to Figure 16) and pumping water around the construction area. The following procedures will be used for dam and pump crossings:

- Dams may be constructed of sandbags, inflatable dams, aqua-dams, sheet piling, and/or steel plates. The dams will prevent the stream from flowing into the construction area. The dams will be continuously monitored for a proper seal. Additional sandbags, plastic sheeting, steel plating, or similar materials will be used where necessary to minimize the amount of water seeping around the dams and into the construction work area. The dam will not be removed until after the pipeline has been installed, the trench has been backfilled, and the banks have been stabilized.
- Pumping of the stream across the ROW will commence simultaneously with dam construction to prevent interruption of downstream flow. Stream flow will be pumped across the construction area through a hose and will be discharged to an energy-dissipation device, such as plywood boards, to prevent scouring of the streambed.
- The pumps and fuel containers will be located on the upstream side of the crossing and will be placed in impermeable, sided structures which will act as containment units (refer to Section 10.0). The pumps used for this crossing method will not be placed directly in the stream or on the streambed. Pumps will have a capacity greater than the anticipated stream flow. The pumping operation will be staffed 24 hours a day and pumping will be monitored and adjusted as necessary to maintain an even flow of water across the work area and near-normal water levels upstream and downstream from the crossing.

The pump intake will be suspended to prevent sediment from being sucked from the bottom of stream and will be equipped with a screen, or equivalent device, to prevent fish uptake.

- Where possible, excavating equipment will operate from one or both banks, without entering the stream. If equipment must encroach into the stream, it will operate on clean construction mats (free of soil and plant material prior to being transported onto the construction ROW). Streambed material will be segregated as stated in the wet trench method and will be placed within a spoil containment structure in approved construction work area limits. Storage of streambed spoil within the stream will only be allowed if expressly approved in the applicable permits.
- Earthen trench plugs (hard plugs) between the stream and the upland trench will be left undisturbed during excavation of the in-stream trench to prevent diversion of the stream flow into the open trench and to prevent water that may have accumulated in the adjacent upland trench from entering the waterbody. Trench plugs will be removed immediately prior to pipe placement, and then replaced when the pipe is in place. Trench water accumulated upslope of trench plugs will be dewatered appropriately prior to trench plug removal.
- Standing water that is isolated in the construction area by the dams will be managed in accordance with Section 5.0
- Backfilling will begin after the pipe is positioned in the trench to the desired depth. Backfill material will consist of the spoil material and parent streambed excavated from the trench unless otherwise specified in state or federal permits. The in-stream trench

will be backfilled so that the stream bottom is similar to its pre-construction condition, with no impediments to normal water flow.

Temporary Stabilization

Restoration of the stream banks and the installation of temporary erosion controls will be similar to that described for the wet trench method above but will occur immediately following installation of the pipeline. Once the stream banks have been stabilized, the dams and pump will be removed.

2.5.3 Flume Method

Installation

The flume method is a dry crossing technique that is suitable for crossing relatively narrow streams that have straight channels and are relatively free of large rocks and bedrock at the point of crossing (refer to Figure 17). This method involves placement of flume pipe(s) in the stream bed to convey stream flow across the construction area without introducing sediment to the water. The procedures for using the flume method are described below.

- The flume(s) will be of sufficient diameter to transport the maximum flows anticipated to be generated from the watershed. The flume(s), typically 40 to 60 feet in length, will be installed before trenching and will be aligned so as not to impound water upstream of the flume(s) or cause downstream bank erosion. The flumes will not be removed until after the pipeline has been installed, trench has been backfilled, and the stream banks have been stabilized.
- The upstream and downstream ends of the flume(s) will be incorporated into dams made of sand bags and plastic sheeting (or equivalent). The upstream dam will be constructed first and will funnel stream flow into the flume(s). The downstream dam will prevent backwash of water into the trench and construction work area. The dams will be continuously monitored for a proper seal. Adjustments to the dams will be made where necessary to prevent large volumes of water from seeping around the dams and into the trench and construction work area.
- Where possible, excavating equipment will operate from one or both banks, without entering the stream. If equipment must encroach into the stream, it will operate on clean construction mats. Streambed material will be segregated and placed within a spoil containment structure in approved construction work area limits. Storage of streambed spoil within the stream will only be allowed if expressly approved in the applicable permits.
- Earthen trench plugs (hard plugs) between the stream and the upland trench will be left undisturbed during excavation of the in-stream trench to prevent diversion of the stream flow into the open trench and to prevent water that may have accumulated in the adjacent upland trench from entering the waterbody. Trench plugs will be removed immediately prior to pipe placement, and then replaced when the pipe is in place. Trench water accumulated upslope of trench plugs will be dewatered appropriately prior to trench plug removal.

- If additional trench dewatering is necessary to complete the installation of the pipe, the discharge will be managed in accordance with Section 5.0.
- Backfilling will begin after the pipe is positioned in the trench to the desired depth. Backfill material will consist of the spoil material excavated from the trench and parent streambed unless otherwise specified in state or federal permits. The in-stream trench will be backfilled so that the stream bottom is similar to its pre-construction condition, with no impediments to normal water flow.

Temporary Stabilization

Restoration of the ROW and the installation of temporary erosion controls will be similar to that described for the wet trench method above but will occur immediately following installation of the pipeline. After the stream banks have been stabilized, the dams and flume will be removed from the stream bed allowing water to resume its flow in the channel.

2.5.4 Directional Drill and/or Guided Bore Method

Installation

Installing the pipe underneath a stream will involve placing a drill unit on one side of the stream (refer to Figure 18). A small-diameter pilot hole will be drilled under the stream along a prescribed profile. After the pilot hole has been completed, barrel reams will be used to enlarge the pilot hole to accommodate the desired pipeline diameter. Drilling mud will be necessary to remove cuttings and maintain the integrity of the hole. Water from an Enbridge-approved source will be used to prepare the slurry of drilling mud, and will be appropriated according to applicable permits. The pipe section will be pulled through the hole by the drilling rig and welded to the adjoining sections of pipe on each side of the river.

Drilling Mud

During drilling operations, drilling mud and slurry will be stored back from the waterbody in an earthen berm sediment control structure, in tanks, or by other methods so that it does not flow into the waterbody, adjacent wetlands or off the workspace (refer to Section 11.0 for additional details).

After the pipe is in place, excess drilling mud will be hauled off-site to an Enbridge-approved disposal location or licensed disposal facility.

Temporary Stabilization

The directional drilling/guided bore method normally does not result in the disturbance of the stream banks or riparian vegetation (with exception of extremely limited hand clearing of woody vegetation required to facilitate guide wire placement), which reduces the potential for erosion and sedimentation at the stream crossing. Consequently, temporary erosion control measures that are installed at open-cut crossings typically are not necessary for drilled/bored crossings.

2.6 PERMANENT RESTORATION

Stream/channel banks disturbed during installation of the pipelines will be stabilized with erosion control materials such as an erosion control blanket and seeded in accordance with Section 7.0. Permanent stabilization will be initiated within 24 hours after installation of the crossing using the wet trench method and prior to restoring flow using the dam and pump or flume method, unless site and permit conditions delay permanent installation. Where the banks have been disturbed, the Contractor will restore the slopes as near as practicable to pre-construction conditions unless that slope is determined by Enbridge to be unstable. Where the slope of the banks is determined to be unstable or has the potential to erode or fail, the banks will be reshaped to transition the disturbed areas into the natural stream bank with the intent to stabilize the bank and create a blended, natural appearance.

Berms or other sediment filter devices will be installed at the base of sloped approaches to streams greater than five percent and the outlet of the berm will be directed away from the stream into a well vegetated area. Temporary sediment control devices will remain in place until the area has stabilized and adequate revegetation has established.

2.6.1 Vegetative Bank Restoration

Typically, waterbody banks will be restored as near as practicable to preconstruction conditions after backfilling is complete and will be seeded with an appropriate seed mix as specified in Section 7.0 and covered with an erosion control blanket. Erosion controls, (e.g. straw bales, bio-logs, silt fences, etc.) will be installed as necessary based on site-specific conditions.

2.6.2 Supplemental Bank Stabilization

Unstable soils and/or site-specific factors such as stream velocity and flow direction may require additional restoration efforts, such as installation of rock rip-rap, to stabilize disturbed stream banks. Rock rip-rap will be used only where site-specific conditions require and where applicable permits or approvals have been acquired. Geotextile fabric and rock riprap will be placed according to site and permit conditions (refer to Figure 23). Disturbed soils upslope and on either side of the riprap will be prepared for seeding according to Section 7.0 and other stream bank protection requirements. Bioengineering techniques may also be implemented as determined by Enbridge (refer to Figures 26 through 28).

2.6.3 Bridge Removal

Equipment bridges will be removed during final cleanup or, if access is needed, after final cleanup and permanent seeding. Restoration of the bridge area will be completed upon bridge removal.

2.6.4 Swales

Swales will be restored as near as practicable to original conditions. Swales will be seeded and either mulched with straw or erosion control blankets will be installed to the perceivable top of bank for the width of the construction ROW.

3.0 WETLAND CROSSING GENERAL REQUIREMENTS

The procedures in this section apply to all wetlands that will be affected by the Project. These procedures require that judgment be applied in the field and will be implemented under the supervision of Enbridge and the EI. The intent of these procedures is to minimize construction-related disturbance and sedimentation of wetlands and to restore wetlands as nearly as possible to pre-existing conditions. Additionally, in wetlands that are being farmed at the time of construction, Enbridge will construct the pipeline using standard upland methods. Most seasonally saturated farmed wetlands are used for crop production and topsoil will be segregated in the same manner as topsoil in upland agricultural lands. Pipe stringing and fabrication may occur within the farmed wetland adjacent to the trench, or adjacent to the farmed wetland in a designated ATWS.

Wetland crossing requirements, including construction methods, timing, erosion control, and restoration, are described in this section and in the wetland crossing permits issued by state, federal and/or tribal agencies as applicable. If the contractor considers certain parts of these procedures to be technically impractical due to site-specific engineering constraints, they may submit an on-site modification request to Enbridge for approval of alternative measures. Enbridge will review the contractor's alternatives and consult with appropriate regulatory agencies. The contractor must receive approval from Enbridge prior to implementing the alternatives.

3.1 WETLAND ACCESS

The Contractor will use the construction ROW and only approved roads to access wetland areas.

3.2 CLEARING

Clearing the construction ROW in wetlands will be similar to clearing in uplands. For construction to proceed, obstructions (e.g., trees, brush, and logs) need to be removed. Typically, low ground pressure equipment will be used, limiting disturbance to the wetland. Vegetation and trees within wetlands will be cut off at ground level, leaving existing root systems intact; clearing debris will generally be removed from the wetland for disposal. Hydro-axe debris, or similar can be left in the wetland if spread evenly in the construction ROW to a depth which will allow for normal revegetation, as determined by the EI.

3.3 ADDITIONAL TEMPORARY WORKSPACE IN WETLANDS

In general, Enbridge attempts to locate ATWS outside of wetlands wherever practicable; however, ATWS may be sited in select wetlands where the wetland is adjacent to a waterbody, road, railroads, foreign utility crossings, and/or pipeline cross-over with prior approval from the applicable regulatory agencies. Clearing of forested wetlands for ATWS will be avoided as much as possible.

- Staging areas, additional spoil storage areas, and other ATWS will be located in upland areas at least 50 feet away from wetland boundaries (refer to Figures 24), where safe work practices or site conditions permit, except where the adjacent upland consists of cultivated or rotated cropland or other disturbed land. If site conditions do not permit a 50-foot setback, then these areas will be located as far away from the wetland as is

practicable. Vegetation will not be cleared between these areas and the wetland in any event. No construction activities including vegetation clearing or earthwork will occur between the ATWS and the wetland.

- The size of the ATWS areas will be limited to the minimum needed to construct the wetland crossing.

3.4 GRADING IN A WETLAND

Grading activities will be confined to the area of the trench and will be minimized to the extent practicable. Grading outside the trench will only be allowed where required to ensure safety and restore the construction ROW after backfilling the trench with prior approval from Enbridge.

ECDs will be installed:

1. across the entire construction ROW upslope of the wetland boundary, where necessary, to prevent sediment flow into the wetland;
2. along the edge of the construction ROW as necessary to prevent sediment flow into off-ROW wetlands; and
3. along the edge of the construction ROW as necessary to contain spoil and sediment within the construction ROW through wetlands.

ECDs will be maintained in proper working order to prevent the flow of sediment into wetlands from spoil piles or sloped approaches that are adjacent to the wetlands. .

3.5 RIGHT-OF-WAY STABILIZATION

Tree stumps, brush riprap, imported soil, and rock fill will not be brought in to stabilize the ROW in wetlands. Where low ground pressure equipment is not used, construction equipment will operate from timber construction mats or equivalent means with prior approval from Enbridge (refer to Figure 24). To prevent the spread of noxious and invasive plant species, timber mats will be free of soil and plant material prior to being transported onto the construction ROW and/or moved from one area of the construction ROW to another area. Timber riprap (also known as corduroy road) will not be used without prior written approval from Enbridge and the appropriate regulatory agencies. Pre-existing corduroy roads in wetlands may be used but may not be improved, maintained, restored, or replaced without site-specific authorization from applicable agencies.

Subsoil from the pipeline trench within the immediate wetland may be placed on top of equipment mats for additional stabilization. Timber mats may be placed over the ditch line or on the working side to facilitate trench excavation. All timber mats, construction debris, and larger woody vegetative debris will be removed during cleanup of wetlands.

3.6 TRENCHING

Excavation of the pipeline trench in wetlands typically will be accomplished using backhoe excavators. The Contractor will take reasonable steps to ensure that the duration of open trench in wetlands, including tie-ins, is minimized to the fullest extent possible.

3.6.1 Topsoil Segregation

When constructing in wetland areas without standing water, up to one foot of topsoil (organic layer) will be stripped from the trench line and stockpiled separate from trench spoil to preserve the native seed stock. In standing water wetlands, organic soil segregation is not typically practical; however, the Contractor will attempt to segregate as much of the organic layer as possible based on site/saturation conditions. If normally unsaturated wetlands are saturated at the time of construction, topsoil segregation will be attempted according to Figure 2 and based on recommendations from the EI and appropriate regulatory agencies.

3.6.2 Trench Breakers

Where the EI determines that the pipeline trench has the potential to drain or partially drain a wetland, trench breakers will be installed as necessary to maintain the original wetland hydrology.

3.7 PIPELINE INSTALLATION

The following procedures are intended to minimize siltation and disturbance to wetlands during installation.

3.7.1 Push/Pull Method

Large wetlands with standing water can generally not be crossed with typical crossing methods. In these areas, the pipeline will be assembled in an upland area and positioned in the trench using the "push-pull" and/or "float" techniques.

Usually this fabrication requires use of ATWS adjacent to the construction ROW. A backhoe (or equivalent) supported on timber mats or equivalent low ground pressure equipment will be used to dig the trench. The prefabricated section of pipeline will then be pushed-pulled into position or floated across the wetland. When the pipeline is in position, floats, if used, will be removed and the pipeline will sink into position. The trench will then be backfilled and a backhoe or similar equipment working from construction mats or by low ground pressure equipment will be used restore the wetland.

3.7.2 Temporary Erosion and Sediment Controls

ECDs at approaches to wetlands will be installed as previously described and in accordance with Section 1.0.

3.7.3 Concrete Coating

Concrete will generally be mixed off-site, and concrete coated pipe will be transported to the construction ROW on trucks. If required, pre-fabricated concrete weights and/or saddlebag weights will also be used to provide negative buoyancy. Concrete weights will be manufactured off-site and transported to the ROW. Weights will be strung along the construction ROW, where necessary, until they are placed over the pipe within the excavated ditch. Limited mixing and coating activities may occur on the construction ROW for coating pipe joints and concrete weight repairs according to the concrete usage specifications in Section 10.0. Washing equipment used for mixing, pouring, casting, or coating will not be within 100 feet of any wetland

and will be conducted and contained in a leak-proof containment facility or impermeable liner. The EI will determine where ECDs will be installed down slope of equipment wash areas to capture sediments and minimize erosion from runoff.

3.8 BACKFILLING

Subsequent to pipe installation, backfilling of wetland trenches will take place immediately, or as approved by EI. The Contractor will restore wetlands as near as practicable to pre-construction conditions and will make a reasonable attempt to return the subsoil to its pre-construction density. During backfilling of wetland areas, subsoil material removed from the trench during construction will be replaced so that the material is not mounded above the adjacent ground surface (undisturbed trench wall). Subsoil that exceeds the elevation of the ground adjacent to the trench will be removed from the wetland and disposed of in an upland area or an Enbridge-approved disposal site. After the trench has been backfilled with subsoil, previously segregated topsoil will be spread over the trench area and mounded.

3.9 ROUGH GRADING, CLEANUP, AND TEMPORARY RESTORATION

Cleanup and rough grading activities may take place simultaneously. Cleanup typically involves removing construction debris and replacing fences removed during construction. Rough grading includes restoring original conditions within the disturbed areas (i.e., ditch line, spoil storage areas, and equipment travel lane) and installing or repairing temporary ECDs. Temporary slope breakers will be installed near the boundary between the wetland and adjacent sloped approaches, to prevent sediment flow into the wetland.

3.9.1 Timing

Cleanup and rough grading (including installation of temporary erosion control measures) will begin as soon as practical after the trench is backfilled, weather permitting.

3.9.2 Temporary Stabilization

Where necessary, disturbed wetland areas will be seeded with oats (40 lbs/acre) and/or a temporary seed mix, unless standing water is prevalent or unless permanent planting or seeding with native wetland vegetation is required by applicable permits. No fertilizer, lime, or mulch will be applied in wetlands.

4.0 HIGHWAY, ROAD AND RAIL CROSSINGS

4.1 ADDITIONAL WORKSPACE

Additional workspaces for bored road and railroad crossings and open-cut road crossings will be determined on a site-specific basis. These workspaces will be adjacent to the road or railroad and limited to the size needed to contain spoil, stage equipment, and store supplies for the crossing.

4.2 MAINTENANCE

Roadway crossings will be maintained in a condition that will prevent tracking of mud onto the roadway.

Rock tracking pads, constructed of stone as required by the applicable permits, will be installed adjacent to paved public roads to prevent or minimize the tracking of soil onto the roadway. If the roadside ditch is part of a jurisdictional waterway, a permit will be obtained prior to installing the tracking pad or culvert. If permitted in wetlands, tracking pads will be limited in size to reduce impacts. Tracking pads installed in wetlands will be constructed with clean rock placed on geotextile fabric, as approved by an EI and with approval from applicable regulatory agencies. All rock and fabric will be removed from the wetland during cleanup.

4.3 TEMPORARY EROSION AND SEDIMENT CONTROLS

Temporary ECDs (e.g., silt fence and/or double-staked straw bales) will be installed on sloped approaches to road crossings where vegetation has been disturbed (refer to Figure 25).

5.0 CONSTRUCTION DEWATERING

5.1 TRENCH DEWATERING

Prior to initiating dewatering activities, the EI will approve the water discharge plan to ensure that the BMPs are applied in such a way as to minimize the potential for scour and water containing sediment from reaching a wetland or waterbody. Furthermore, landowner approval is required in advance of placement of dewatering structures outside of the approved construction ROW. The Contractor will assess each water discharge situation to include:

1. **Water Discharge Setting** - This includes:
 1. Soil Type - The soil type the discharged water would flow over. The management of discharged water traveling over sandy soil is more likely to soak into the ground as compared to clay soils.
 2. Ground Surface - The topography in the area that would influence the surface flow of the discharged water.
 3. Adjustable Discharge rate - The flow rate of the discharged water (which may need to vary) can be managed based on the site conditions to minimize instances of water from reaching a sensitive resource area such as a wetland or waterbody. (Example - Water discharged at 500 gallons per minute may soak into the ground while if discharged at a higher flow rate would cause water to flow via overland runoff into a sensitive resource area)
 4. Discharge Outfall - The amount of hose and number/size of pumps needed to attempt to discharge water at a location which drains away from waterbodies or wetlands.
2. **Pump Intake** - Use floating suction hose or other similar measures to prevent sediment from being sucked from bottom of trench.
3. **Overwhelming Existing Drainage** - If the discharge (assumed to be clean) enters a stream, the flow added to the stream will not exceed 50 percent of the peak storm event flow (to prevent adding high water volumes to a small stream channel that causes erosion due to imposing high flow conditions on the stream).
4. **Filtering Mechanism** – All dewatering discharges will be directed through a filtering device as indicated below.
 1. Well-Vegetated Upland Area – Water can be directed to a well-vegetated upland area through a geotextile filter bag. Geotextile bags need to be sized appropriately for the discharge flow and suspended sediment particle size.
 2. Straw Bale Dewatering Structure – Where the dewatering discharge point cannot be located in an upland area due to site conditions and/or distance, the discharge should be directed into a straw bale dewatering structure. The size of the straw bale dewatering structure is dependent on the maximum water discharge rate (refer to

Figure 21). A straw bale dewatering structure should be used in conjunction with a geotextile filter bag to provide additional filtration near sensitive resource areas.

3. Alternative dewatering methods - Alternative methods may be approved by Enbridge on a site-specific basis.

5.1.1 Flow Measurement and Water Sampling

The volume of water discharged from the trench will be recorded as required by the applicable permits. The volume may be determined using a flow meter, or equivalent method, as approved by Enbridge or specified by applicable permit conditions.

Samples of the water discharged will be sampled if required by tribal permits and/or state-issued discharge permits.

5.1.2 Regulatory Notification and Reporting

Enbridge will notify and submit reports to appropriate tribal, state and federal agencies as required by all permits/authorizations.

5.2 HYDROSTATIC TEST DISCHARGES

Hydrostatic testing involves filling the new pipeline segments with water acquired in accordance with applicable permits (refer to Section 6.0), raising the internal pressure level, and holding that pressure for a specific period of time per federal DOT specifications. Hydrostatic testing will be done to verify that there are no flaws in the pipe or welds. Pre-built sections may be hydrostatically tested prior to installation using HDD and/or guided bore techniques. Hydrostatic testing will be conducted in accordance with applicable appropriation and discharge permits obtained by Enbridge. Hydrostatic test waters will not be transferred from one waterbody to another. Chlorinated source water will be used and treated as specified in applicable permits. After the hydrostatic test is complete, the line will be depressurized and the water discharged.

5.2.1 Refueling

The operation and refueling of hydrostatic test equipment will be in accordance with the conditions outlined in Section 10.0.

5.2.2 Siting of Test Manifolds

Hydrostatic test manifolds will be installed where necessary to ensure proper test pressures and incorporates changes due to topography. Where feasible, Enbridge will incorporate minor adjustments to the test manifold locations to avoid placement in wetlands and riparian areas. However, completely avoiding the placement of a test manifold in a wetland may not always be possible. The Contractor will install appropriate erosion control measures where the EI determines they are necessary.

5.2.3 Water Sampling

Water discharged from hydrostatic tests will be sampled as required by state-issued appropriation or discharge permits. Water volumes and flow rates will be recorded using the form provided in Appendix D.

5.2.4 Best Management Practices

Prior to hydrostatic testing the pipeline, Enbridge will prepare the pipe by removing accumulated construction debris, mill scale, dirt, and dust using a cleaning pig. The debris will be collected in a temporary receiver and will be properly disposed off-site of by the Contractor. Upon completion of the cleaning operation, the pipeline will be sealed with the test headers.

Test headers and pigs will be arranged to allow for rinse water to be installed ahead of the fill pigs. Rinse water will be treated and disposed of in accordance with applicable permit conditions.

Following testing, the test section will be depressurized and the water will be discharged to a well-vegetated, upland area with an appropriate dewatering structure such as a geotextile filter bag and/or a hay bale structure that will be lined with geotextile fabric. Direct discharges to surface waters, if allowed by permit, will be directed into an energy dissipation device such as a splash pup.

At no time will the discharge rate exceed the applicable discharge rates specified in state-issued or other discharge permits. In the event no maximum discharge rate is identified, discharges will be monitored and adjusted as necessary to avoid scouring, erosion, or sediment transport from the discharge location.

To minimize the potential for introduction and/or spread of invasive species due to hydrostatic testing activities, Enbridge will discharge water to the same source location from which it was appropriated. If water is used to test multiple test sections, it will be relayed back to the source water through the pipeline for final discharge. Test water will not be discharged to a waterbody other than the appropriation source, unless coordinated and permitted through the applicable agencies.

5.2.5 Flow Measurement

The total volume of water discharged will be determined with a flow meter (or equivalent), or as required by the applicable state permit. The total volume of water discharged will not exceed the volume specified in the applicable permit.

6.0 WATER APPROPRIATION

6.1 GENERAL

Water may be drawn from local sources, such as lakes, streams, and private or municipal wells for construction activities such as dust control, HDD/guided boring, trench dewatering, and hydrostatic testing. The Project will follow applicable permit conditions for the appropriation of water.

The intake hose will be suspended off of the stream or lake bottom and equipped with a screen, or equivalent device, to prevent fish uptake. During withdrawal, adequate waterbody flow rates and volumes will be maintained to protect aquatic life and allow for downstream uses. The volume and rate of withdrawal will be monitoring to comply with applicable permit conditions.

6.2 WATER SOURCES

Water will only be withdrawn from sources approved by Enbridge and in accordance with applicable permits. No additives to the water are permitted unless written approval is received from Enbridge and applicable permits authorize such additives.

If appropriation is scheduled to occur during possible periods of low flow, including frozen conditions, a backup source will be identified.

6.3 FLOW MEASUREMENT

At no time will the withdrawal rate for the water source exceed the rate specified in the applicable permits.

The Contractor will measure the withdrawal rate and total volumes of water appropriated with a flow meter (or equivalent) and provide the data to Enbridge, as required by the applicable permits.

6.4 WATER SAMPLING

Where required by permit conditions, Enbridge will sample the water during appropriation. The Contractor will assist Enbridge in obtaining these samples.

6.5 REGULATORY NOTIFICATION AND REPORTING

Enbridge will notify appropriate agencies of the time of appropriations if required by the state appropriations permits. Enbridge will submit reports regarding the volume and quality of the water withdrawn if required by the applicable permits.

7.0 REVEGETATION & MONITORING

This section was developed in conjunction with Natural Resources Conservation Service (“NRCS”) guidelines. Project-specific permit conditions and landowner requests (with exception to wetlands) for specific seed mixes (as indicated in the Project CLL) take precedence over this section.

7.1 PROJECT SEED SPECIFICATIONS

Seed used will be purchased on a “Pure Live Seed” (“PLS”) basis for seeding (both temporary and permanent) revegetation areas. Seed tags will identify:

- purity;
- germination;
- date tested;
- total weight and PLS weight;
- weed seed content; and
- seed supplier’s name and business information.

Seed will be used within 12 months of testing as required by applicable state rules and regulations. The seed tags on the seed sacks will also certify that the seed is “Noxious Weed Free”. Seed rates used on the Project will be based on PLS rate, not actual weight basis. Therefore, to determine the correct application rate if not indicated on the seed tag, a correction calculation will be performed based the purity and germination. For example, a seed mix that has a specified 10 pounds PLS per acre, 95 percent germination rate, and is 80 percent pure needs to be applied at the following rate:

$$(95\% \text{ germination} \times 80\% \text{ purity})/100 = 76\% \text{ PLS}$$
$$10 \text{ pounds PLS per acre}/.76\% \text{ PLS} = 13.2 \text{ pounds per acre actual seeding rate}$$

The species components of individual mixes are subject to availability at the time of purchase. Grass species may be substituted with alternative native or non-invasive species that are included in the NRCS guidelines and subject to approval by Enbridge.

Seed tags will be collected by the contractor and provided to Enbridge during seeding activities. The tags will be reviewed by the EI prior to installation to ensure that the seed mix complies with Enbridge’s specifications and that it is being applied to the correct location. If bulk delivery of seed is made, the above information will still be made available to Enbridge. Off-loading/on-loading of seed will not be performed in a designated wetland area.

Legume seed (if used) will be treated with an inoculant specific to the species and in accordance with the manufacturer’s recommended rate of inoculant appropriate for the seeding method (broadcast, drill, or hydroseeding). When hydroseeding, four times the manufacturer’s recommended rate of inoculant will be used.

7.2 TEMPORARY REVEGETATION

Enbridge’s temporary seed mix (refer to Appendix C) was developed based on recommendations from the NRCS. Unless specifically requested by landowners or land

managing agencies, Enbridge does not intend to establish temporary vegetation in actively cultivated land, standing water wetlands, and/or other standing water areas.

7.3 TIMING FOR TEMPORARY VEGETATION

Temporary revegetation will be established in construction work areas where 14 days or more will elapse between:

- the completion of final grading at a site and the establishment of permanent vegetation; and/or,
- where there is a high risk of erosion due to site-specific soil conditions and topography.

Enbridge may require the Contractor(s) to conduct temporary seeding sooner than 14 days at site-specific locations near sensitive resource areas and/or areas prone to wind/water erosion.

Temporary vegetation should be established at any time between **April 1 and September 1**. Attempts at temporary revegetation after this date should be assessed on a site-specific basis and with approval from Enbridge.

7.4 MULCH

Mulch (weed-free straw, wood fiber hydromulch, or a functional equivalent) will be applied to disturbed areas (except for actively cultivated land and wetlands) if requested by the landowner or land managing agency, if specified by the applicable permits or licenses, or as required by Enbridge. Mulch will specifically be required on:

- slopes greater than 5 percent; and
- dry, sandy areas that can blow or wash away (field decision).

Mulch will be free of noxious weeds as listed in applicable state laws. Certified weed-free mulch may also be required at site-specific locations. The Contractor will be responsible for identifying and acquiring sources of weed-free and certified weed-free mulch. Sources will be approved by Enbridge prior to purchase.

Mulch will be applied at a rate of 2 tons per acre to cover at least 75 percent of the ground surface unless otherwise stipulated by permit conditions. Mulch will be uniformly distributed by a mechanical mulch blower, or by hand in areas not accessible to the mulch blower. Mulch will be anchored/crimped using a mulch-anchoring tool or disc set in the straight position to minimize loss by wind and water, as site conditions allow. In areas not accessible to a mulch-anchoring tool or too steep for safe operation, the mulch may be anchored by liquid tackifiers, with advance written approval from Enbridge. The manufacturer's recommended method and rate of application will be followed.

Hydro-mulch and liquid tackifier can be used in place of straw or weed-free hay mulch with prior approval from Enbridge. All hydromulch and liquid tackifier products used will be on the applicable state DOT product list. Application rates will be at the manufacturer's recommended rate, equal to or greater than 2 tons per acre of straw mulch.

7.5 PERMANENT REVEGETATION

Permanent vegetation will be established in areas disturbed within the construction work area (permanent easement, TWS, and ATWS) except in actively cultivated areas and standing water wetlands. The seed mixes for permanent seeding include native seed varieties commonly found and/or available from local seed distributors. Enbridge's seed mixes (refer to Appendix C) were selected to augment revegetation via natural recruitment from native seed stock in the topsoil and are not intended to change the natural species composition. Rates provided are assumed for a drill application and will be adjusted as discussed in Section 7.1.

7.6 UPLAND CONSTRUCTION AREAS

In consulting with the NRCS and other agencies, Enbridge developed standard upland seed mixes for restoring disturbed areas affected by the Project (Appendix C, Tables 1-23). These mixes include species that will provide for effective erosion control and revegetation of the project area. These seed mixes will be used by Enbridge as the standard upland mixes unless an alternate seed mix is specified by a landowner or land managing agency.

7.7 PERMANENT SEEDING OF WETLAND AREAS

7.7.1 Unsaturated Wetland Areas

Non-standing water wetlands in Minnesota will be seeded with the mix provided in Appendix C, Table 17 (MN Seed Mix 3) to provide temporary cover and allowed to revegetate naturally. No unsaturated wetlands will be seeded in North Dakota. The natural revegetation process will be encouraged by the seeds and rhizomes in the topsoil spread back over the ROW after pipe installation. No fertilizer, lime, or mulch will be applied in wetlands.

7.7.2 Saturated/Standing Water Wetlands

Enbridge does not propose to seed saturated or standing water wetland areas. It is widely accepted that the reestablishment of vegetation within standing water wetlands occurs best through natural process without supplemental seeding.

7.7.3 Forested Wetland Restoration

Enbridge proposes to allow natural reforestation of the TWS area within forested wetlands via stump sprouting, root sprouting, and natural recruitment. Specific forested wetland restoration provisions will be followed as indicated in applicable permits issued for the Project.

7.8 PERMANENT SEEDING OF WATERBODY BANKS

Enbridge will reestablish stream bank vegetation in North Dakota using ND Seed Mix 2 (Table 2, Appendix C), and in Minnesota using MN Seed Mix 2 (Table 16 Appendix C) unless an alternate seed mix is requested by applicable agencies. Additional vegetation requirements may also be contained within project-specific permits. Where a waterbody is located within a wetland, the Contractor will re-seed the banks with the applicable wetland seed mix.

7.9 SPECIALIZED SEED MIXES

Enbridge developed specialized seed mixes for restoring these areas:

1. Native prairie in North Dakota and Minnesota;
2. Openings in forested areas in Minnesota;
3. Mixed native prairie/tamed hayland areas and road ditches in North Dakota, and Minnesota;
4. Tame pasture and Conservation Reserve Program (“CRP”) lands;
5. North Dakota State School land; and
6. Protected waterbody banks and wetland fringes in Minnesota.

Enbridge will provide other specialized seed mixes upon landowner request on a site-specific basis for:

- Residential Areas: This seed mix will be used to reestablish residential lawns or other types of “turf-type” land cover.
- Wildlife Areas: This seed mix will be used to provide a desirable food source for wildlife, specifically deer.

7.10 CONSERVATION RESERVE PROGRAM PROPERTIES

Enbridge’s Land Agents will contact landowners where the construction ROW crosses land enrolled in CRP. Enbridge will work with the respective landowners to identify the parcel-specific CRP seed mixes. CRP lands will be seeded at the direction of the landowner per the site-specific landowner CRP requirements for that parcel and no non-CRP approved seed mix will be planted on CRP lands. CRP parcels will also be seeded with Enbridge’s temporary cover seed mix. Seed for CRP seeding will meet the same criteria as other seed described in Section 7.1

7.11 SEED BED PREPARATION AND SEEDING PROCEDURES

After final grading, deep tillage will be performed in actively cultivated areas and in non-agricultural areas (as directed by Enbridge) to relieve soil compaction and promote root penetration. Deep tillage will not be conducted in non-farmed wetlands. The soil will then be tilled with a disc, field cultivator, or chisel plow (or equivalent) to prepare a seedbed, breaking up large clods and firm the soil surface.

Tillage and equipment operations related to seeding and mulching will be performed parallel to ground contours as much as practicable. Fertilizer and other soil amendments will be incorporated into the soil during seedbed preparation as specified by Enbridge in the project-specific CLL requirements and permits. No soil amendments will be applied in wetlands unless directed by the appropriate agencies.

7.12 SEEDING METHODS

Seed will be applied uniformly at specified rates across the prepared construction ROW by drilling, broadcasting, hydroseeding, or air seeding. The EI will suspend seeding activities if conditions are such that equipment will cause rutting of the surface in the designated seeding areas. Enbridge will continue to monitor ROW conditions to resume seeding activities as site conditions improve and according to the general seeding timing restrictions listed in Section 7.15.

7.12.1 Drill Seeding

Seeding equipment will be capable of uniformly distributing the seed and sowing it at the required depth. Drills will be equipped with a feeding mechanism that will provide a uniform flow of seed at the desired application rate. Double-disc furrow openers equipped with depth bands and packer wheels to firm the soil over the seed will be used where practicable.

7.12.2 Broadcast Seeding

Broadcast seeding rate will be double the drill-seeding rate. Seed will be uniformly distributed by a mechanical or hand operated seeder. Following seeding, a cultipacker, harrow, or hand rake will be used to cover the seeds and firm the seedbed as is appropriate for the area.

7.12.3 Hydroseeding

Hydroseeding rate will be double the drill seeding rate, or the same as broadcast seeding rate. Seed will be applied alone or in a seed, fertilizer, and/or hydromulch slurry. If seeding is applied alone, the amount of hydromulch material will be adjusted to the seed slurry to show where seeding has taken place, providing a means to identify uniform cover of the construction ROW. Hydroseeders will provide continuous agitation and be capable of supplying a continuous, non-fluctuating flow of slurry. Enbridge will pre-approve all hydromulch products, which must be on the applicable state DOT product list.

7.13 COMPANION CROPS

A companion crop is an annual that can be planted with the perennial species where soil erosion is a severe hazard. A companion crop may be used for all seed mixes.

Seeding rates for companion crops are lower than normal seeding rates for those crops to reduce competition with the seeded perennial species.

Seed	Planting Rate
Barley	10 lbs/acre
Oats	10 lbs/acre
Spring wheat	15 lbs/acre
Flax	7 lbs/acre

7.14 SOIL AMENDMENTS

Enbridge will consult with NRCS representatives and review county soil survey information to assess where soil amendments, specifically the application of fertilizer or lime are needed to promote successful revegetation. No fertilizer or lime will be added with native seed mixes. When using non-native species on dry, dry-mesic and mesic sites for permanent seeding a minimum of 150 pounds of 20-10-10, and 2 tons of 80-85 lime or equivalent will be applied, unless otherwise specified or restricted by the landowner, NRCS, or land-managing agency. Soil amendments may be applied to agricultural, pasture, and/or residential lands if requested by landowners and/or land managing agencies. Enbridge will apply phosphate free fertilizers to areas within 100 feet of a waterway if soil amendments are required.

7.15 SEEDING PERIODS

Recommended seeding dates in Table 7.15-1 are based on climatic records, research, and experience; and they also represent optimum periods for the germination of grass and legumes. The dates below provide adequate development of adventurous roots prior to stressful periods.

Table 7.15-1 Recommended Seeding Dates	
Species Type and Season of Planting	Recommended Dates
<u>Cool Season Species</u> Spring Late Summer Late fall dormant seeding	Prior to May 20 August 10 to September 1 Typically, November 1 and later
<u>Warm Season Species</u> Spring	May 10 to June 25
<u>Warm/Cool Season Mix</u> Spring	May 1 to June 14

Enbridge will delay seeding during frozen ground conditions until the applicable spring seeding period or will complete dormant seeding where conditions allow (i.e., no snow cover). Enbridge will install temporary erosion controls during frozen conditions.

7.16 TIMING OF FINAL SEEDING

Upon final grading of the construction ROW, and upon the restoration of wetland and waterways, seeding and restoration/stabilization will occur within 48 hours if weather and soils conditionals allow. Other methods of stabilization will be used if temporary seeding is not appropriate due to seasonal conditions (e.g., mulch, erosion control matting).

7.17 EROSION AND SEDIMENT CONTROL

Erosion control blankets, such as sewn straw mats, jute mats, coconut erosion control blankets, or biodegradable synthetic erosion control blankets, as approved by Enbridge, will be used on slopes over 30 percent, on stream banks and ditch banks and as directed by Enbridge.

7.18 DORMANT SEEDING

Dormant seeding is a method used after soil temperatures have cooled to 55 degrees Fahrenheit or cooler to prevent seed germination. Dormant seeding is only practicable if the soil is not frozen and snow is not present. Procedures for applying soil amendments, seedbed preparation, seeding, and mulching are the same as outlined for permanent revegetation in this section.

Where dormant seeding is conducted, one or more of the following temporary erosion and sediment controls will be put in place over the freshly seeded area unless the local soil conservation authority, landowner, or land managing agency specifies otherwise. The temporary measures will be in place within 48 hours of seeding, and are as follows:

- noxious weed-free straw mulch, at not more than 2 tons/acre, anchored;
- hydromulch, at 2 tons/acre, anchored; and/or
- erosion control blanket.

Additional erosion control measures will be applied as requested by the EI.

7.19 MANAGEMENT AND MONITORING

Enbridge will monitor and address all areas where stabilization techniques have been implemented in accordance with conditions identified in the applicable project permits and/or licenses.

8.0 WINTER CONSTRUCTION

Frozen conditions can preclude effective topsoil segregation. When soil is frozen to a depth greater than the depth of topsoil, the soil will come off in thick slabs that contain both topsoil and subsoil, and mixing can result. If topsoiling will proceed under these conditions, it should be done at the excavation only. A ripper (deep tillage device or scarifier) should be used to break up the frozen topsoil over the trench line only. Care should be taken to only rip to the actual depth of topsoil or to a maximum depth of 12 inches, whichever is less. Topsoil in the spoil storage area should be graded smooth to minimize mixing during backfilling. Sufficient time is needed to allow the newly graded topsoil to freeze in place prior to trenching.

Summer construction of large diameter pipelines in saturated/standing water wetlands with unconsolidated soils can be difficult and potentially result in greater wetland disturbance including wider trench widths and extensive rutting/surface disturbance. Constructing across these types of wetlands in the winter can result in fewer impacts. Heavy construction equipment use and travel along the construction ROW, which may not be possible in summer conditions due to saturated, unstable soil conditions, can be accomplished in the winter by establishing temporary winter frost/ice roads. These frost/ice roads protect underlying vegetation and upper layers of wetland surfaces from disturbance potentially created during summer construction.

The area of open excavation will be minimized during winter construction to reduce amount of frozen backfill and facilitate restoration to pre-construction contours. If winter conditions preclude final grading and cleanup, the Contractor will stabilize the area and temporary erosion control measures will remain in place until permanent erosion control measures are installed. Depending on site and weather conditions, Enbridge may require the Contractor to install dormant seeding, mulching, and/or installation of erosion control blanket on stream banks or other sensitive locations.

9.0 WASTE MANAGEMENT

The Contractor will properly handle, store, and dispose of all solid and hazardous materials and wastes that are used or generated by the Contractor as a result of the Project. The Contractor will determine if the materials and wastes associated with the Project classify as hazardous materials and/or wastes in accordance with applicable federal and/or state criteria. Upon request by Enbridge, the Contractor will provide documentation to Enbridge to substantiate findings of the regulatory status of materials and/or wastes used and/or generated as a result of the Project.

The Contractor will collect all waste materials, including oil or other waste liquids generated as a result of equipment maintenance, daily in suitable or approved containers (i.e., labeled and meeting any relevant regulatory requirements). On a routine basis, the Contractor will remove the containers of waste from the site and properly dispose of them. Throughout the duration of the Project, the Contractor will cleanup areas to the satisfaction of Enbridge. The Contractor is responsible for proper off-site disposal of all wastes generated during the Project. No wastes are to be left on Enbridge property, along the ROW, or buried in an excavation or otherwise disposed of on Enbridge property or ROW.

9.1 HAZARDOUS WASTES

If a Contractor generates a hazardous waste from materials they have brought on-site (e.g., paint clean-up solvents, waste paints), then the Contractor is responsible for proper waste collection, storage and disposal in accordance with all applicable regulations. The Contractor remains responsible for the proper handling, storage and disposal of the hazardous waste. Any release of the hazardous waste as a result of the improper handling, storage or disposal by the Contractor in this instance is the responsibility of the Contractor to rectify to the satisfaction of Enbridge and all applicable regulatory agencies.

9.2 ABRASIVE BLAST DEBRIS

The Contractor will contain and collect spent abrasive blast materials and place it into appropriate containers. The Contractor is responsible for covering the containers with appropriate means of rainwater and stormwater control to prevent said waters from entering or exiting the container. The Contractor is responsible for disposal of the spent abrasive in accordance with applicable federal, state and local regulatory requirements. The Contractor is responsible for determining if the spent abrasive is classified as a “hazardous” or “special” waste as defined by applicable federal and state regulations. If the spent abrasive is determined to be hazardous waste as a direct result of constituents of an Enbridge facility or equipment, Enbridge will coordinate proper disposal with the Contractor as previously discussed.

10.0 SPILL PREVENTION, CONTAINMENT, AND CONTROL MEASURES

This section describes planning, prevention and control measures to minimize impacts resulting from spills of fuels, petroleum products, or other regulated substances as a result of construction. These measures will be implemented by the Contractor, unless otherwise indicated by Enbridge.

10.1 PLANNING AND PREVENTION

Enbridge requires its Contractors to implement proper planning and preventative measures to minimize the likelihood of spills, and to quickly and successfully clean up a spill should one occur. This section sets forth minimum standards for handling and storing regulated substances and cleaning up spills. Potential sources of construction-related spills include machinery and equipment failure, fuel handling, transfer accidents and storage tank leaks. The Contractor will be responsible for implementing, at a minimum, the following planning and prevention measures.

10.2 ROLES AND RESPONSIBILITIES

10.2.1 Spill Coordinator

A Spill Coordinator will be designated by the Contractor, subject to approval by Enbridge. For all construction related spills, the Spill Coordinator will:

- report all spills to the Enbridge Representative immediately;
- report spills to appropriate federal, state and local agencies as soon as possible (subject to EI verification);
- mobilize on-site personnel, equipment, and materials for containment and/or cleanup commensurate with the extent of the spill;
- assist the Emergency Response Contractor (refer to a list of potential contractors provided in Appendix E) and monitor containment procedures to ensure that the actions are consistent with the requirements of this section;
- in consultation with Enbridge and appropriate agencies, determine when it is necessary to evacuate spill sites to safeguard human health;
- in consultation with Enbridge, coordinate with appropriate agencies the need to contact additional parties or agencies; and
- complete a Spill Report Form (refer to Appendix F) within 24-hours of the occurrence of a spill, regardless of the size of the spill.

10.2.2 Environmental Inspector

The EI will monitor the Contractor's compliance with the provisions of this section to ensure that appropriate agency notifications are made, spill resources are allocated, and clean-up is accomplished in accordance with applicable agency requirements

10.2.3 Authorized Personnel

Authorized Personnel are representatives of the Contractor who are designated to handle fuel, lubricants or other regulated substances. Authorized Personnel will be familiar with the requirements of this section and the consequences of non-compliance.

10.2.4 Construction Superintendent

The Contractor's Construction Superintendent or representative will notify the EI immediately of any spill of a petroleum product or hazardous liquid, regardless of volume.

10.2.5 Construction Personnel

Construction Personnel are representatives of the Contractor involved with the installation of the pipeline. Construction Personnel will notify the crew foreman or Spill Coordinator immediately of any spill of a petroleum product or hazardous liquid, regardless of volume.

10.3 TRAINING

The Contractor will train all employees handling fuels and other regulated substances to follow spill prevention procedures. The Contractor will train all employees who handle fuels and other regulated substances to prevent spills and to quickly and effectively contain and clean up spills that may occur in accordance with applicable regulations. .

10.4 EQUIPMENT

- Each construction crew will have adequate absorbent materials and containment booms on hand, to enable the rapid cleanup of any spill which may occur.
- The Contractor will maintain spill kits containing a sufficient quantity of absorbent and barrier materials to adequately contain and recover foreseeable spills. These kits may include, but are not limited to absorbent pads, straw bales, absorbent clay, sawdust, floor-drying agents, spill containment barriers, plastic sheeting, skimmer pumps, and holding tanks. This equipment will be located near fuel storage areas and other locations as necessary to be readily available to control foreseeable spills.
- Suitable plastic lining materials will be available for placement below and on top of temporarily-stored contaminated soils and materials.
- All fueling vehicles, and where necessary, service vehicles, will carry materials adequate to control foreseeable spills. Such material may include but not be limited to absorbent pads, commercial absorbent material, plastic bags with ties, and shovels.

- The Spill Coordinator will inform the Authorized Personnel, Construction Personnel, and the EIs of the locations of spill control equipment and materials, and have them readily accessible during construction activity. Spill kits should be clearly labeled for quick and easy identification in the field.
- All fuel nozzles will be equipped with functional automatic shut-offs.
- Fuel trucks transporting fuel to on-site construction equipment will travel only on approved access roads.

10.5 SUPERVISION AND INSPECTION

The Contractor will perform a pre-construction inspection and test of all equipment to ensure that it is in good repair. During construction, the Contractor will regularly inspect hoses, pipes, valves, and tanks to ensure equipment is free of leaks. Any equipment that found to be leaking or in need of repair will be immediately removed from service by Contractor and repaired, prior to resuming work.

10.6 STORAGE AND HANDLING OF FUELS/HAZARDOUS LIQUIDS

10.6.1 Fuel Storage - General

The Contractor will follow proper fuel storage practices, including, but not limited to the following:

- Fuel storage will be at Contractor yards only or as approved by Enbridge.
- Proper signage at and adjacent to fuel storage areas to include “Fuel Storage Area – No smoking within 50 feet.”
- Tools and materials to stop the flow of leaking will be kept on-site. Such equipment may include, but not be limited to, plugs of various sizes, 3M tank patches, a hammer, assorted sizes of metal screws with rubber washers, a screwdriver, and plastic tape.
- Fuels, lubricants, waste oil, and any other regulated substances will be stored in aboveground tanks only.
- Storage tanks and containers will conform to all applicable industry codes (e.g., National Fire Protection Association [NFPA], Unified Facilities Criteria [UFC]).
- A suitable secondary containment structure will be utilized at each fuel storage site. These structures will be lined with suitable plastic sheeting; provide a minimum containment volume equal to 150 percent of the volume of the largest storage vessel.
- Secondary containment areas will not have drains. Precipitation may be drawn off as necessary. If visual inspection indicates that no spillage has occurred in the secondary containment structure, accumulated water may be drawn off and discharged in accordance with Section 5.0. If spillage has occurred in the structure, accumulated waste will be drawn off and pumped into drum storage for disposal.

10.6.2 Refueling

Contractor will make all efforts to dispense fuel by Authorized Personnel during daylight hours. Fuel dispensing operations will be attended by Authorized Personnel at all times. Personnel will be stationed at both ends of the hose during fueling unless both ends are visible and are readily accessible by one person.

10.6.3 Refueling, Maintenance, and Fuel Storage Near Wetlands and Waterbodies

Enbridge requires that the storage of petroleum products, refueling, maintenance, and lubricating operations take place in upland areas that are more than 100 feet from wetlands, streams, and waterbodies (including drainage ditches), and water supply wells. In addition, the Contractor will store hazardous materials, chemicals, fuel and lubricating oils, and perform concrete coating activities outside these areas.

In certain instances, refueling or fuel storage may be unavoidable due to site-specific conditions or unique construction requirements (e.g., continuously operating pumps or equipment on barges). These locations will be approved in advance by the EI. Site-specific precautions, in addition to those practices described above, will be taken when refueling or maintenance activities are required within 100 feet of streams, wetlands or other waterbodies. These precautions include, but are not limited to:

- adequate amounts of absorbent materials and containment booms will be kept on hand by each construction crew to enable the rapid cleanup of any spill which may occur;
- if fuel will be stored within wetlands or near streams for refueling of continuously operating pumps, secondary containment will be used;
- secondary containment structures will be lined with suitable plastic sheeting, provide a containment volume of at least 150 percent of the storage vessel, and allow for at least one foot of freeboard; and
- provide adequate lighting for these locations and activities.

10.6.4 Overnight parking

Overnight parking of equipment (including but not limited to light plants, generators, pumps, and machinery) is not allowed within 100 feet of a wetland or waterbody unless special containment provisions have been implemented and approved by the EI in advance.

10.6.5 Concrete Washout Handling

Concrete wash water, grindings and slurry, will not be discharged to wetlands, waterbodies, and storm sewer systems or allowed to drain onto adjacent properties. Wash water disposal will be limited to a defined area of the site or to an area designated for cement washout. The area(s) will be sufficient to contain the wash water and residual cement. Contractors hired to provide concrete products will provide equipment capable of reclaiming wash water during wash out.

10.7 INITIAL SPILL MANAGEMENT

10.7.1 Immediate Response

Immediately upon learning of any fuel, oil, hazardous material or other regulated substance spill, or upon learning of conditions that will lead to an imminent spill, the person discovering the situation will:

- initiate actions to contain the fluid that has spilled or is about to spill, and initiate action to eliminate the source of the spill to the maximum extent that is safely possible; and
- notify the crew foreman and/or the Spill Coordinator and provide them with the following information:
 - location and cause of the spill;
 - the type of material that has spilled; and
 - whether the spill has reached or is likely to reach any surface water.

Upon learning of a spill or a potential spill the Spill Coordinator will:

- assess the situation and determine the need for further action;
- direct subsequent activities and/or further assign responsibilities to other personnel; and
- notify the EI.

10.7.2 Mobilization

The Spill Coordinator will mobilize on-site personnel, equipment, and materials for containment and/or cleanup commensurate with the extent of the spill. If the Spill Coordinator feels that a spill is beyond the scope of on-site equipment and personnel, the Spill Coordinator will immediately notify the Construction Superintendent that an Emergency Response Contractor is needed to contain and/or clean up the spill. Appendix E contains a list of potential Emergency Response Contractors. The Spill Coordinator will assist the Emergency Response Contractor and monitor containment procedures to ensure that the actions are consistent with the requirements of this Section.

In the event of a suspected Enbridge pipeline spill (or from an adjacent pipeline), Enbridge's Emergency Pipeline Control Center will be notified at 1-800-858-5253 (24-hours/day), as well as the Enbridge EI. Actions requiring emergency response will be coordinated by Enbridge.

10.8 SPILL NOTIFICATION RESPONSIBILITIES

10.8.1 Notification Volumes

The Contractor's Construction Superintendent or representative will notify the Enbridge Representative and the EI immediately of any spill of a petroleum product or hazardous liquid, regardless of volume.

10.8.2 Spill Report Form

The Spill Coordinator will complete a Spill Report Form (Appendix F) for each release of a regulated substance, regardless of volume. The Spill Report Form will be submitted to the EI within 24 hours of the occurrence of a spill. Follow-up written reports, associated laboratory analyses, and other documentation may also be required separately on a site-specific basis as directed by the EI. Documentation is the responsibility of the Contractor.

10.8.3 Agency Notification

The Contractor will report spills to appropriate federal, state and local agencies as soon as possible. A listing of federal, state, and local agencies including reporting thresholds and timeframes is provided in Appendix G.

The Contractor, in coordination with Enbridge and the appropriate federal, state and local agencies will ensure that additional parties or agencies are properly notified. Additionally, the Contractor is responsible for ensuring that all cleanup activities required by a jurisdictional agency are satisfactorily met and provide documentation to Enbridge demonstrating this compliance.

10.9 SPILL CONTAINMENT AND CLEANUP

In the event of a spill, the Contractor will abide by all applicable federal, state and local regulations with respect to cleaning up the spill. All clean-up and other construction related spill activities will be completed by, and costs assumed by the Contractor. Specific cleanup measures for both upland and wetland/waterbody spills are described below.

10.9.1 Spill Control - Upland Areas

- If a spill should occur during refueling operations, STOP the operation until the spill can be controlled and the situation corrected.
- The source of the spill will be identified and contained immediately.
- For large spills on land, the spill will be contained and pumped immediately into tank trucks. The Contractor or, if necessary, an Emergency Response Contractor, will excavate contaminated soil.
- The spilled material and the contaminated soil will be treated and/or disposed of in accordance with all applicable federal, state, and local agency requirements.

- Smaller spills on land will be cleaned up with absorbent materials. Contaminated soil or other materials associated with these releases will also be collected and disposed of in accordance with applicable regulations.
- Flowing spills will be contained and/or absorbed before reaching surface waters or wetlands.
- Absorbent material(s) will be placed over spills to minimize spreading and to reduce its penetration into the soil.
- The Spill Coordinator, in consultation with the EI and appropriate agencies, determine when spill sites will be evacuated as necessary to safeguard human health. Evacuation parameters will include consideration for the potential of fire, explosion, and hazardous gases.

10.10 SPILL CONTROL - WETLANDS AND WATERBODIES

In addition to the above measures, the following conditions apply if a spill occurs near or into a wetland or waterbody, regardless of size:

- If a spill occurs during refueling operations, **STOP** the operation until the spill can be controlled and the situation corrected.
- The Contractor will use absorbent booms and pads to contain and recover released materials in standing water.
- If necessary, for large spills in waterbodies, The Contractor will secure an Emergency Response Contractor to further contain and clean up the spill.
- The Contractor will excavate contaminated soils in wetlands and temporarily place them on plastic sheeting in a bermed area, a minimum of 100 feet away from the wetland. Contaminated soils will be covered with plastic sheeting while being stored temporarily and properly disposed of as soon as possible, in accordance with Section 10.11.

10.11 STORAGE AND DISPOSAL OF CONTAMINATED MATERIALS

- Appendix E lists potential treatment and disposal facilities for contaminated materials, petroleum products, and other construction-related wastes. The Contractor should recycle those wastes, such as motor oil, where there is an established recycling program available. Wastes such as grease or oily rags shall be disposed of in accordance with state requirements.
- The Contractor will store and dispose of all contaminated soils, absorbent materials, and other wastes in accordance with all applicable state and federal regulations.
- Only licensed carriers may be used to transport contaminated material from the site to a disposal facility.

- If it is necessary to temporarily store excavated soils on site, these materials will be placed on, and covered by, plastic sheeting, and the storage area bermed to prevent and contain runoff.

11.0 DRILLING FLUID RESPONSE, CONTAINMENT, AND NOTIFICATION PROCEDURES

Construction of a pipeline may include the use of trenchless methods known as the HDD and guided/road bore methods. Throughout this section, both methods are referred to collectively as “drilling”. While the HDD method always includes the use of drilling fluid, the guided or road bore method might use drilling fluid or only use water to power and lubricate the bore. The HDD drilling fluids/mud consists primarily of water mixed with inert bentonite clay. Under certain conditions an additive may need to be mixed with the drilling fluids/mud for viscosity or lubricating reasons. Only non-hazardous additives will be used and a Safety Data Sheet for the drilling fluid will be maintained on-site.

This section elaborates on measures to be implemented by the Contractor if an inadvertent release of drilling fluid occurs despite prevention efforts. Prior to the commencement of drilling operations, the Contractor will inform construction personnel involved as to the responsible party(ies) for release containment and response. The Contractor will ensure that the appropriate response personnel and containment equipment are on site for each drill/bore.

11.1 ON-SITE OBSERVATION DURING CONSTRUCTION

During construction of a drilled crossing, Contractor personnel will monitor the pipeline route throughout the process, as follows:

The Contractor will inform construction observers on what to watch for and will make them aware of the importance of timely detection and response actions to any release of drilling fluid.

- Construction observers will have appropriate, operational communication equipment (e.g., radio and cell phones) available at all times during installation of the directionally drilled crossing, with the ability to communicate directly with the HDD operator.
- The HDD operator will monitor the annular drilling fluid pressures during pilot hole operations.
- If the HDD operator identifies a sustained loss in fluid pressure or loss of circulation:
 - The operator will immediately notify the construction observers of the assumed position of the drill tool; and
 - The Contractor will visually monitor the appropriate portion of the drill path where the drill tool is located to determine if an inadvertent return occurred. The Contractor may perform this monitoring by walking or by using a boat, as appropriate.
- Construction observers, EI(s), or the Enbridge HDD craft inspector have the authority to order installation of containment structures, if needed, and to require additional response measures if deemed appropriate.

11.2 CONTAINMENT, RESPONSE, AND CLEAN-UP EQUIPMENT

Containment, response and clean-up equipment will be available at both sides of an HDD crossing location and one side of a guided or road bore prior to the commencement to assure a timely response in the event of an inadvertent release of drilling fluid. Containment and response equipment includes but is not limited to:

- A. straw bales and staking
- B. pre-filled sandbags
- C. turbidity curtain (not necessary for guided or road bores that do not involve a waterbody)
- D. silt fence
- E. plastic sheeting and/or geotextile fabric
- F. shovels, brooms, buckets, and other appropriate hand tools
- G. pumps and sufficient hose
- H. fluid storage tanks (may not be necessary for guided or road bores)
- I. vacuum truck on 24-hour call
- J. one small boat (for larger rivers and open water wetlands)
- K. light plant/generator (only necessary where operations are conducted outside of daylight hours)

11.3 RESPONSE

In the event an inadvertent drilling fluid release is observed, the EI and the Contractor will assess to determine the amount of fluid being released and potential for the release to reach sensitive resource areas (e.g., wetlands and waterbodies). Response measures will vary based on location of inadvertent release as discussed below.

11.3.1 Upland Locations

Response measures include the following:

- The EI will evaluate the release to determine if containment structures are warranted and if they will effectively contain the release.
- If the amount of the surface release is not great enough to allow the practical physical collection from the affected area, it will be diluted with clean water and/or the fluid will be allowed to dry and dissipate naturally.
- Earthen or sandbag berms, silt fence, and/or hay bales will be installed to contain small releases and prevent migration of drilling fluid.
- The Contractor will remove excess fluid at a rate sufficient to prevent an uncontrolled release.
- If the amount of the surface release exceeds that which can be completely contained with hand-placed barriers, small collection sumps (less than 5 cubic yards) may be used (with approval from Enbridge) to remove released drilling fluid by the use of portable pumps and hoses.

- The EI will inform the Contractor to initiate immediate suspension of drilling operations if the fluid release cannot be effectively contained.

11.3.2 Wetland and Waterbody Locations

This section also applies to areas immediately adjacent to wetlands and waterbodies, such as stream banks or steep slopes, where drilling fluid releases could quickly reach surface waters.

- In the event of a drilling fluid release in wetlands, waterbodies, or adjacent areas:
 1. The EI will evaluate the release, and the Contractor will implement appropriate containment measures.
 2. The EI and the Contractor will evaluate the recovery measures to determine the most effective collection method.
 3. Enbridge Engineering and the Contractor will review and consider adjusting drill pressures, pump volume rates, and drill profile, based on BMPs, to minimize the extent of the release.
 4. Enbridge will suspend drilling operations if containment measures do not effectively control the release.
- If the amount of the surface release exceeds that which can be contained with hand-placed barriers, small collection sumps (less than 5 cubic yards) may be utilized to collect released drilling fluid for removal by the use of portable pumps and hoses.
- If the amount of the surface release is not great enough to allow the practical physical collection from the affected area without causing additional impacts, with approval from both Enbridge Environmental and Construction Management, the drilling fluid may be diluted with clean water and/or the fluid will be allowed to dry and dissipate naturally.
- Excess fluid will be held within the containment area and removed using pumps or other appropriate measures at a rate sufficient to maintain secure containment.
- Recovered fluid will be stored in a temporary holding tank or other suitable structure out of the floodplain and/or wetland for reuse or eventual disposal in an approved disposal facility
- Enbridge will consult with the appropriate regulatory agencies to evaluate the circumstances of the release, discuss additional containment or cleanup requirements, and determine whether and under what conditions the HDD may proceed.

11.4 NOTIFICATION AND RESUMPTION OF SUSPENDED HDD OPERATIONS

The Contractor will immediately notify the EI of all drilling fluid releases. If the EI determines the release affects wetland or waterbody areas, he or she will immediately notify Enbridge Environment and Construction Management and the appropriate regulatory agencies.

If notifications are necessary during non-business hours they will be done according to prior arrangements made between Enbridge and the regulatory agencies. Follow-up notifications will be made as necessary and practicable.

The conditions under which drilling/boring operations can resume will be discussed with appropriate regulatory agencies and/or field representatives. If containment measures are functioning, and the circumstances and potential impacts of the release are understood, drilling/boring operations will resume.

11.5 CLEAN-UP

The following measures are to be considered as appropriate:

- Drilling fluid will be cleaned up by hand using hand shovels, buckets and soft-bristled brooms as possible without causing extensive ancillary damage to existing vegetation. Clean water washes may also be employed if deemed beneficial and feasible.
- Containment structures will be pumped out and the ground surface scraped to bare topsoil without causing undue loss of topsoil or ancillary damage to existing and adjacent vegetation.
- Material will be collected in containers for temporary storage prior to removal from the site.
- The EI will regularly evaluate the potential for secondary impact from the clean-up process and clean-up activities terminated if physical damage to the site is deemed to exceed the benefits of removal activities. This decision will be made in consultation with the appropriate regulatory agencies and/or Enbridge.


11.6 RESTORATION AND POST-CONSTRUCTION MONITORING

Following cleanup activities, restoration and revegetation of affected areas will be completed in accordance with all applicable local, state, and federal permits in addition to Enbridge's EPP. Enbridge will monitor the release site as appropriate to assure adequate restoration.

This page intentionally left blank

Figures

This page intentionally left blank

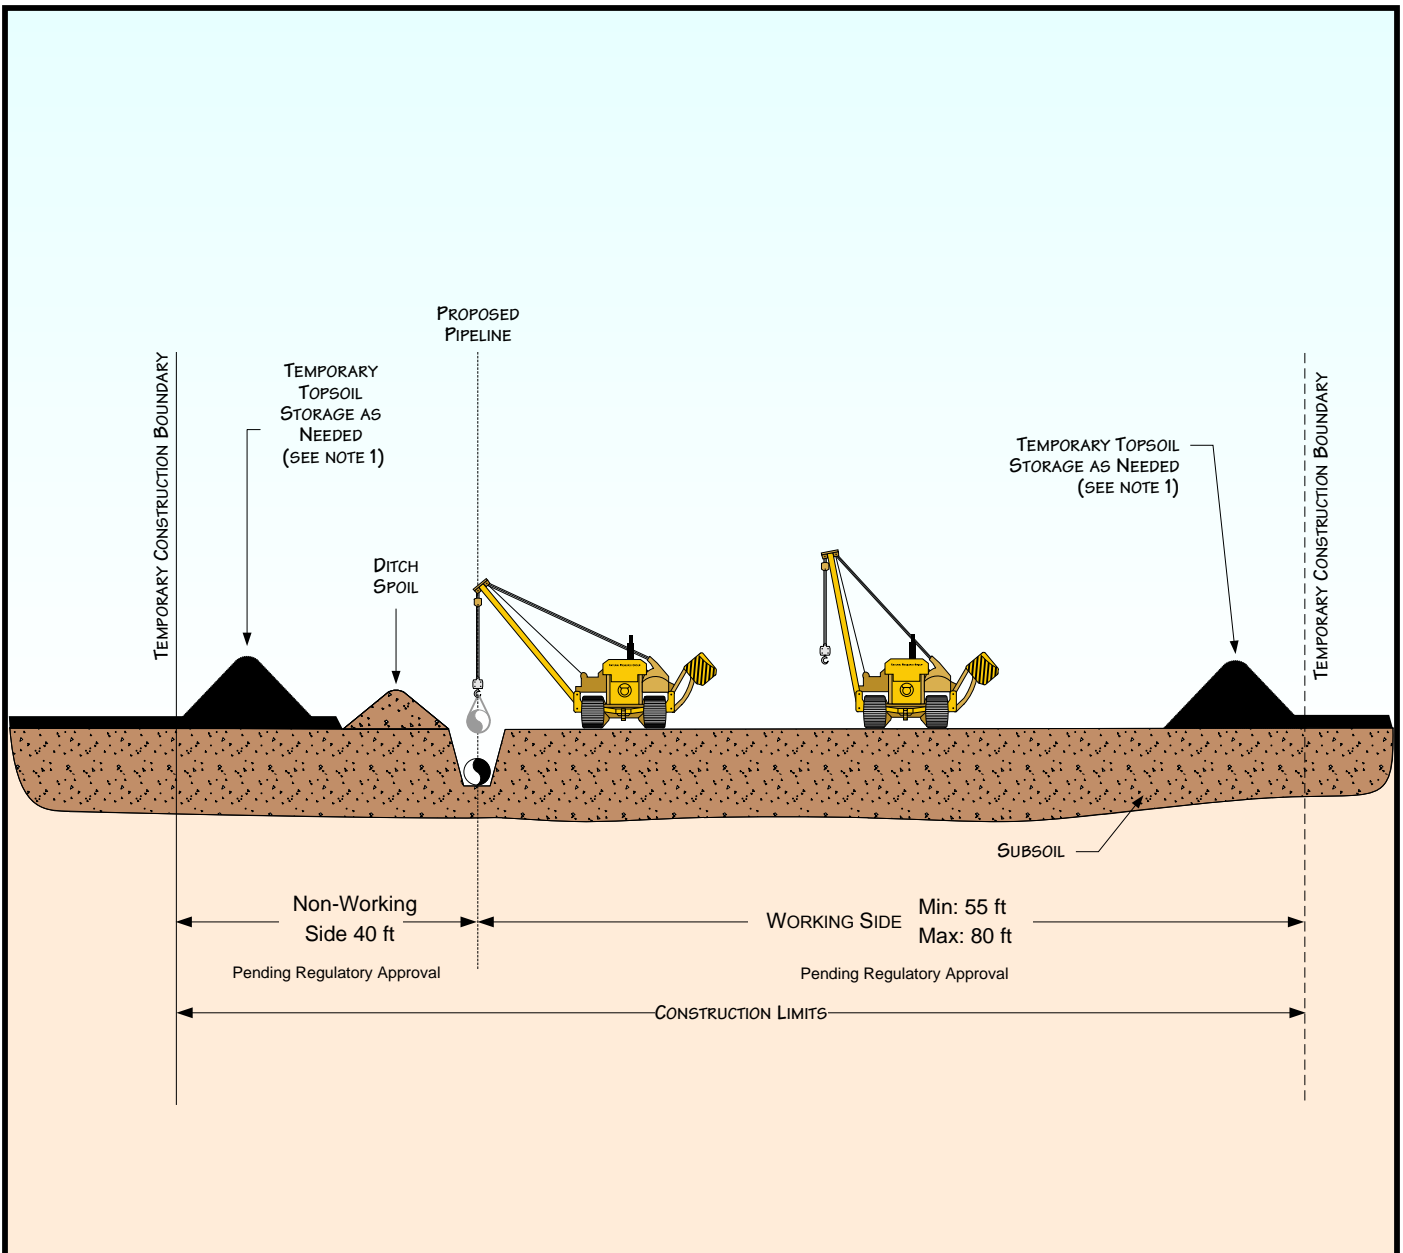

PROFILE


NOTES:

1. STOCKPILE TOPSOIL SEPARATELY FROM DITCH SPOIL AS SHOWN OR IN OTHER CONFIGURATIONS APPROVED BY THE COMPANY.



Figure 1
Environmental Protection Plan
 Typical Topsoil Segregation - Full Right-of-Way

DATE: 7/9/2001	
REVISED: 3/11/2011	
SCALE: NTS	
DRAWN BY: JPBOENTJE	
K:\CLIENT_PROJECTS\ID-FIEEL\2011-019\FIG 1-3_TYPICAL_TOPSOIL_SEGREGATION.VSD	

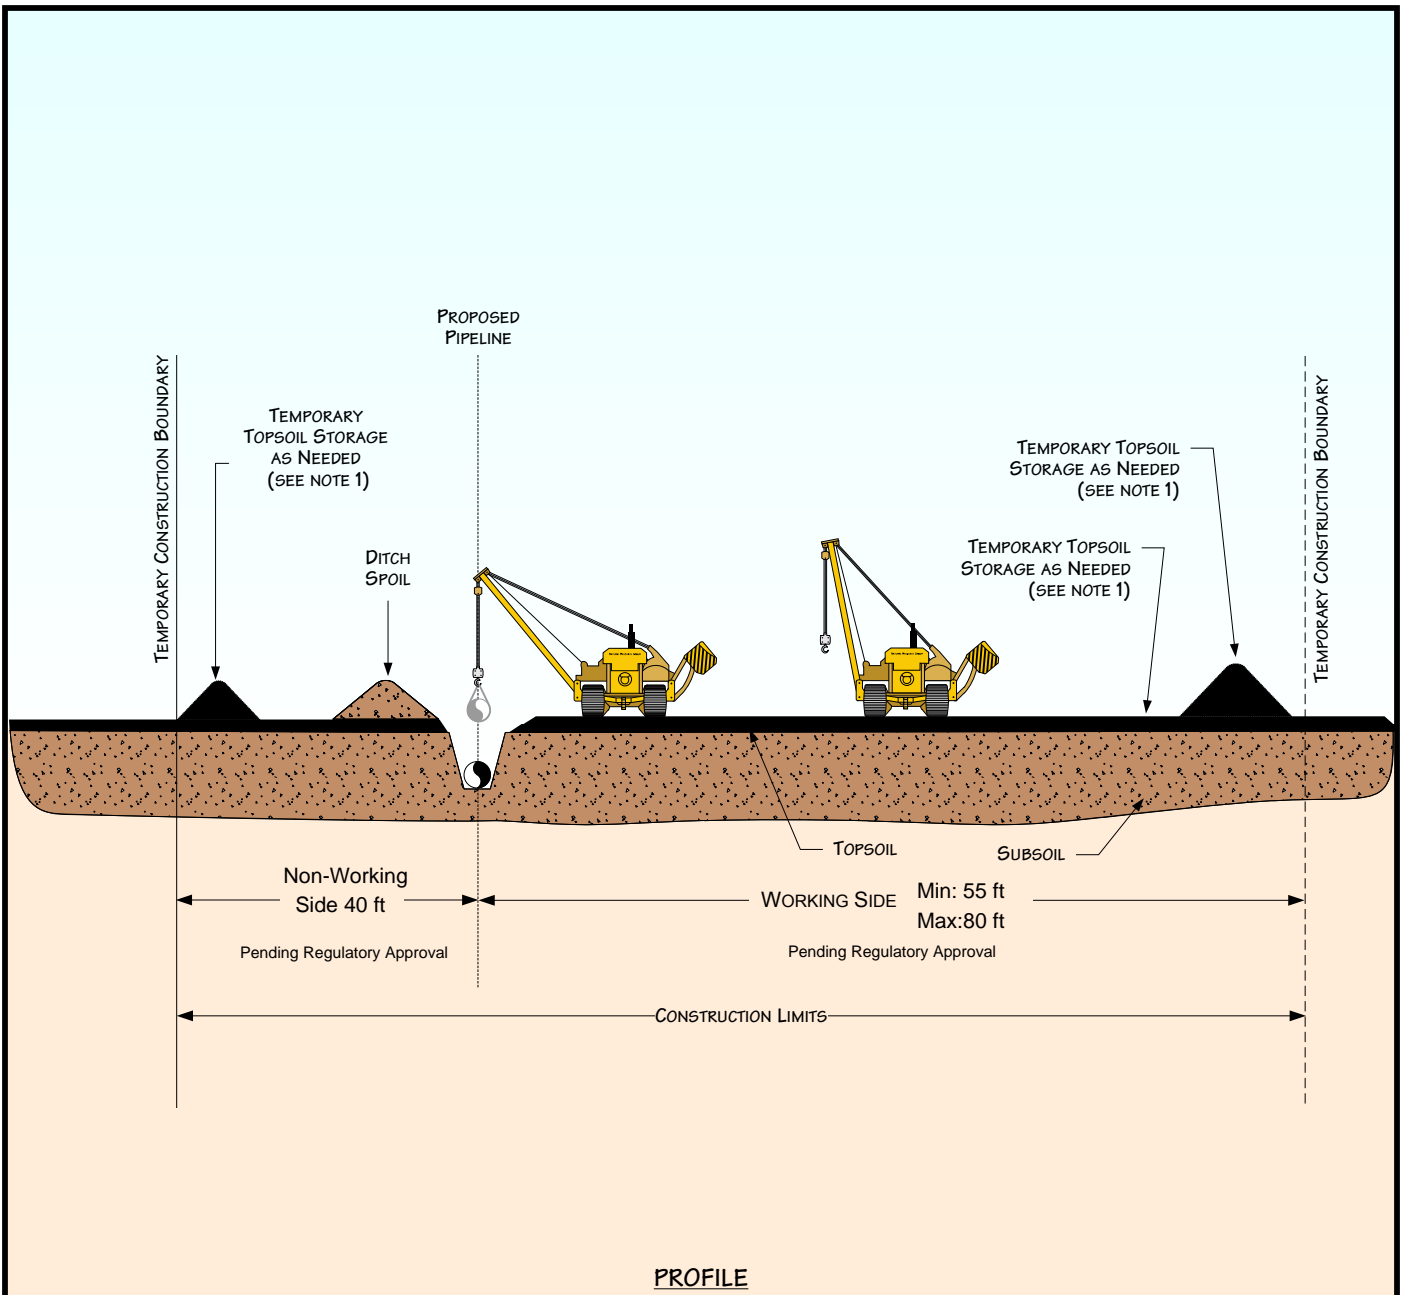

PROFILE


NOTES:

- 1. STOCKPILE TOPSOIL SEPARATELY FROM DITCH SPOIL AS SHOWN OR IN OTHER CONFIGURATIONS APPROVED BY THE COMPANY.



Figure 2
Environmental Protection Plan
 Typical Topsoil Segregation –
 Trench Line Only

DATE: 7/9/2001	
REVISED: 3/11/2011	
SCALE: NTS	
DRAWN BY: JPBOENTJE	
<small> K:\CLIENT_PROJECTS\ID-FIEEL\2011-019\FIG 1-3_TYPICAL_TOPSOIL_SEGREGATION.VSD </small>	

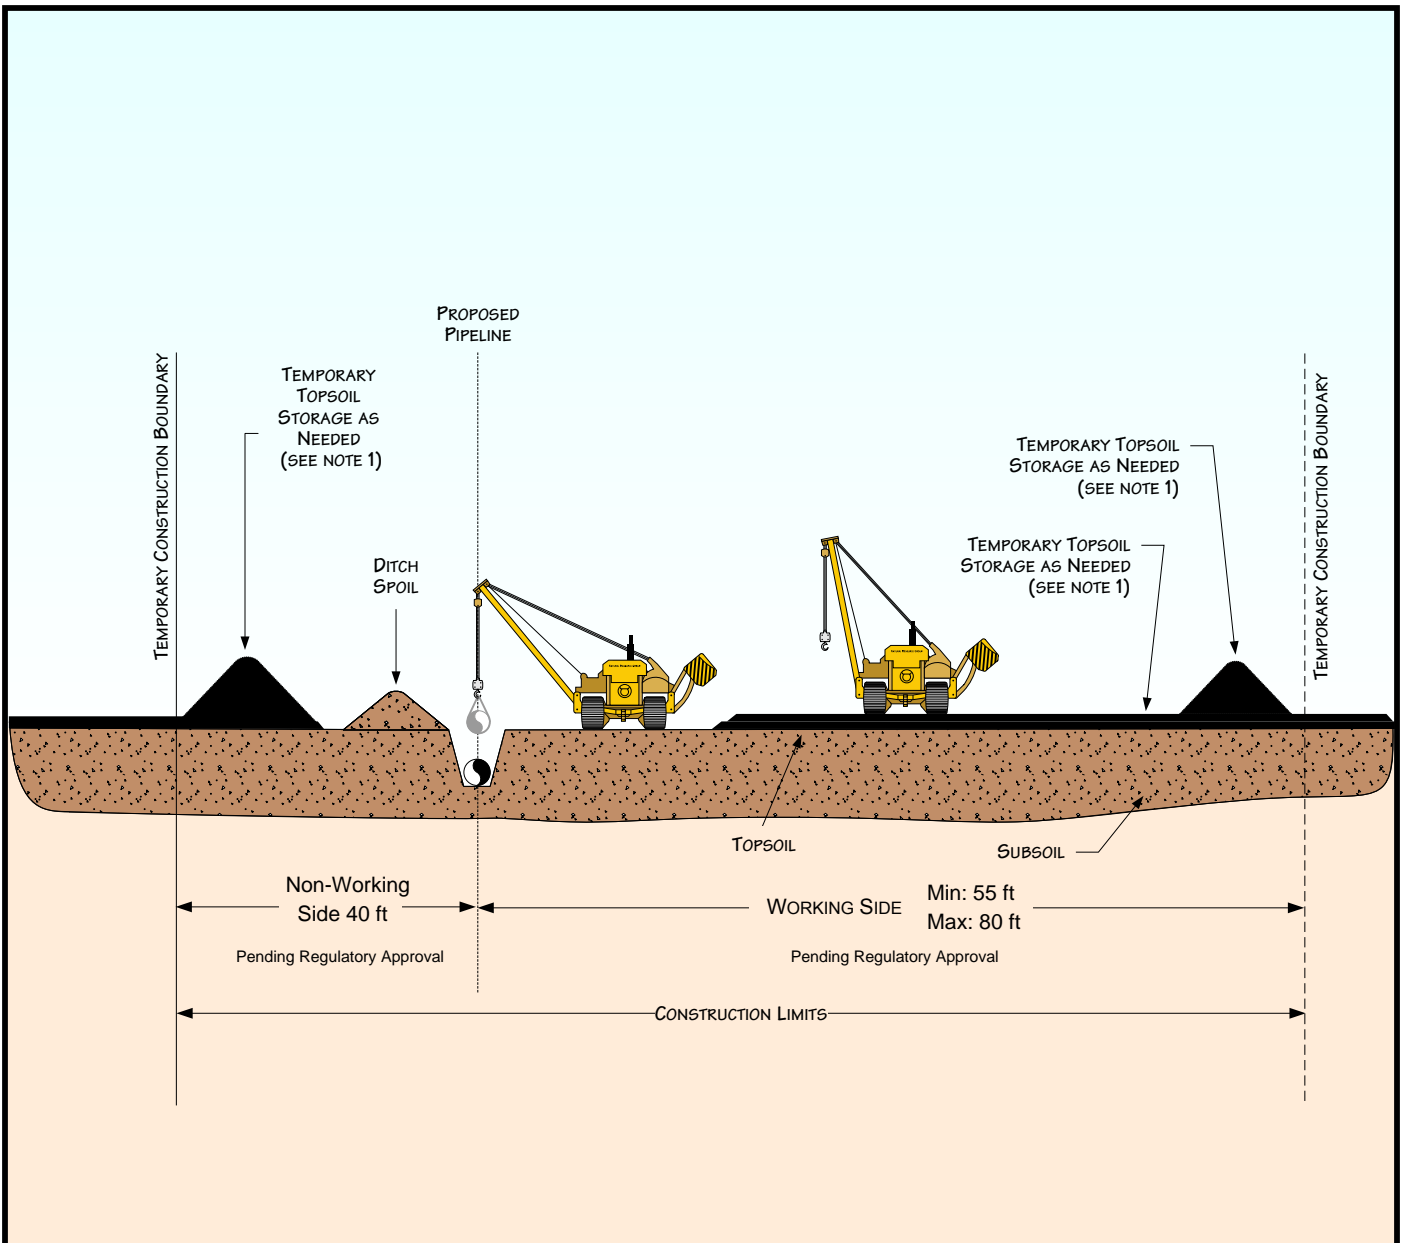

PROFILE


NOTES:

- 1. STOCKPILE TOPSOIL SEPARATELY FROM DITCH SPOIL AS SHOWN OR IN OTHER CONFIGURATIONS APPROVED BY THE COMPANY.



Figure 3
Environmental Protection Plan
 Typical Topsoil Segregation –
 Modified Ditch Plus Spoil Side

DATE: 7/9/2001	
REVISED: 3/11/2011	
SCALE: NTS	
DRAWN BY: JPBOENTJE	
<small> K:\CLIENT_PROJECTS\ID-FIEEL\2011-019\FIG 1-3_TYPICAL_TOPSOIL_SEGREGATION.VSD </small>	

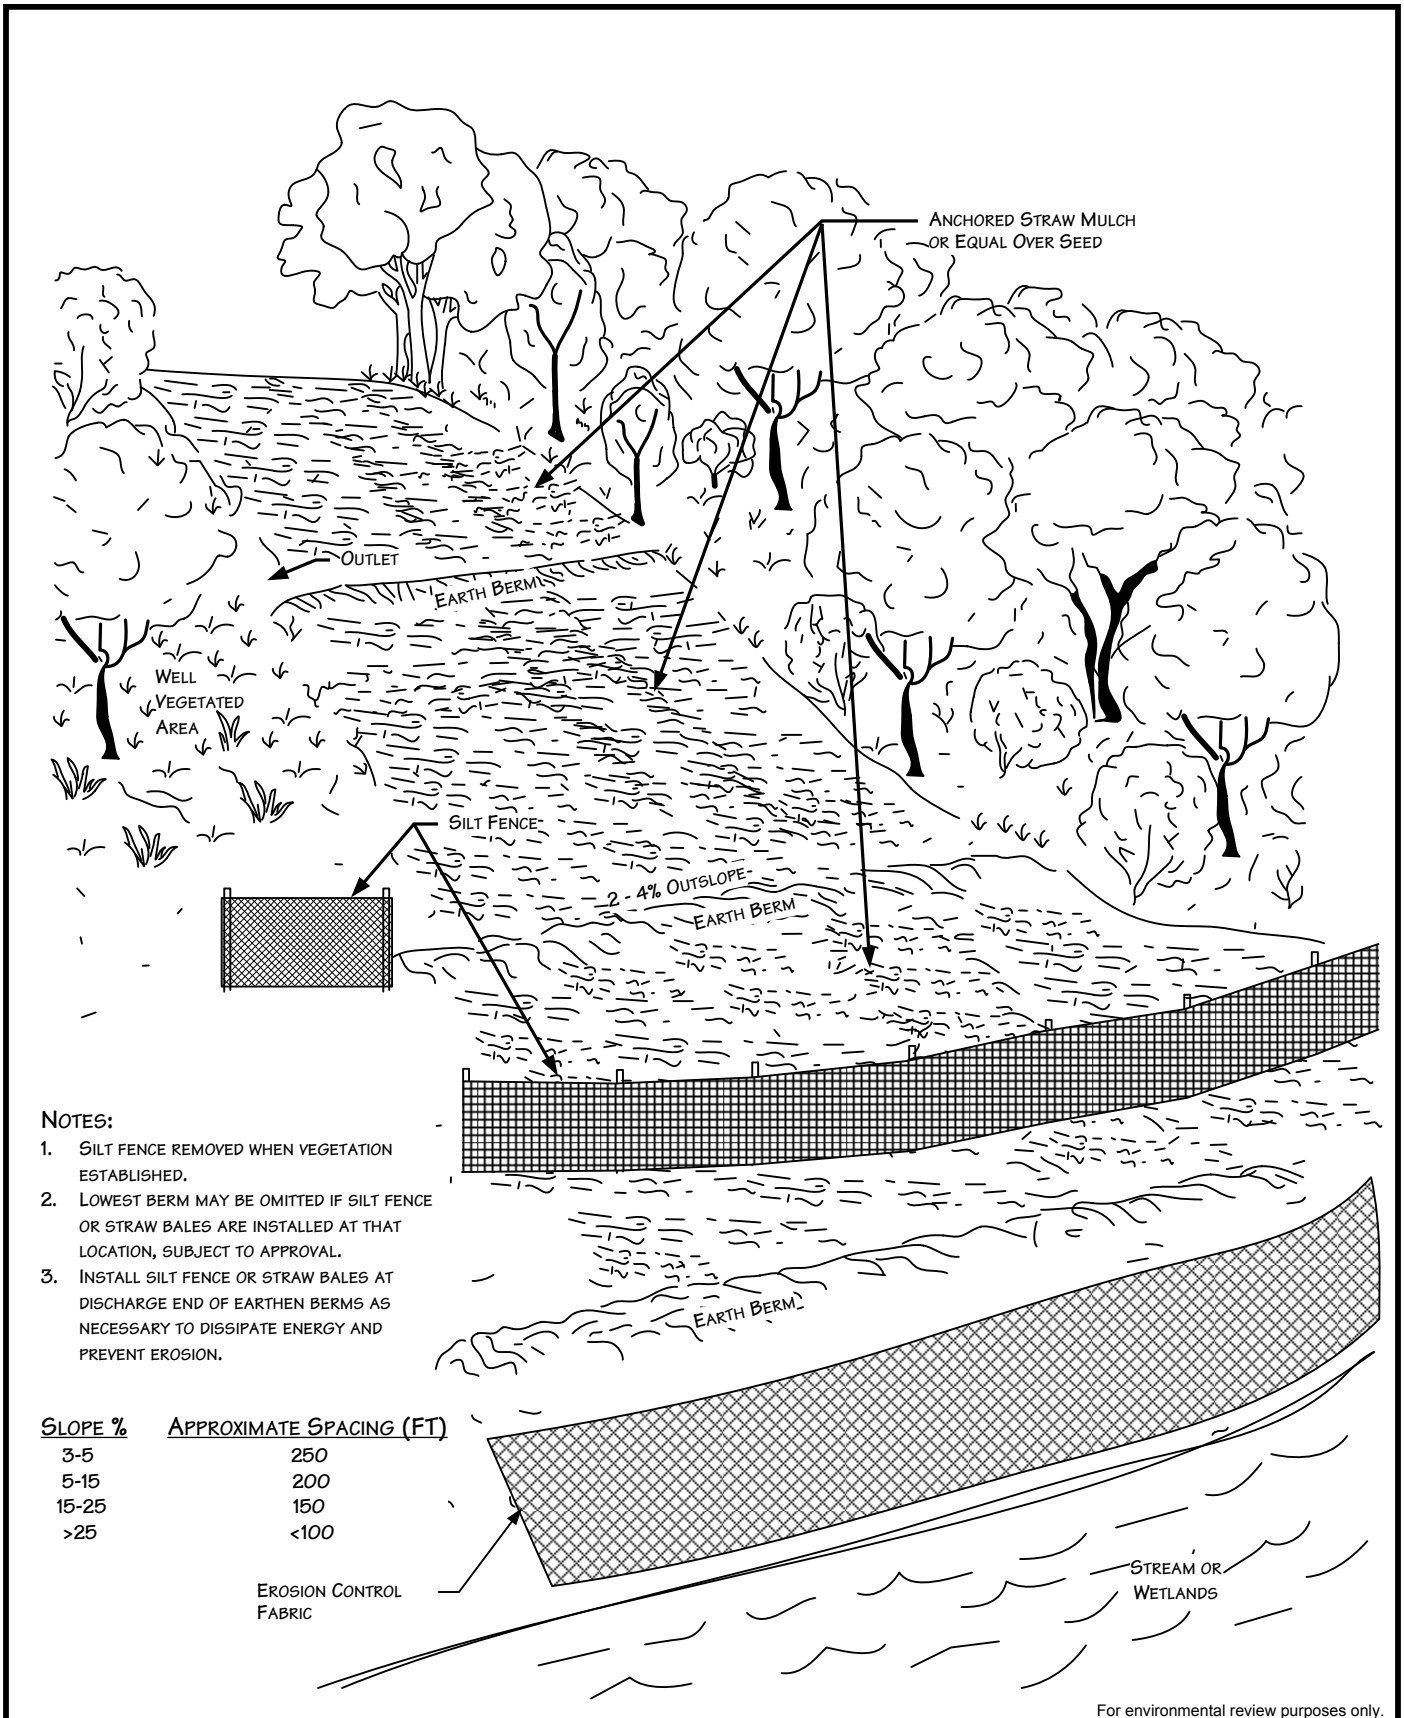

NOTES:

1. SILT FENCE REMOVED WHEN VEGETATION ESTABLISHED.
2. LOWEST BERM MAY BE OMITTED IF SILT FENCE OR STRAW BALES ARE INSTALLED AT THAT LOCATION, SUBJECT TO APPROVAL.
3. INSTALL SILT FENCE OR STRAW BALES AT DISCHARGE END OF EARTHEN BERMS AS NECESSARY TO DISSIPATE ENERGY AND PREVENT EROSION.

SLOPE %	APPROXIMATE SPACING (FT)
3-5	250
5-15	200
15-25	150
>25	<100


For environmental review purposes only.



Figure 4
Environmental Protection Plan
 Typical Temporary or Permanent Berms
 Perspective View

DATE: 11/14/2000
 REVISED: 3/11/2011
 SCALE: NTS
 DRAWN BY: KMKENDALL
K:\ CLIENT PROJECTS\ID-PEEL\2011-019\ FIG_4_BERMS_PERSPECTIVE_VIEW.VSD



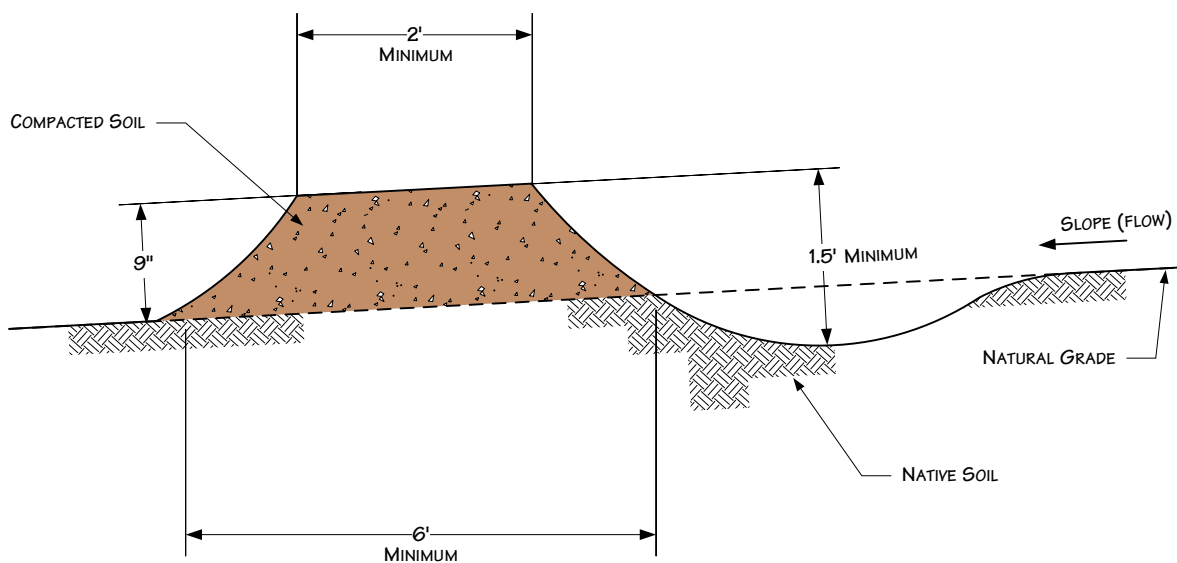

NOTES





1. BERMS SHALL BE CONSTRUCTED WITH 2 TO 4 PERCENT OUTSLOPE.
2. BERMS SHALL BE OUTLETED TO WELL VEGETATED STABLE AREAS, SILT FENCES, STRAW BALES OR ROCK APRONS.
3. BERMS SHALL BE SPACED AS DESCRIBED IN CONSTRUCTION SPECIFICATIONS.
4. ADDITIONAL INFORMATION INCLUDED ON OTHER DRAWINGS.

For environmental review purposes only.



Figure 5
Environmental Protection Plan
 Typical Temporary or Permanent Berms
 Elevation View

DATE: 5/25/2001	
REVISED: 3/11/2011	
SCALE: NTS	
DRAWN BY: KMKENDALL	
K:\CLIENT PROJECTS\ID-PEEL\2011-019\FIG_5_BERMS_ELEVATION_VIEW.VSD	

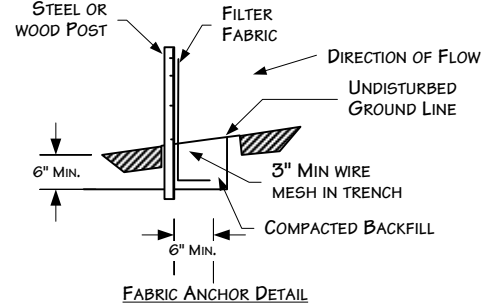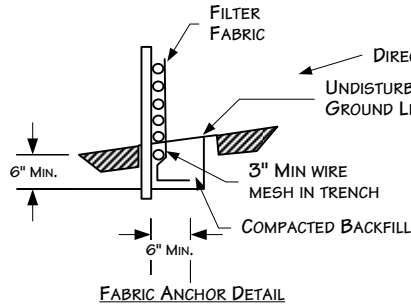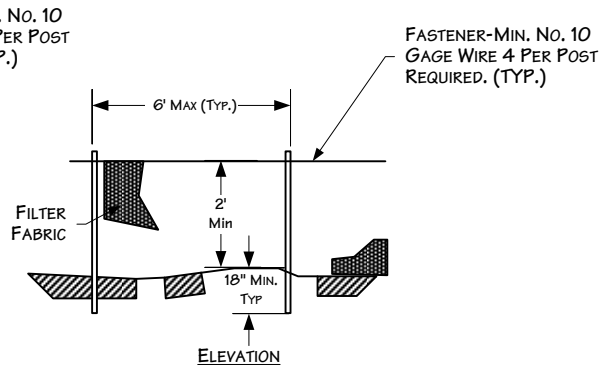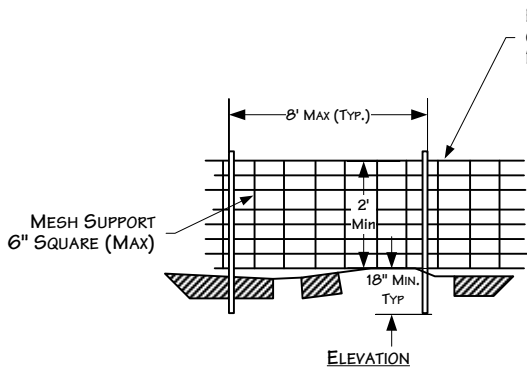


SILT FENCE WITH WIRE SUPPORT PLAN

SILT FENCE PLAN
NTS

NOTES:

1. WIRES OF MESH SUPPORT SHALL BE MIN. GAGE NO. 12.
2. FILTER FABRIC SHALL MEET THE REQUIREMENTS OF THE SPECIFICATION WITH EQUIVALENT OPENING SIZE OF AT LEAST 30 FOR NONWOVEN AND 50 FOR WOVEN. (SIEVE NO.)
3. THE POSTS USED TO SUPPORT THE SILT FENCE SHOULD BE HARDWOOD MATERIAL WITH A MINIMUM CROSS SECTIONAL AREA OF 4 INCHES SQUARE AND 4 FEET LONG. METAL POSTS SHOULD BE USED IN AREAS THAT POND WATER.

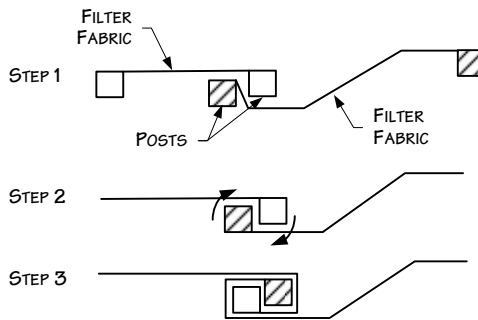

ATTACHING TWO SILT FENCES

NOTES:

1. PLACE THE END POST OF THE SECOND FENCE INSIDE THE END POST OF THE FIRST FENCE.
2. ROTATE BOTH POSTS AT LEAST 180 DEGREES IN A CLOCKWISE DIRECTION TO CREATE A TIGHT SEAL WITH THE FABRIC MATERIAL.
3. DRIVE BOTH POSTS A MINIMUM OF 18 INCHES IN THE GROUND AND BURY THE FLAP.

For environmental review purposes only.



Figure 6
Environmental Protection Plan
Typical Silt Fence Installation

DATE: 5/25/2001



REVISED: 3/23/2011

SCALE: NTS


DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG_6_SILT_FENCE_INSTALL.VSD



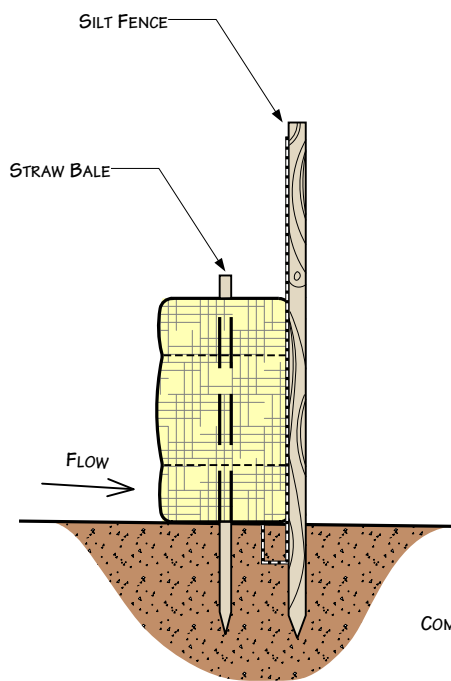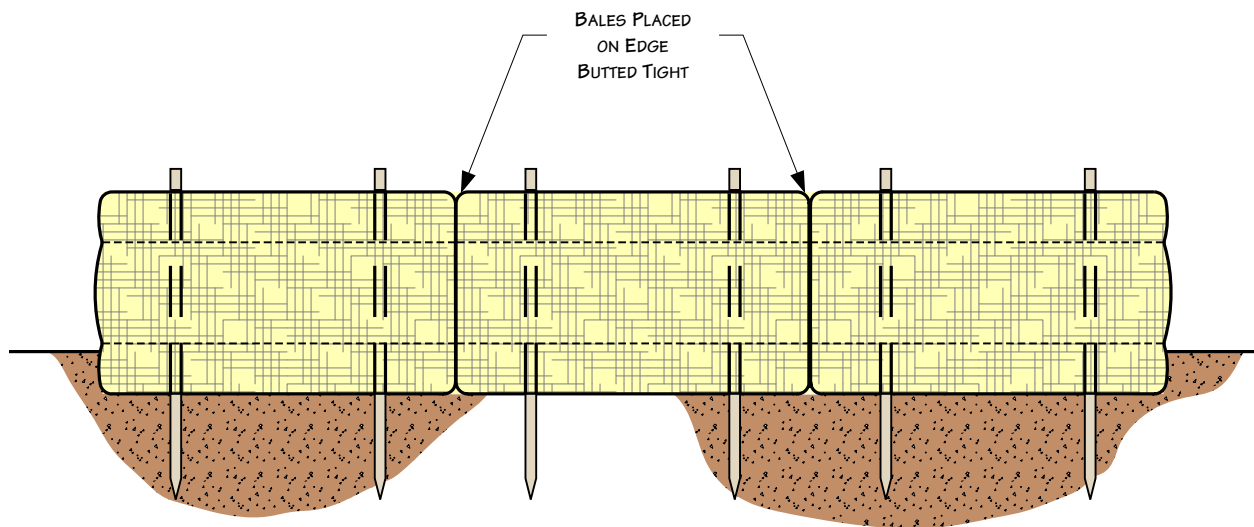

STRAW BALES & SILT FENCE

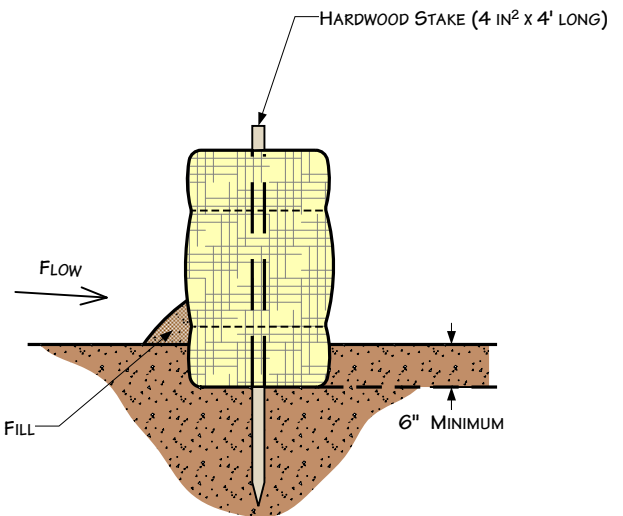

STRAW BALES ONLY

For environmental review purposes only.



Figure 7
Environmental Protection Plan
Typical Straw Bale Installation

DATE: 5/25/01

REVISED: 3/11/11

SCALE: Not to Scale


DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG_7_STRAW_BALE_INSTALL.VSD





FILL SLOPE SECTION
 EROSION CONTROL BLANKETS SHOULD BE
 INSTALLED VERTICALLY DOWNSLOPE.

NOTE: SLOPE SURFACE SHALL BE
 SMOOTH AND FREE OF ROCKS,
 LUMPS OF DIRT, GRASS AND STICKS.
 MAT SHALL BE PLACED FLAT ON SURFACE
 TO ENSURE PROPER SOIL CONTACT.




TOE
 MAINTAIN SLOPE ANGLE

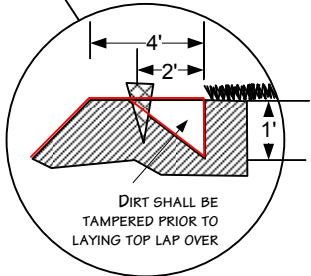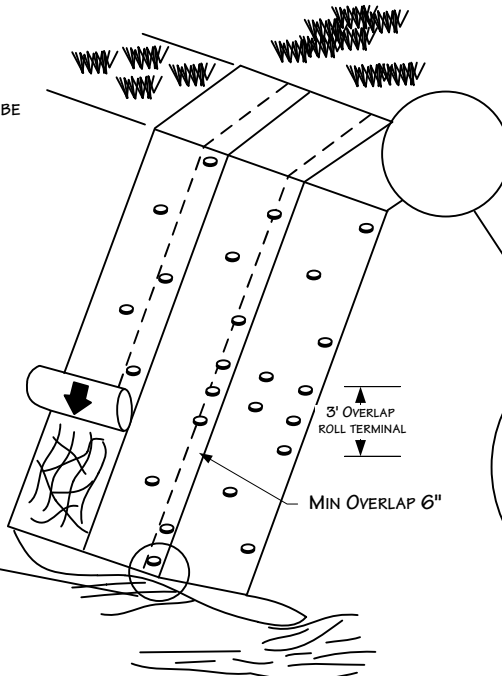

BERM
 TRENCH INTO BERM AND
 PROGRESS DOWNSLOPE

STREAM CHANNEL
 EROSION CONTROL BLANKETS SHOULD BE
 INSTALLED HORIZONTALLY WITH STREAM FLOW.

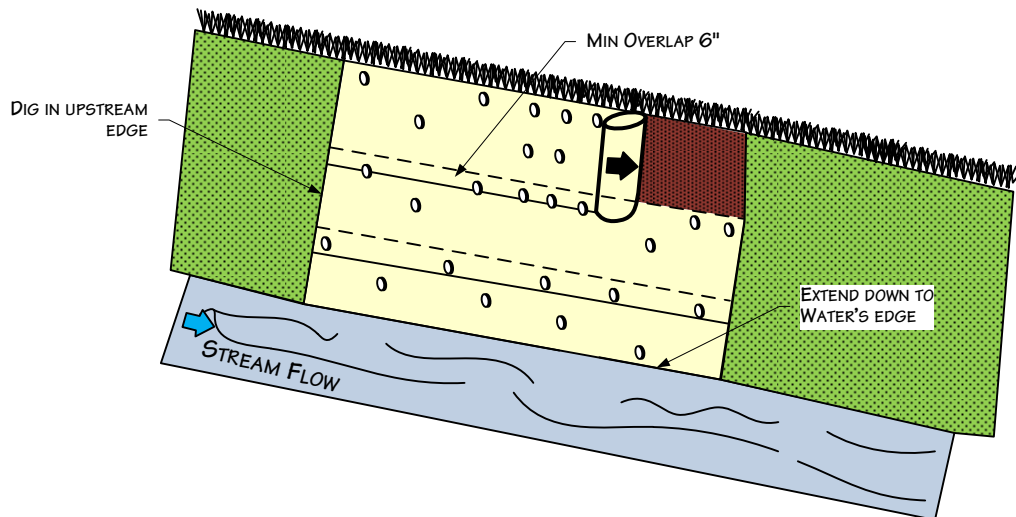


For environmental review purposes only.




Figure 8
 Environmental Protection Plan
 Typical Erosion Control Blanket Installation

DATE: 5/25/2001
 REVISED: 3/23/2011
 SCALE: NTS
 DRAWN BY: KMKENDALL
K:\CLIENT PROJECTS\ID-FIEEL\2011-019\FIG 8 EROSION_CONTROL_BLANKET_INS TALL.VSD





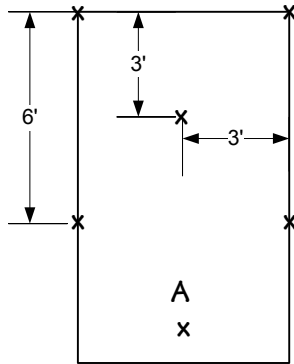


1 STAPLE PER SQ. YD

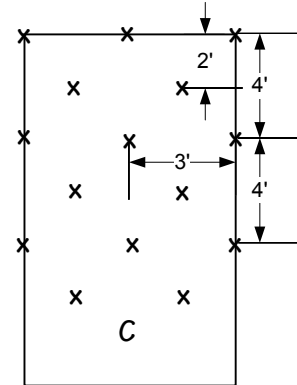

2 STAPLES PER SQ. YD

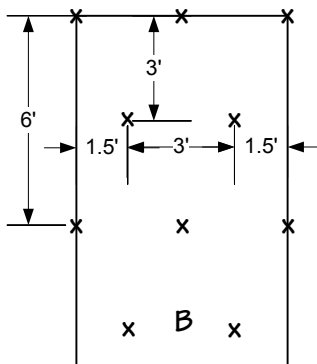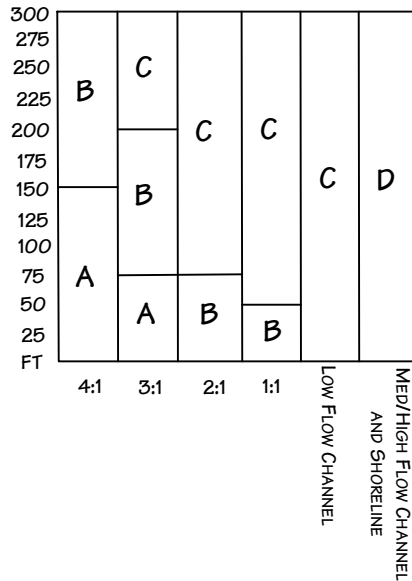

1 1/2 STAPLES PER SQ. YD

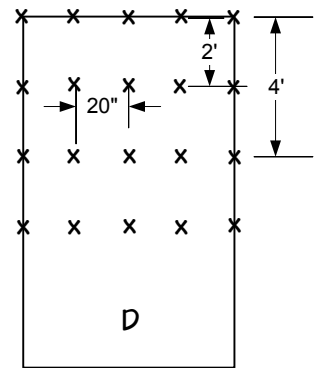

3 1/2 STAPLES PER SQ. YD

FOR OPTIMUM RESULTS, THESE RECOMMENDED STAPLE PATTERN GUIDES MUST BE FOLLOWED. SUGGESTED ANCHORING METHODS VARY ACCORDING TO THE MANUFACTURER. THIS CHART SHOWS HOW TO SLOPE LENGTHS AND HOW GRADIENTS AFFECT SAMPLING PATTERNS.

For environmental review purposes only.



Figure 9
Environmental Protection Plan
Typical Staple Pattern for
Erosion Control Fabric

DATE: 5/25/2001





REVISED: 3/24/2011

SCALE: NTS

DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG 9_STAPLE_PATTERN_EROSION_CON TROL_FABRIC.VSD



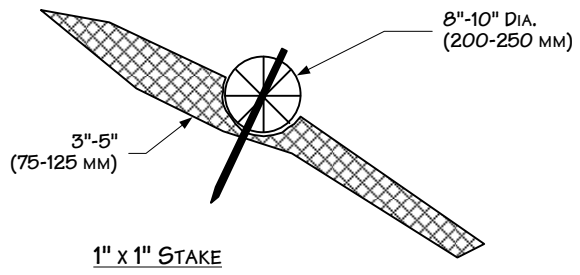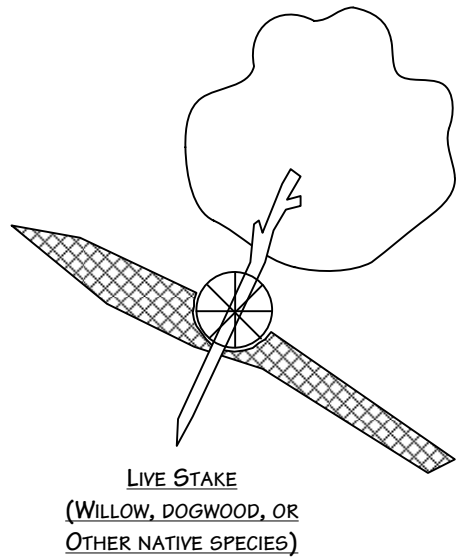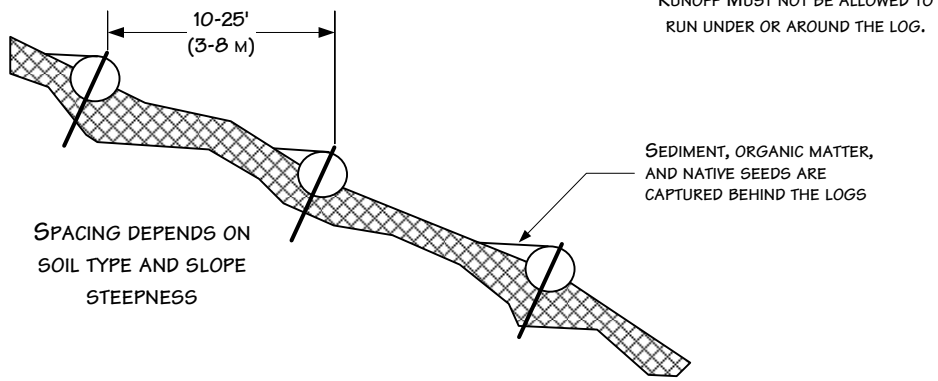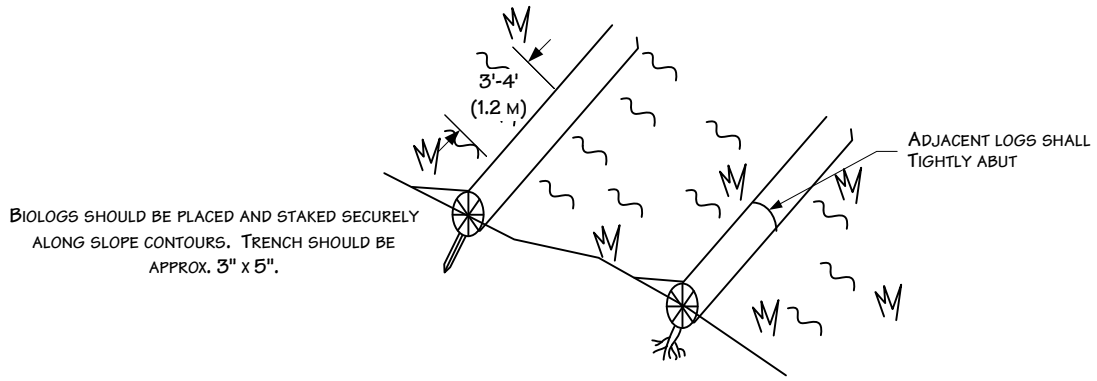


For environmental review purposes only.



Figure 10
Environmental Protection Plan
Typical Biolog Installation

DATE: 5/25/2001	
REVISED: 3/24/2011	
SCALE: NTS	
DRAWN BY: KMKENDALL	
K:\ CLIENT PROJECTS\ID-PEEL\2011-019\ FIG_10_BIOLOG INSTALL.VSD	

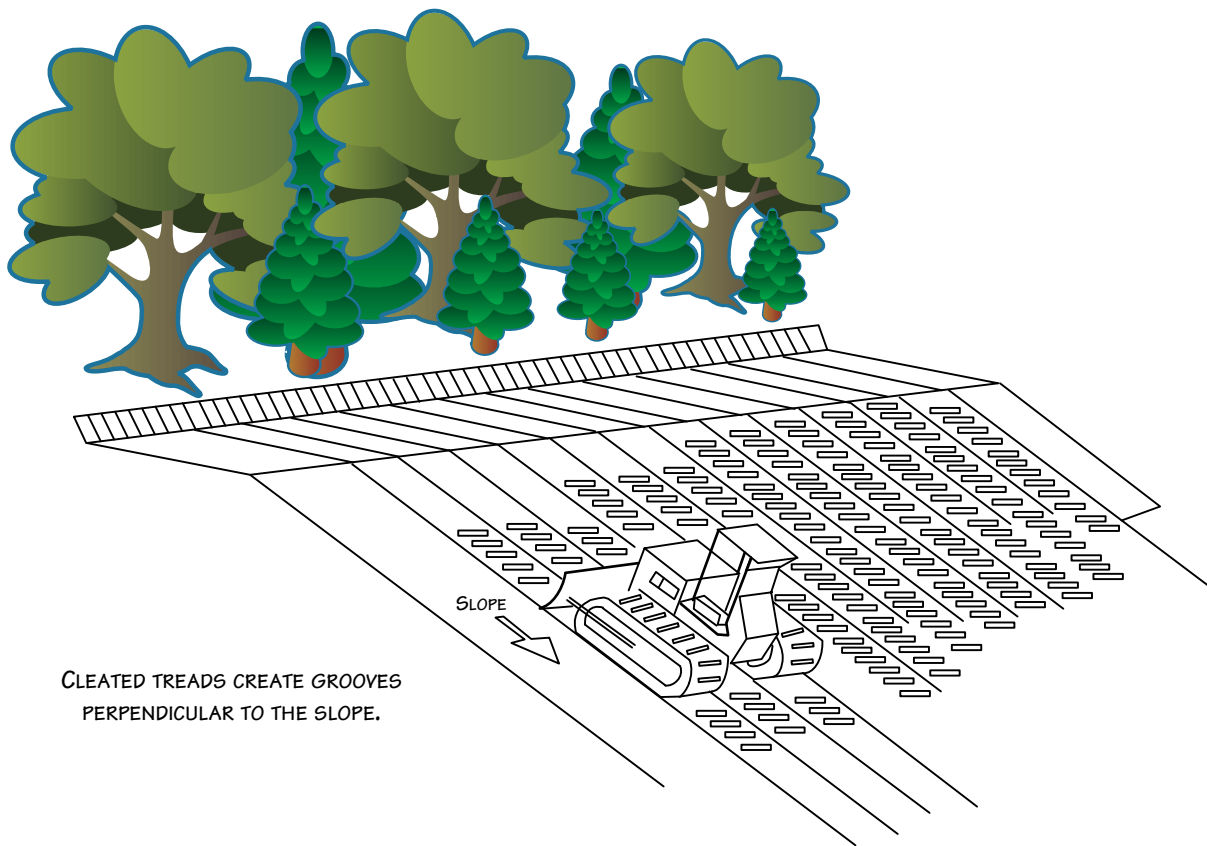

CLEATED TREADS CREATE GROOVES
PERPENDICULAR TO THE SLOPE.

For environmental review purposes only.



Figure 11
Environmental Protection Plan
Typical Cat Tracking

DATE: 5/25/2001


REVISED: 3/24/2011

SCALE: NTS

DRAWN BY: KMKENDALL

K:\CLIENT_PROJECTS\ID-FEEL\2011-019\
FIG_11_CAT_TRACKING.VSD



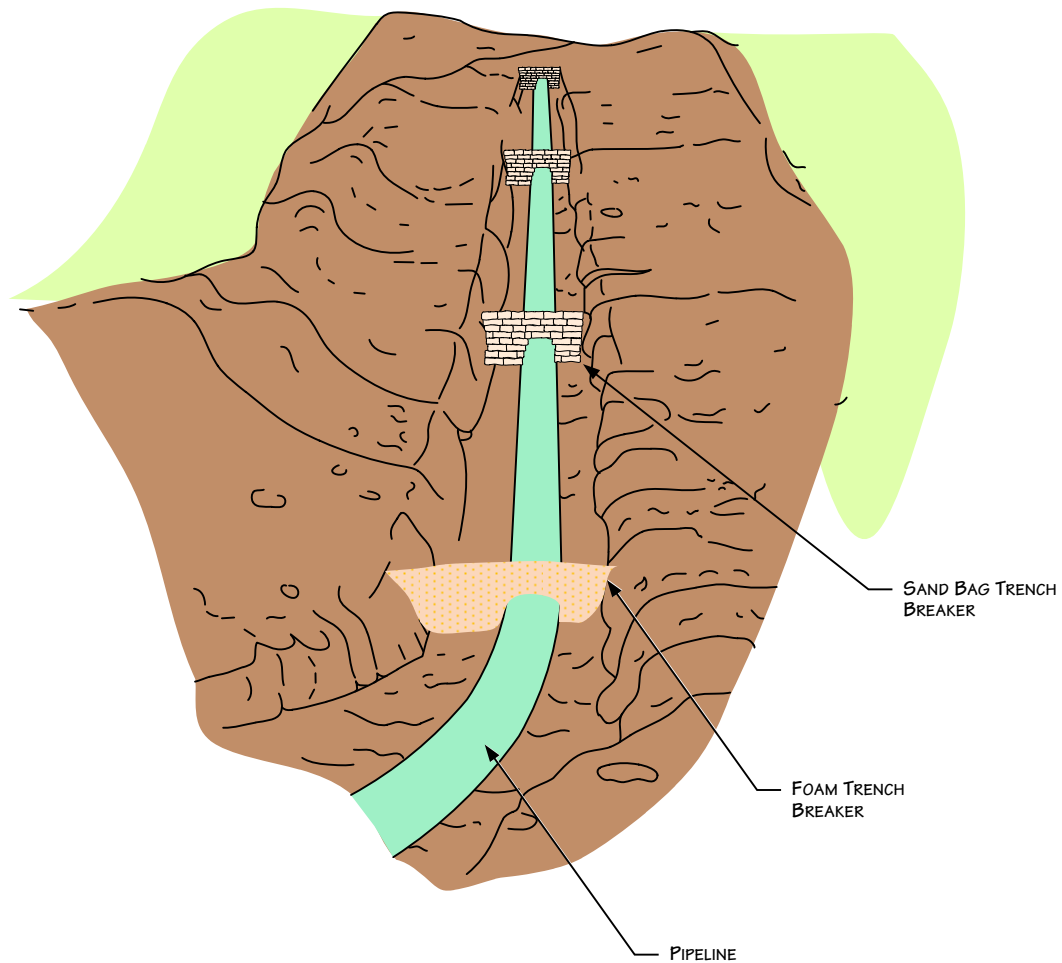

NOTES

1. BAGS WILL NOT BE FILLED WITH TOPSOIL.
2. ADDITIONAL INFORMATION INCLUDED ON OTHER DRAWINGS.

For environmental review purposes only.



Figure 12
Environmental Protection Plan
 Typical Trench Breakers - Perspective View

DATE: 5/25/2001




REVISED: 3/11/11

SCALE: NTS

DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG_12_TRENCH_BREAKER_PERSPECTIV E_VIEW.VSD



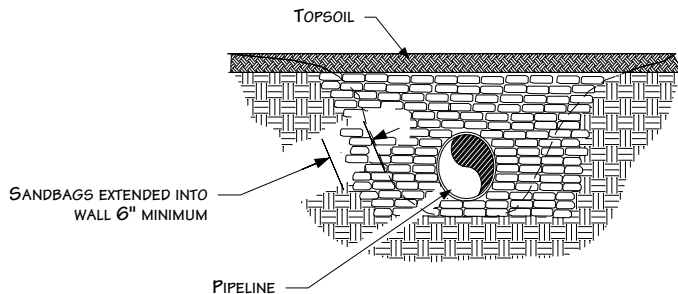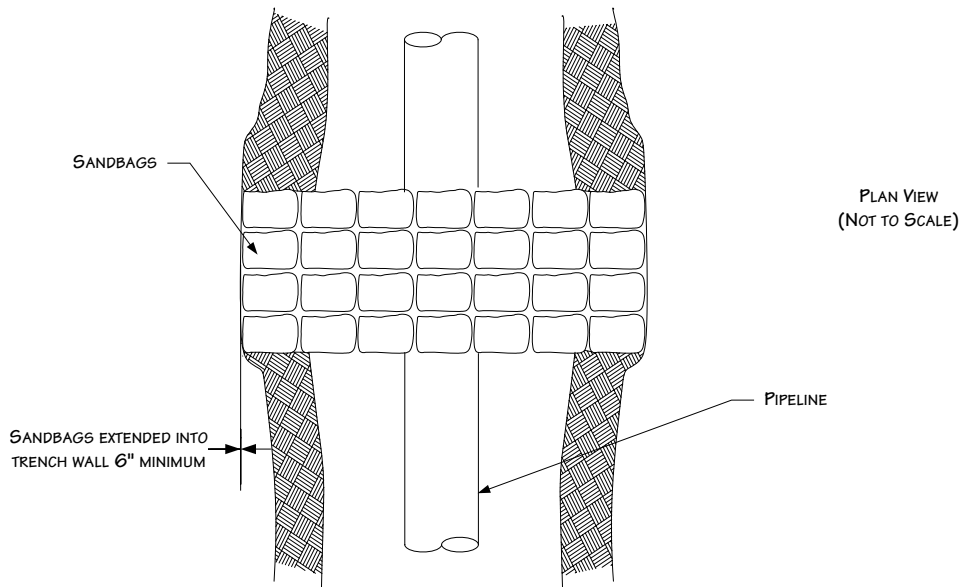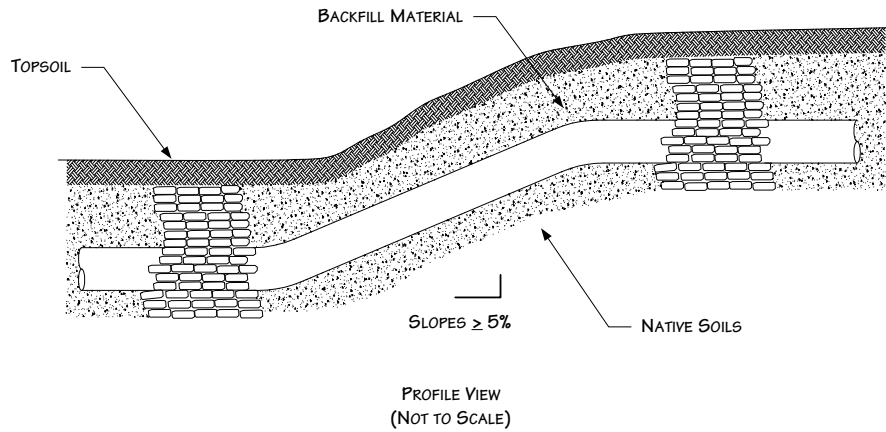

NOTES

1. BAGS WILL NOT BE FILLED WITH TOPSOIL
2. ADDITIONAL INFORMATION INCLUDED ON OTHER DRAWINGS

For environmental review purposes only.



Figure 13
Environmental Protection Plan
 Typical Trench Breakers – Plan & Profile View

DATE: 11/15/2000


REVISED: 3/11/11

SCALE: NTS

DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG_13_TRENCH_BREAKER_PLAN_PROFIL_E_VIEW.VSD



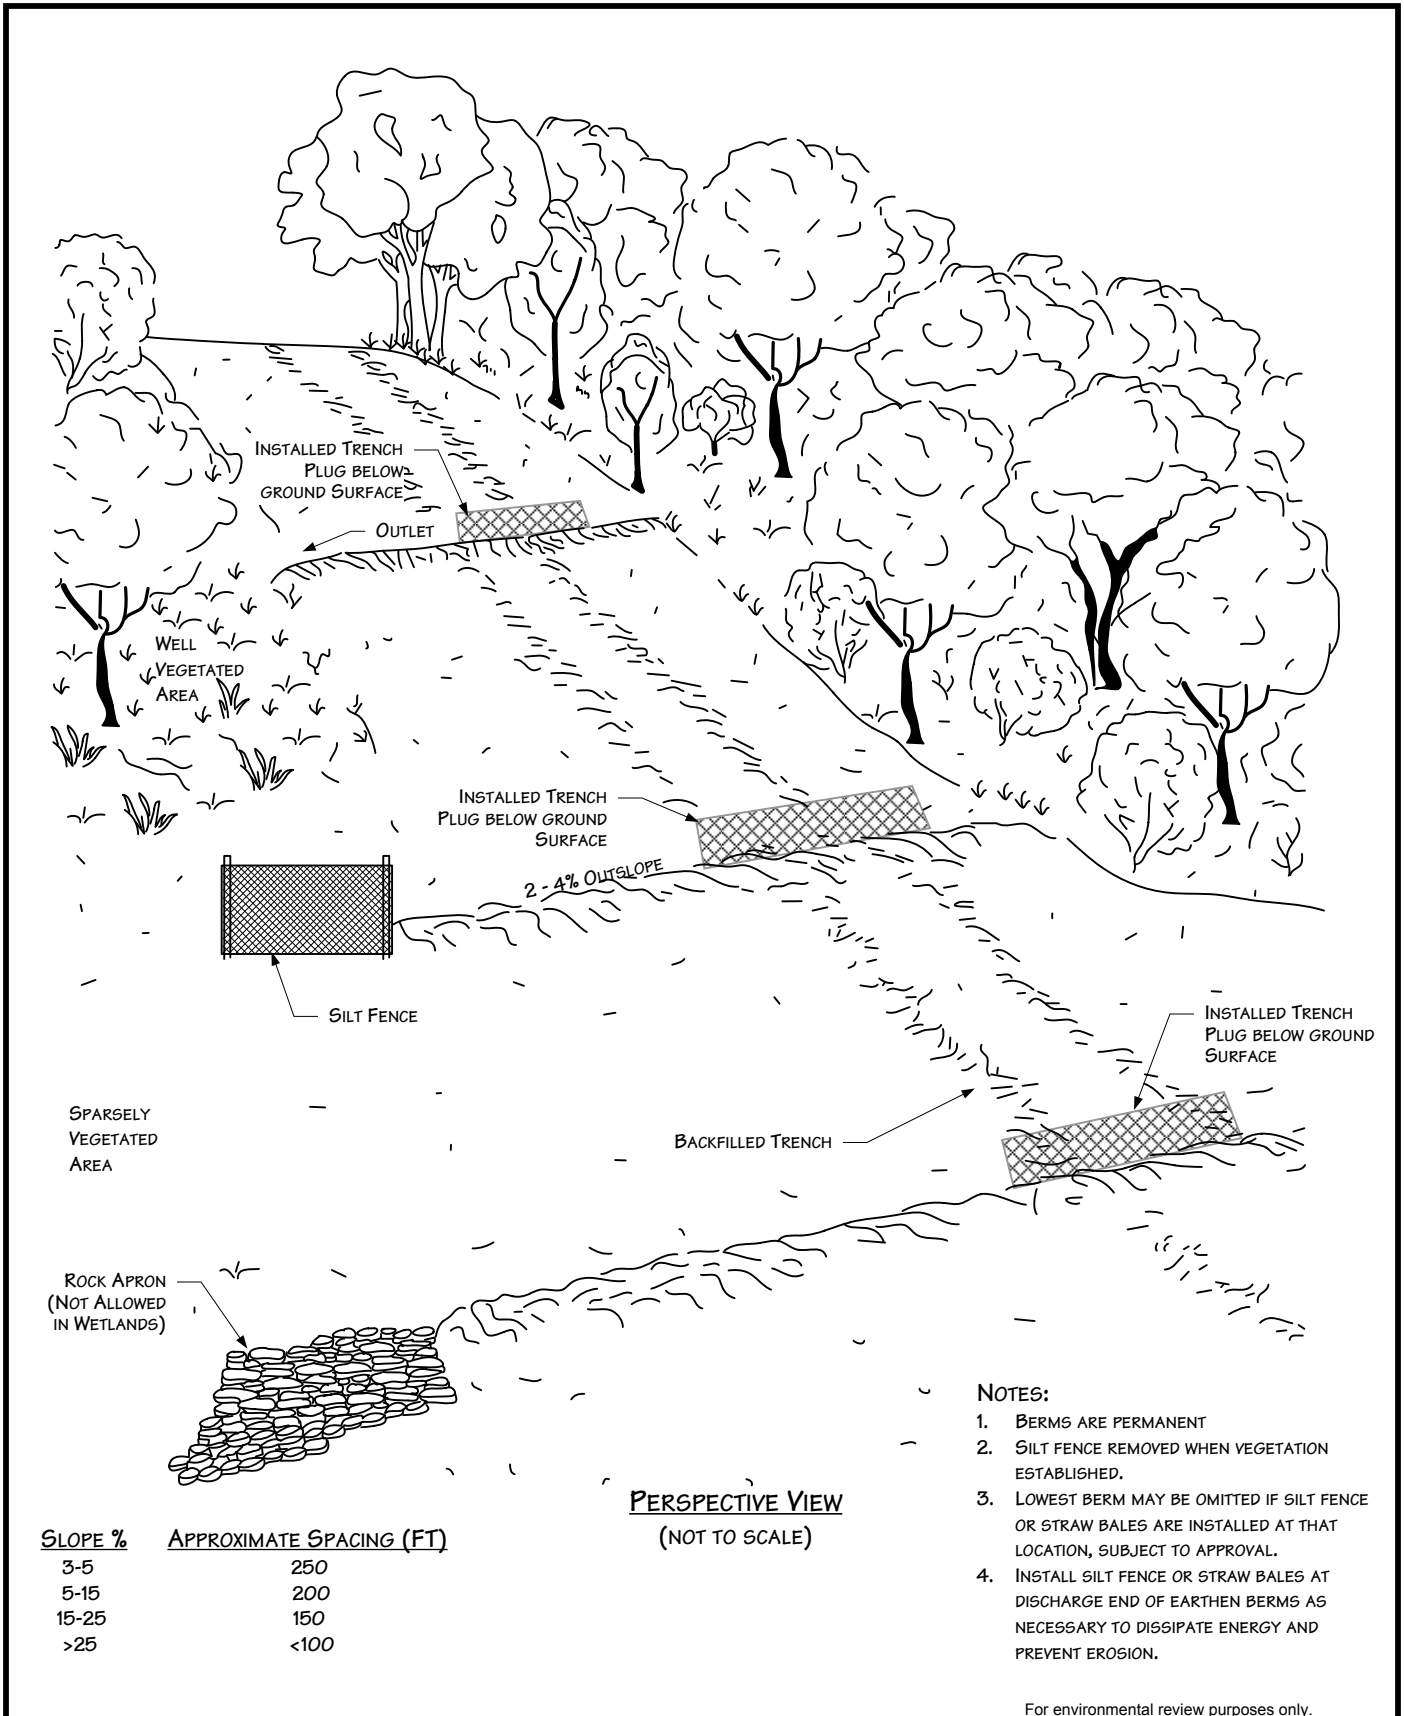

PERSPECTIVE VIEW
(NOT TO SCALE)

SLOPE %	APPROXIMATE SPACING (FT)
3-5	250
5-15	200
15-25	150
>25	<100

- NOTES:**
1. BERMS ARE PERMANENT
 2. SILT FENCE REMOVED WHEN VEGETATION ESTABLISHED.
 3. LOWEST BERM MAY BE OMITTED IF SILT FENCE OR STRAW BALES ARE INSTALLED AT THAT LOCATION, SUBJECT TO APPROVAL.
 4. INSTALL SILT FENCE OR STRAW BALES AT DISCHARGE END OF EARTHEN BERMS AS NECESSARY TO DISSIPATE ENERGY AND PREVENT EROSION.

For environmental review purposes only.




Figure 14
Environmental Protection Plan
Permanent Slope Breakers - Perspective View

DATE: 5/25/2001
 REVISED: 3/11/11
 SCALE: NTS
 DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG 14_SLOPE_BREAKERS_PERSPECTIVE_VIEW.VSD

NOTES:


1. No clearing until time of crossing. Only woody vegetation may be flush cut during initial clearing.
2. 50' ATWS setback from ordinary high water mark (OHWM) except in upland areas of cultivated or rotated cropland or other disturbed land.

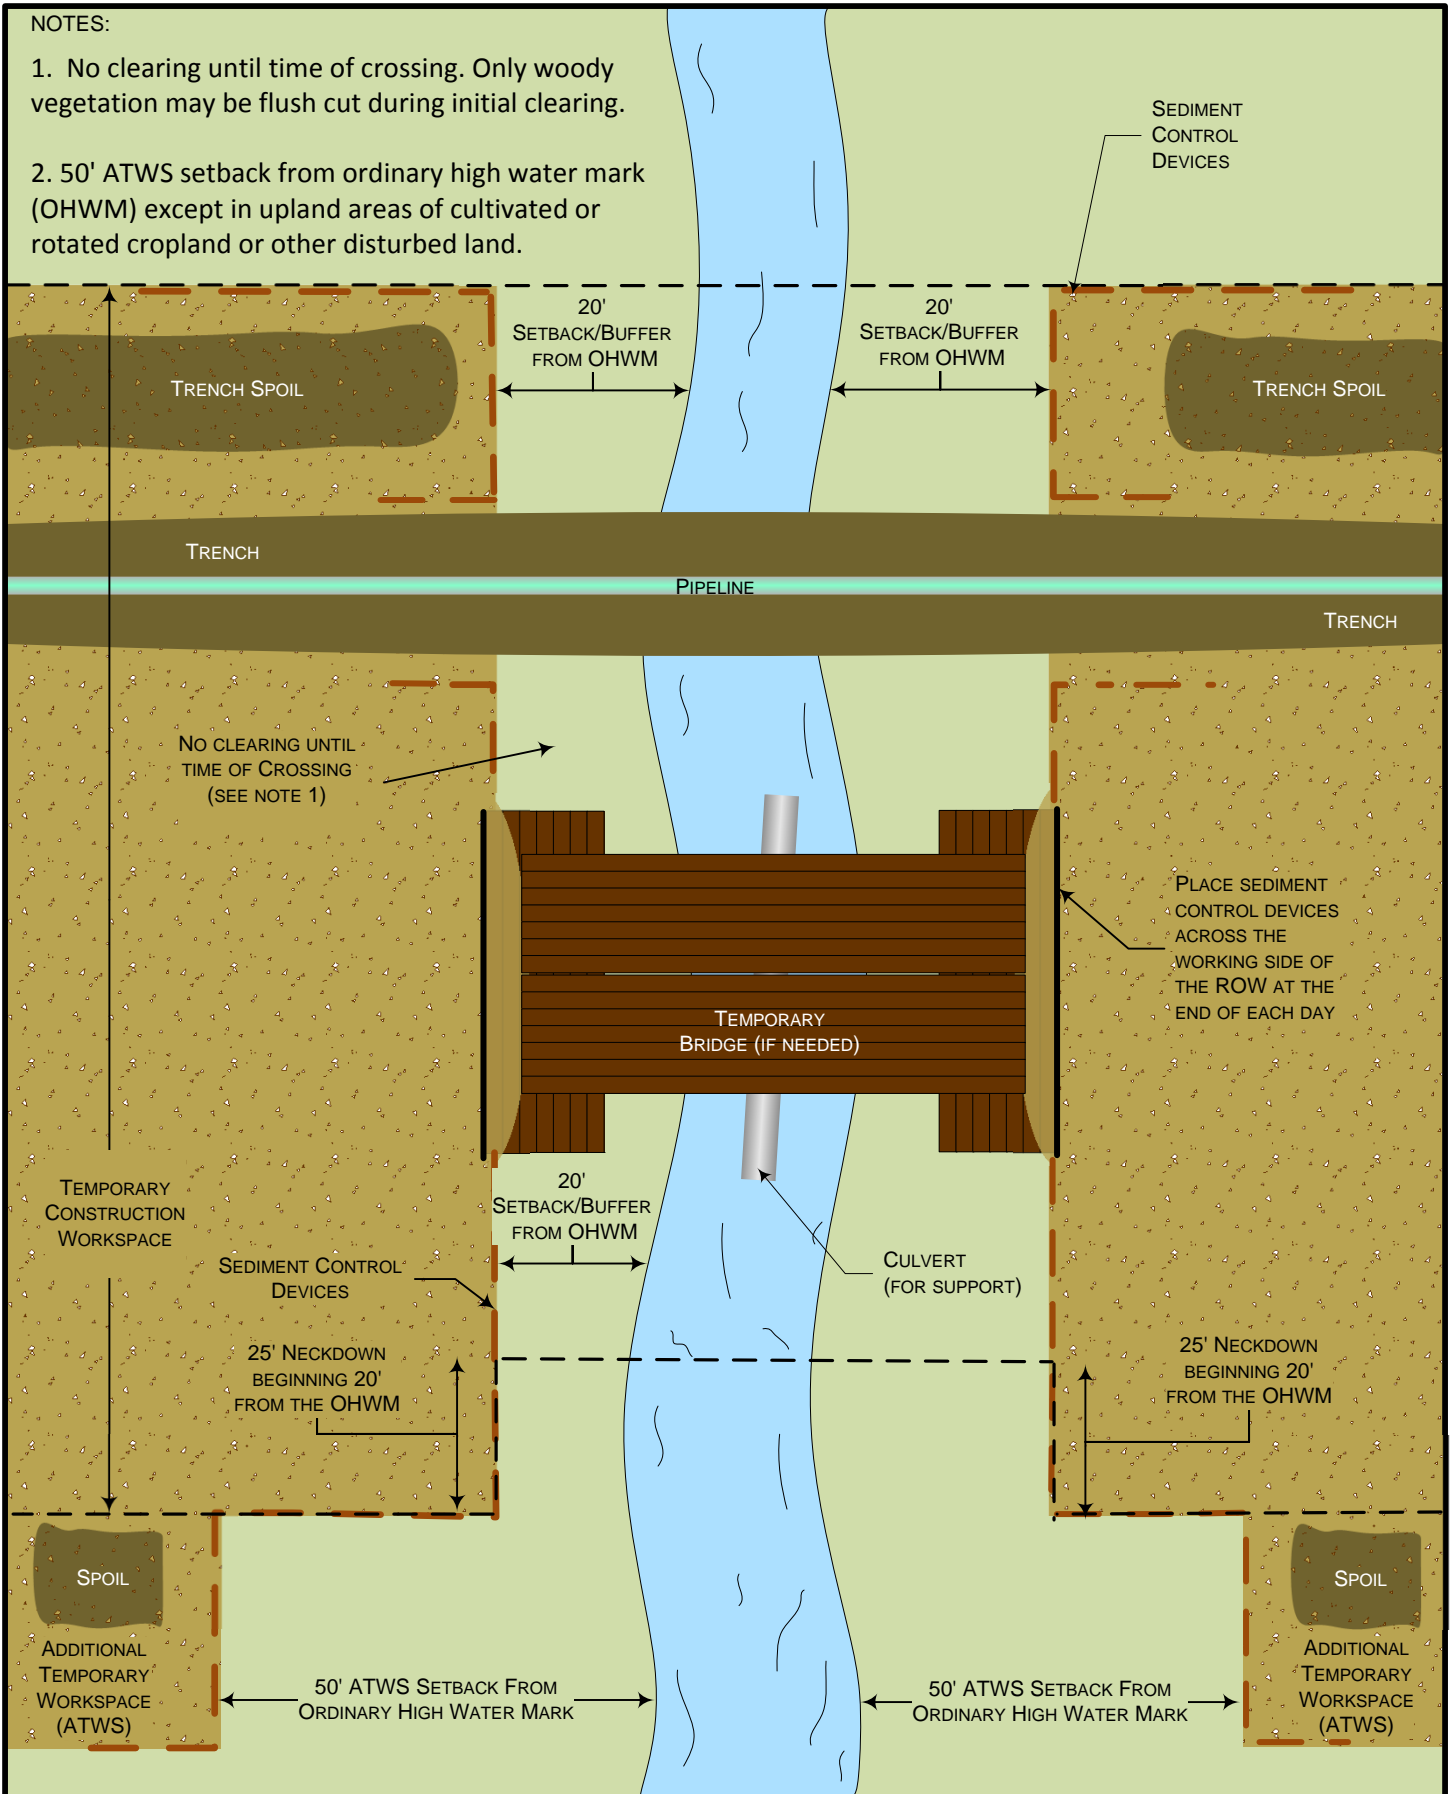

NOTES:


1. No clearing until time of crossing. Only woody vegetation may be flush cut during initial clearing.


2. 50' ATWS setback from ordinary high water mark (OHWM) except in upland areas of cultivated or rotated cropland or other disturbed land.

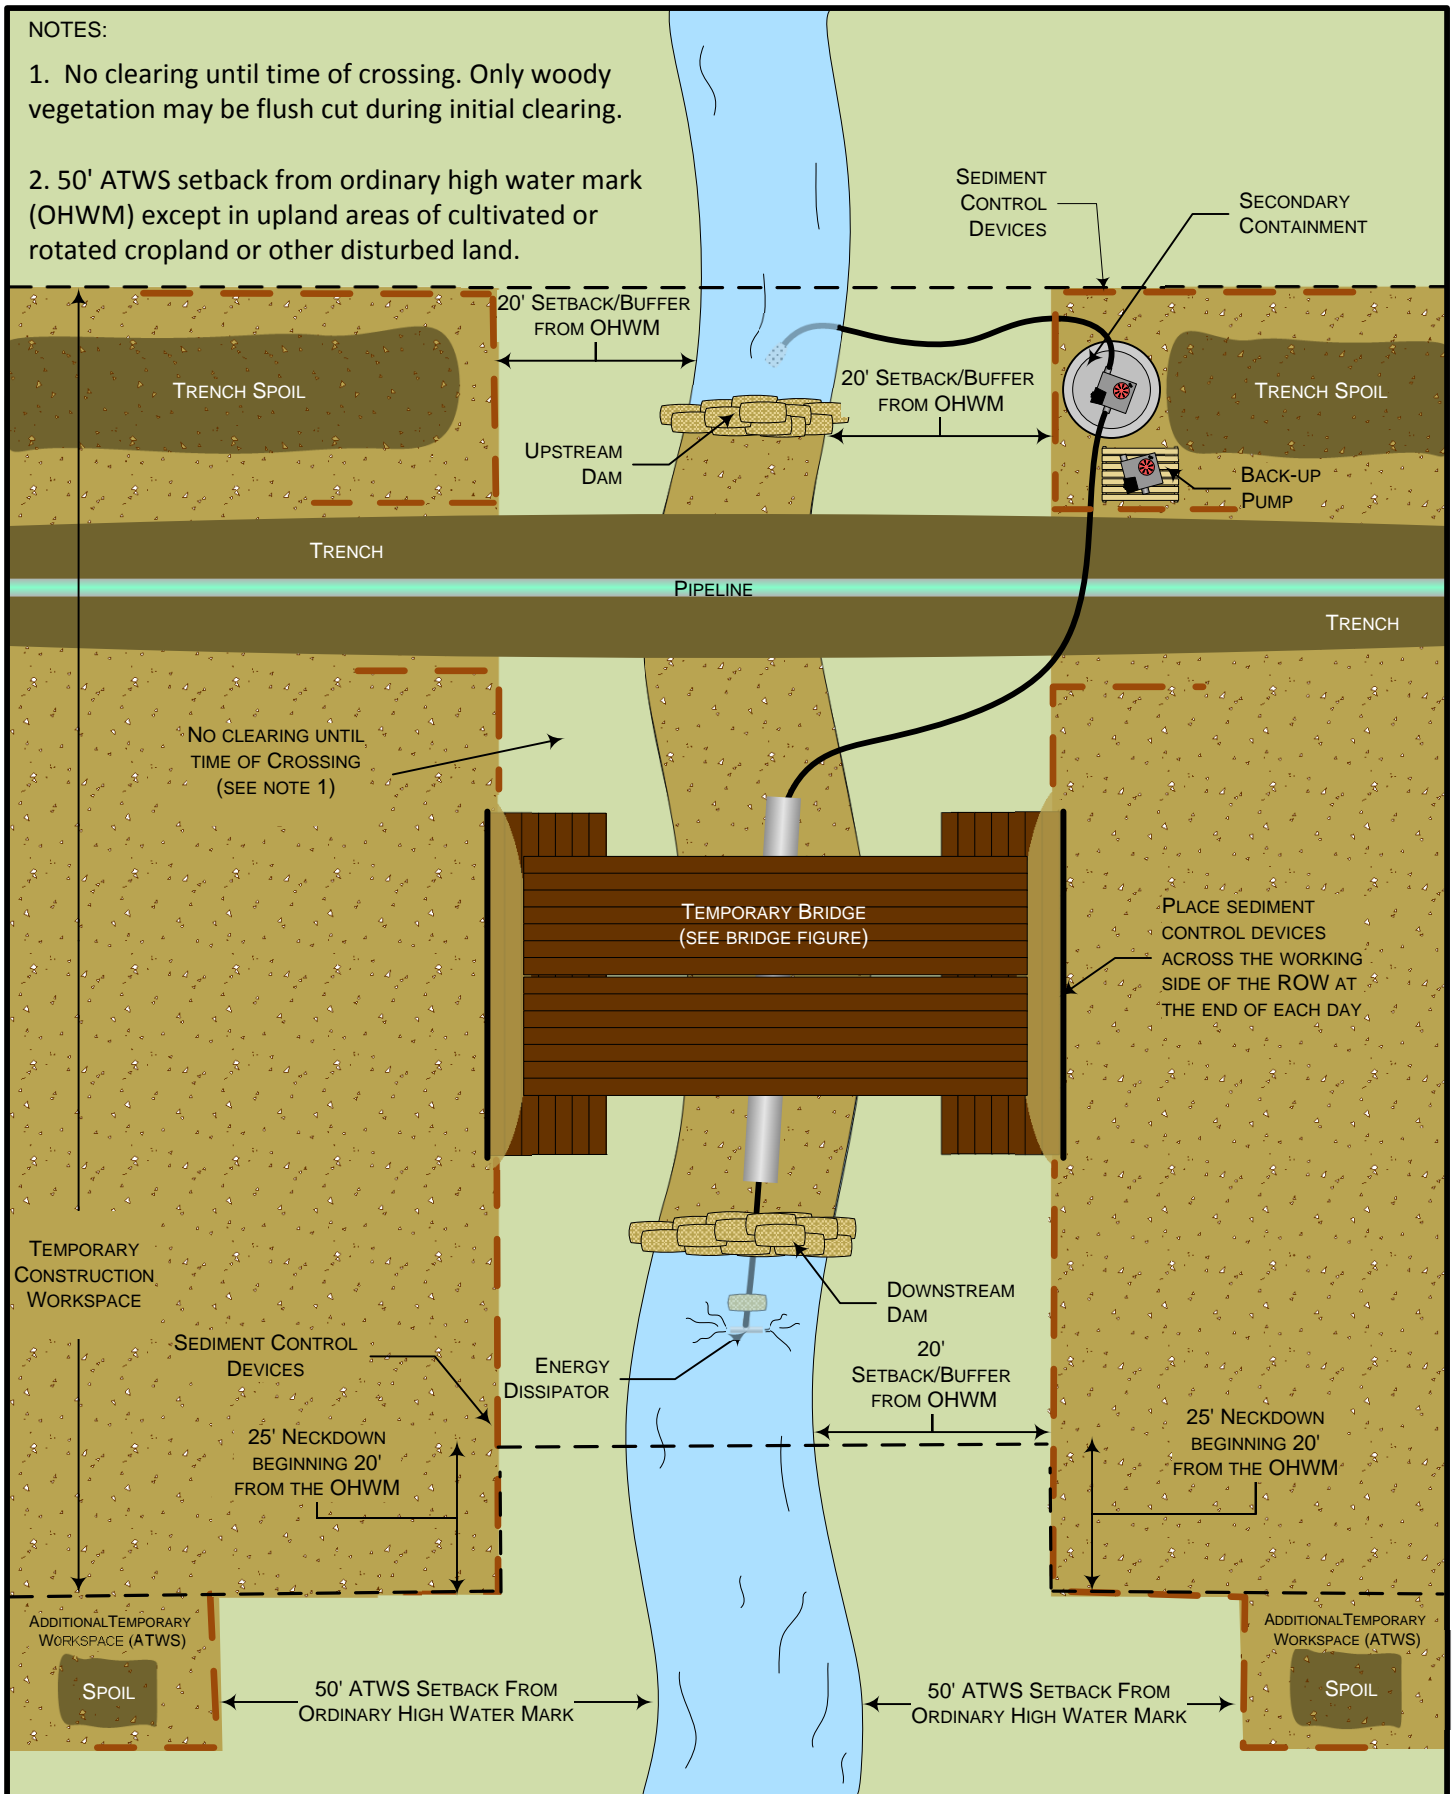

NOTES:

1. No clearing until time of crossing. Only woody vegetation may be flush cut during initial clearing.
2. 50' ATWS setback from ordinary high water mark (OHWM) except in upland areas of cultivated or rotated cropland or other disturbed land.

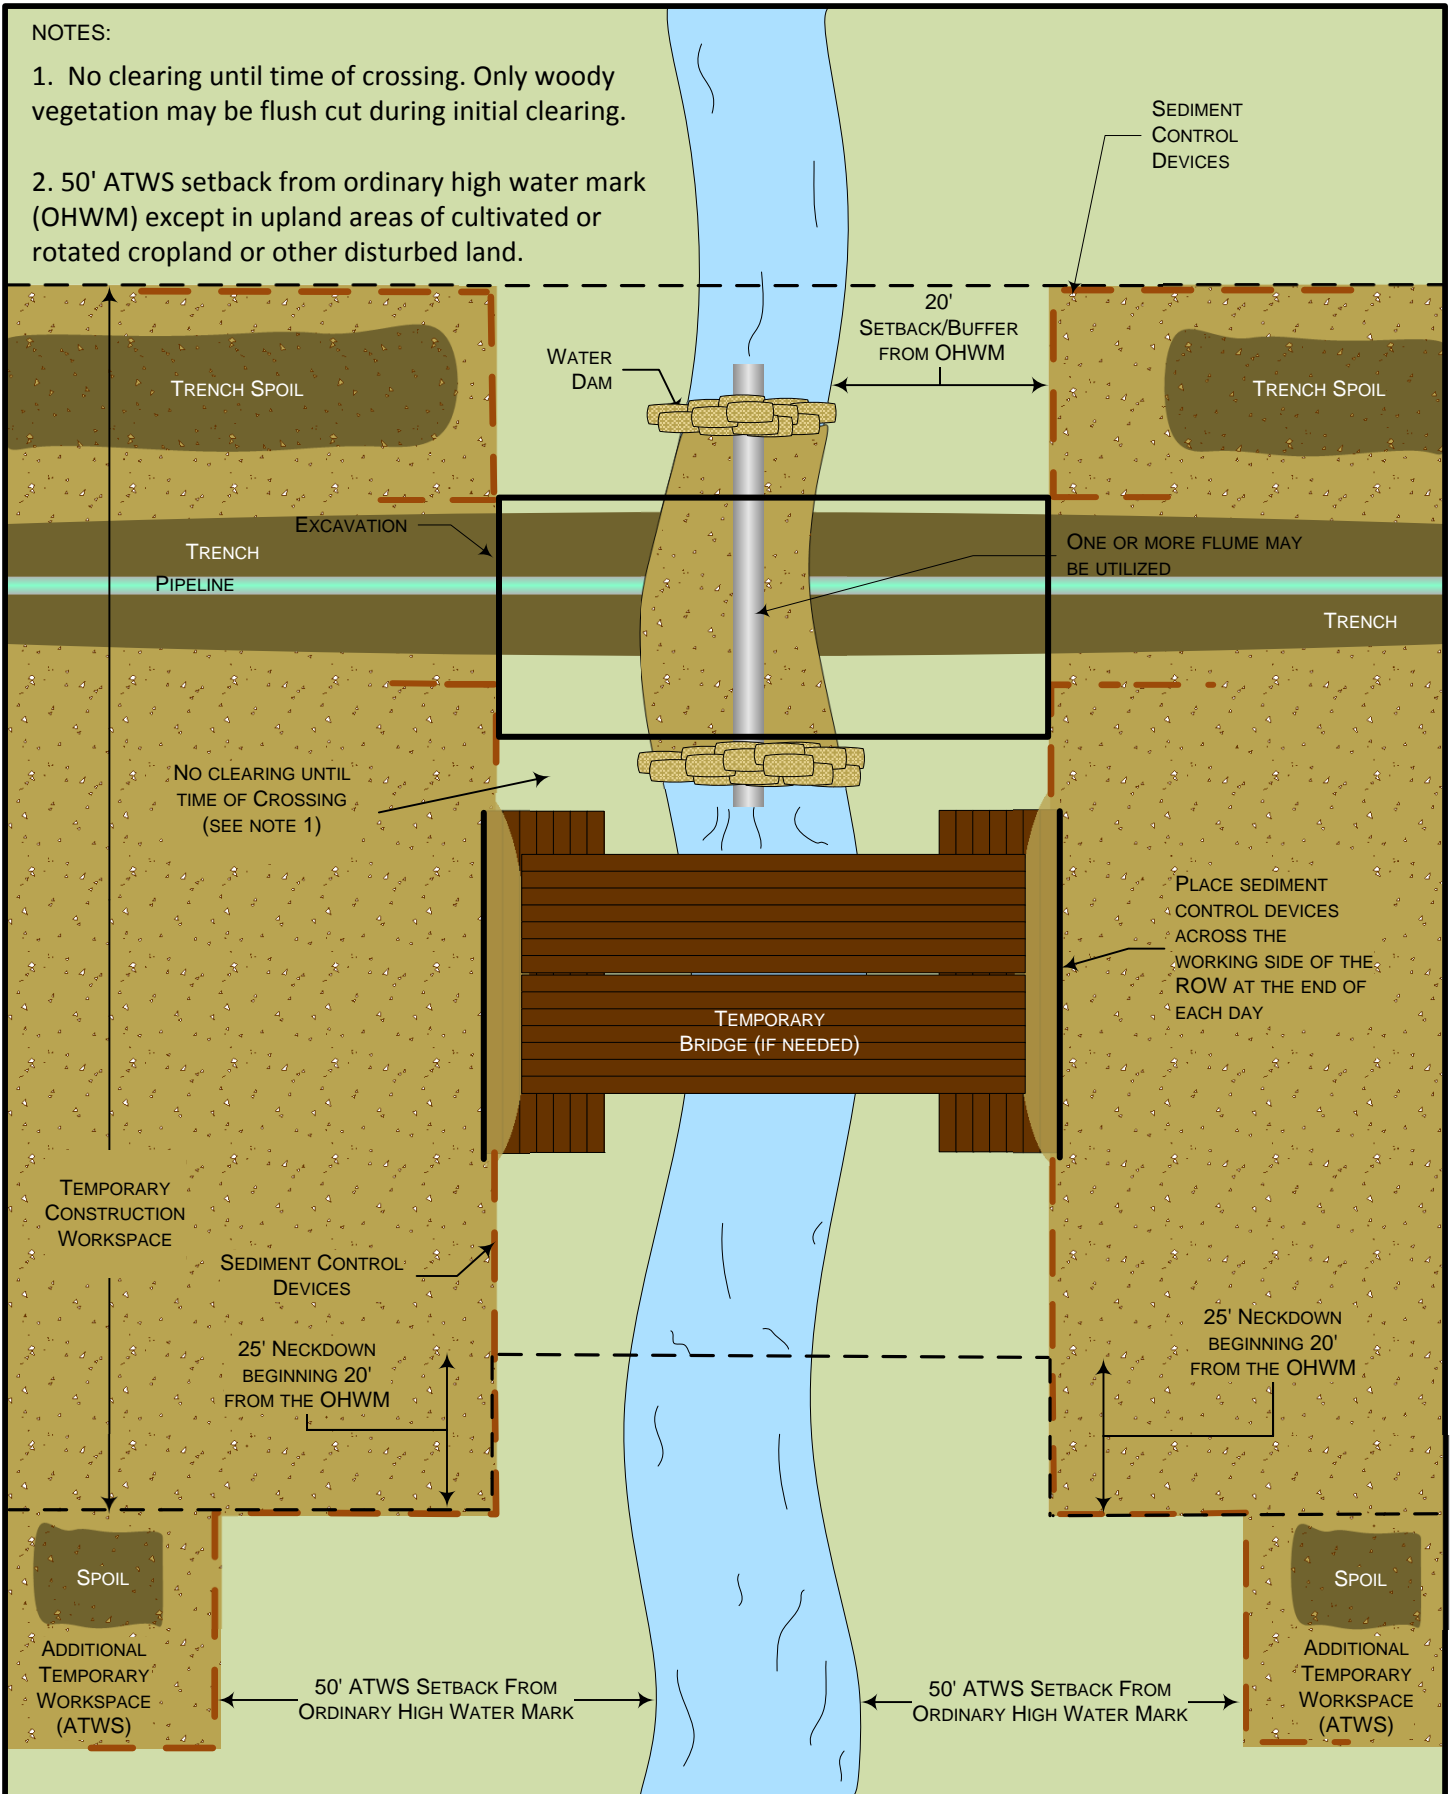

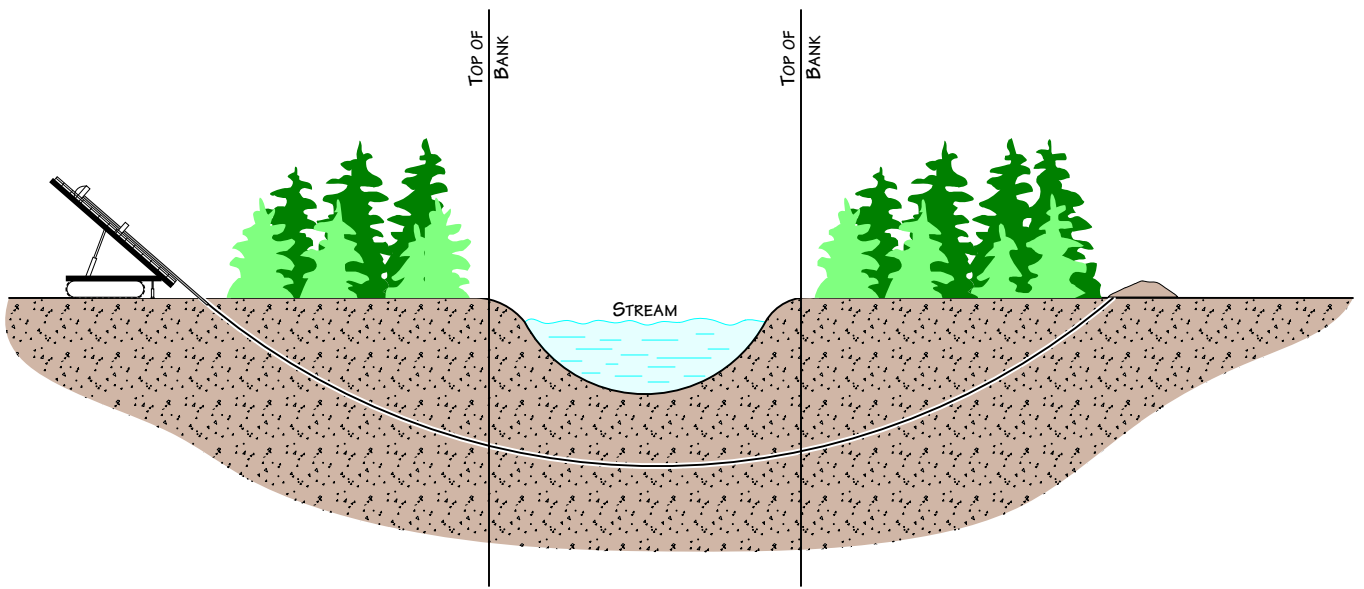

For environmental review purposes only.



Figure 18
Environmental Protection Plan
 Typical Waterbody Crossing
 Directional Drill Method

DATE: 7/14/2000


REVISED: 3/11/11

SCALE: NTS

DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG_18_WATERBODY_DIRECTIONAL_DRILL.VSD



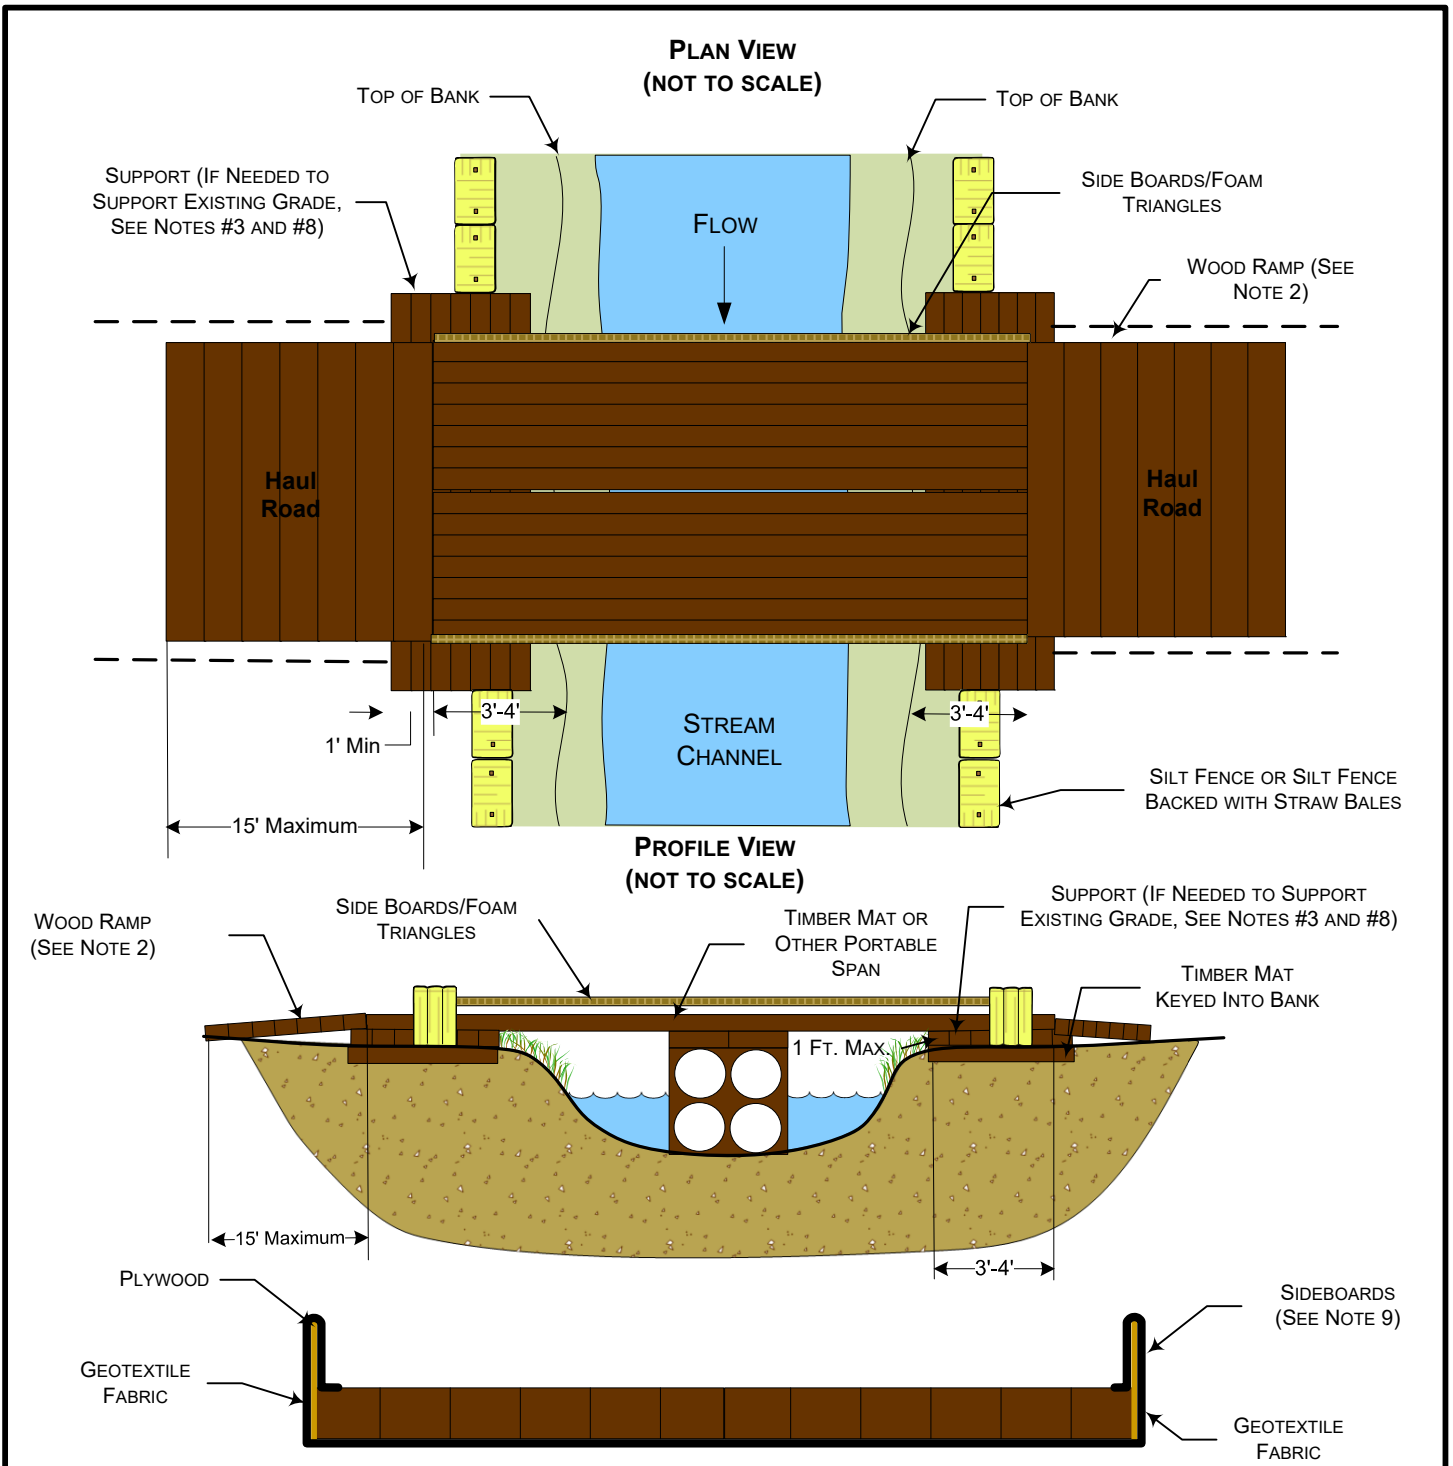

NOTES:


1. INSPECT BRIDGE OPENING PERIODICALLY AND FOLLOWING RAINFALLS OF OVER ½". REMOVE ANY DEBRIS RESTRICTING FLOW AND DEPOSIT IT AT AN UPLAND SITE OUTSIDE OF FLOODPLAIN.
2. IF PHYSICAL CIRCUMSTANCES PROHIBIT WOOD OR METAL RAMPS, EARTHEN RAMPS MAY BE USED AS APPROVED.
3. INSPECT BRIDGE ELEVATION SO BRIDGE REMAINS SUPPORTED ABOVE OHWM.
4. THE CULVERT SUPPORT MUST BE ANCHORED TO THE STREAM BOTTOM AND MAY NOT BE SUPPORTED WITH FILL.
5. EARTHEN RAMP CANNOT BE TALLER THAN 1' AND CANNOT EXTEND FOR MORE THAN 15' ON EITHER SIDE OF THE CROSSING.
6. THE BRIDGE MUST SPAN ABOVE OHWM TO OHWM.
7. ADDITIONAL SUPPORT MUST BE ADDED ON TOP OF BANK AND UNDER SPAN IF THE SPAN IS 12' WIDE OR GREATER, OR IF INITIAL SUPPORT STARTS TO SETTLE.
8. EROSION AND SEDIMENTATION CONTROL MEASURES SHALL BE INSPECTED AND MAINTAINED IN ACCORDANCE WITH THE COMPANY'S ENVIRONMENTAL PROTECTION PLAN.
9. SIDEBOARDS WILL BE INSTALLED ON TEMPORARY BRIDGES TO MINIMIZE THE POTENTIAL FOR SEDIMENT TRANSPORT. SIDEBOARDS MAY BE CONSTRUCTED OUT OF PLYWOOD, OR EQUIVALENT, AND AFFIXED TO THE OUTER SIDES OF THE BRIDGE. GEO-TEXTILE FABRIC, OR EQUIVALENT, MUST ALSO BE ADEQUATELY SECURED TO THE UNDERSIDE OF THE BRIDGE TO PREVENT MATERIAL FROM FALLING THROUGH THE BRIDGE DECK. THE GEO-TEXTILE FABRIC OR AN EQUIVALENT SHOULD BE SECURED TO THE BOTTOM OF THE BRIDGE AND WRAPPED AROUND THE SIDEBOARDS IN A CONTINUOUS FASHION.



Figure 19A
 Environmental Protection Plan
 Typical Span Type Bridge
 With or Without Instream Support (Flume Support)

Environmental Protection Plan

Drawn by: merjent

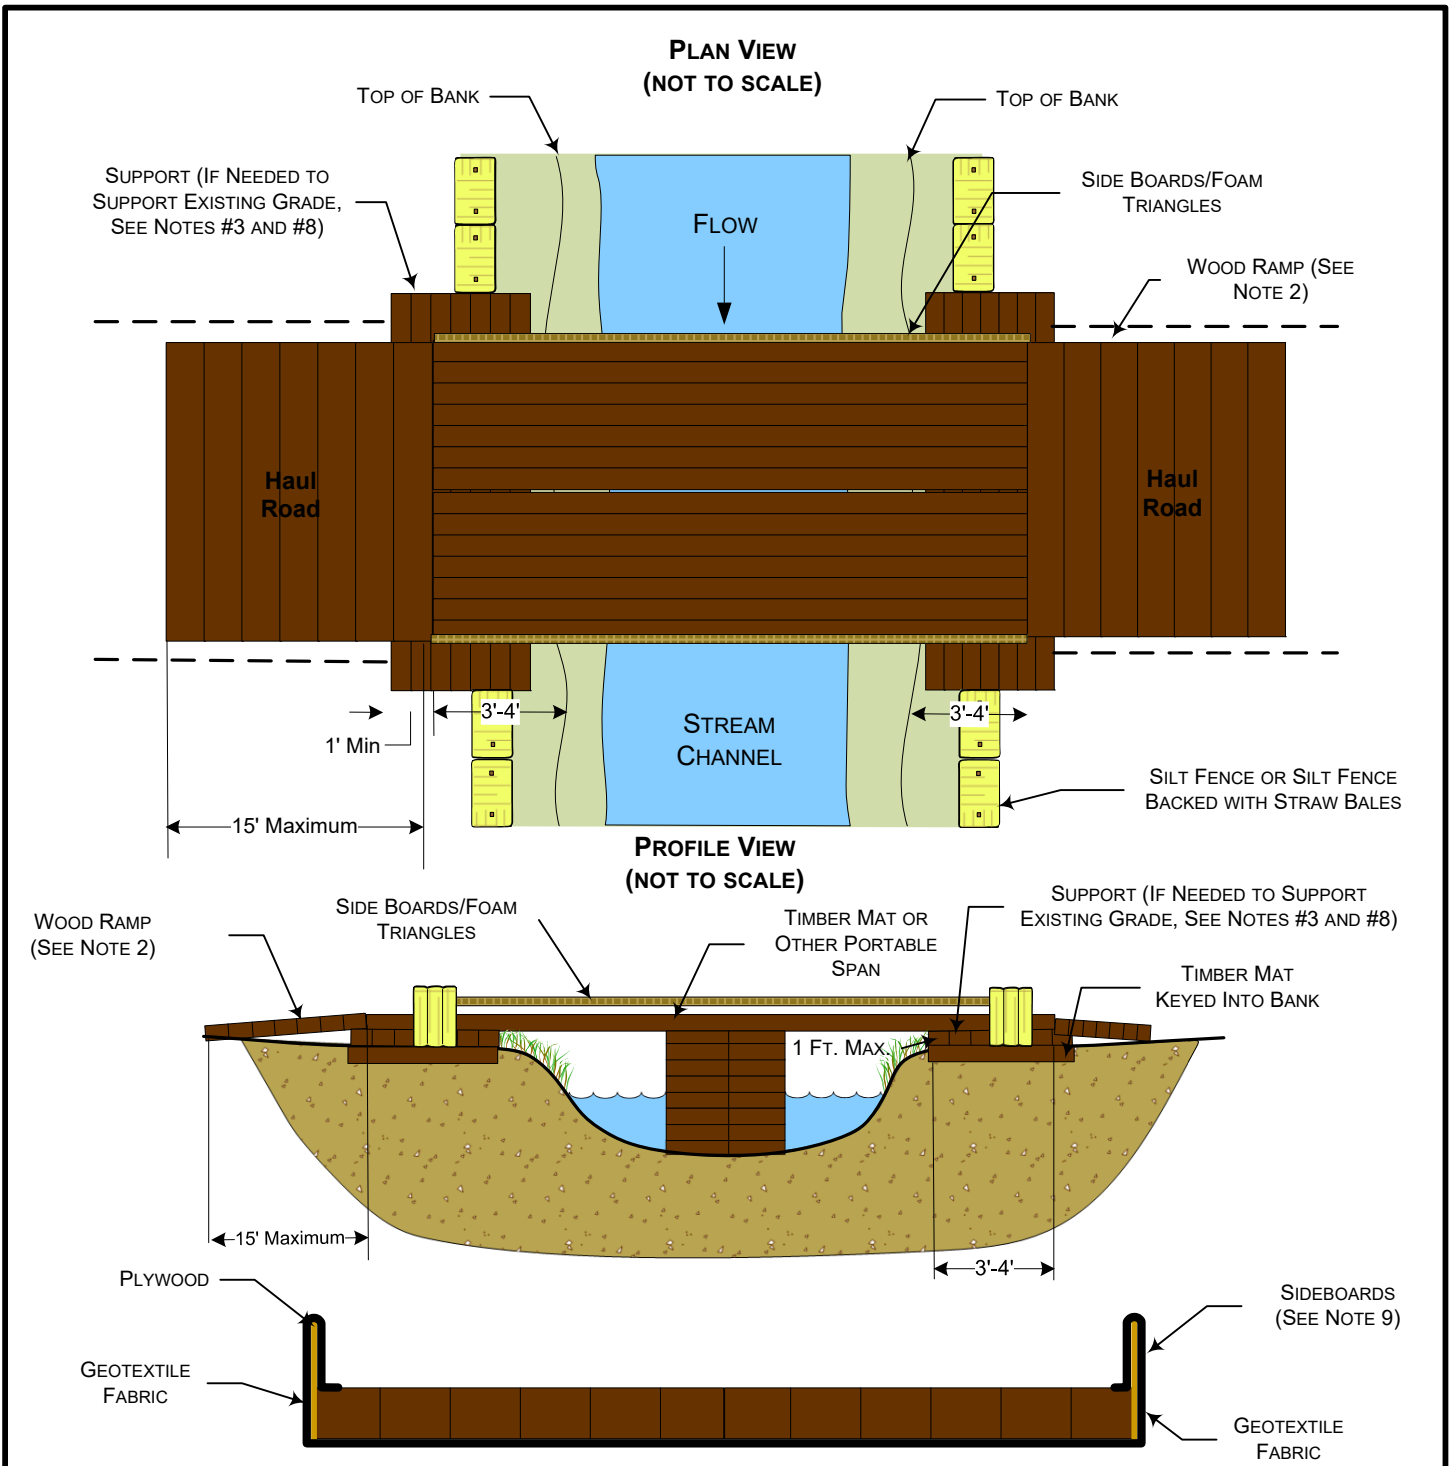

NOTES:



1. INSPECT BRIDGE OPENING PERIODICALLY AND FOLLOWING RAINFALLS OF OVER ½". REMOVE ANY DEBRIS RESTRICTING FLOW AND DEPOSIT IT AT AN UPLAND SITE OUTSIDE OF FLOODPLAIN.
2. IF PHYSICAL CIRCUMSTANCES PROHIBIT WOOD OR METAL RAMPS, EARTHEN RAMPS MAY BE USED AS APPROVED.
3. INSPECT BRIDGE ELEVATION SO BRIDGE REMAINS SUPPORTED ABOVE OHWM.
4. THE CULVERT SUPPORT MUST BE ANCHORED TO THE STREAM BOTTOM AND MAY NOT BE SUPPORTED WITH FILL.
5. EARTHEN RAMP CANNOT BE TALLER THAN 1' AND CANNOT EXTEND FOR MORE THAN 15' ON EITHER SIDE OF THE CROSSING.
6. THE BRIDGE MUST SPAN ABOVE OHWM TO OHWM.
7. ADDITIONAL SUPPORT MUST BE ADDED ON TOP OF BANK AND UNDER SPAN IF THE SPAN IS 12' WIDE OR GREATER, OR IF INITIAL SUPPORT STARTS TO SETTLE.
8. EROSION AND SEDIMENTATION CONTROL MEASURES SHALL BE INSPECTED AND MAINTAINED IN ACCORDANCE WITH THE COMPANY'S ENVIRONMENTAL PROTECTION PLAN.
9. SIDEBOARDS WILL BE INSTALLED ON TEMPORARY BRIDGES TO MINIMIZE THE POTENTIAL FOR SEDIMENT TRANSPORT. SIDEBOARDS MAY BE CONSTRUCTED OUT OF PLYWOOD, OR EQUIVALENT, AND AFFIXED TO THE OUTER SIDES OF THE BRIDGE. GEO-TEXTILE FABRIC, OR EQUIVALENT, MUST ALSO BE ADEQUATELY SECURED TO THE UNDERSIDE OF THE BRIDGE TO PREVENT MATERIAL FROM FALLING THROUGH THE BRIDGE DECK. THE GEO-TEXTILE FABRIC OR AN EQUIVALENT SHOULD BE SECURED TO THE BOTTOM OF THE BRIDGE AND WRAPPED AROUND THE SIDEBOARDS IN A CONTINUOUS FASHION.



Figure 19B
 Environmental Protection Plan
 Typical Span Type Bridge
 With or Without Instream Support (Timber Matted Support)

Environmental Protection Plan

Drawn by: merjent

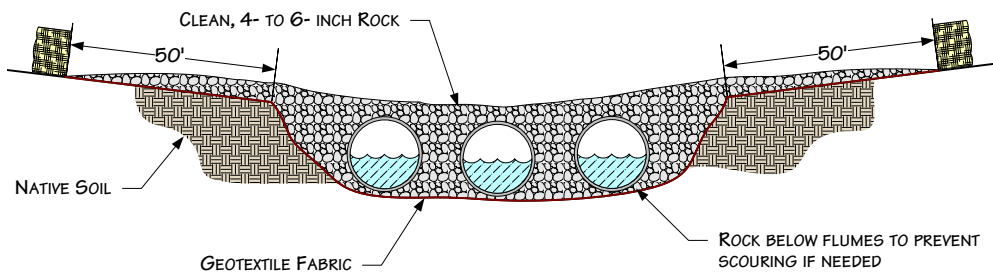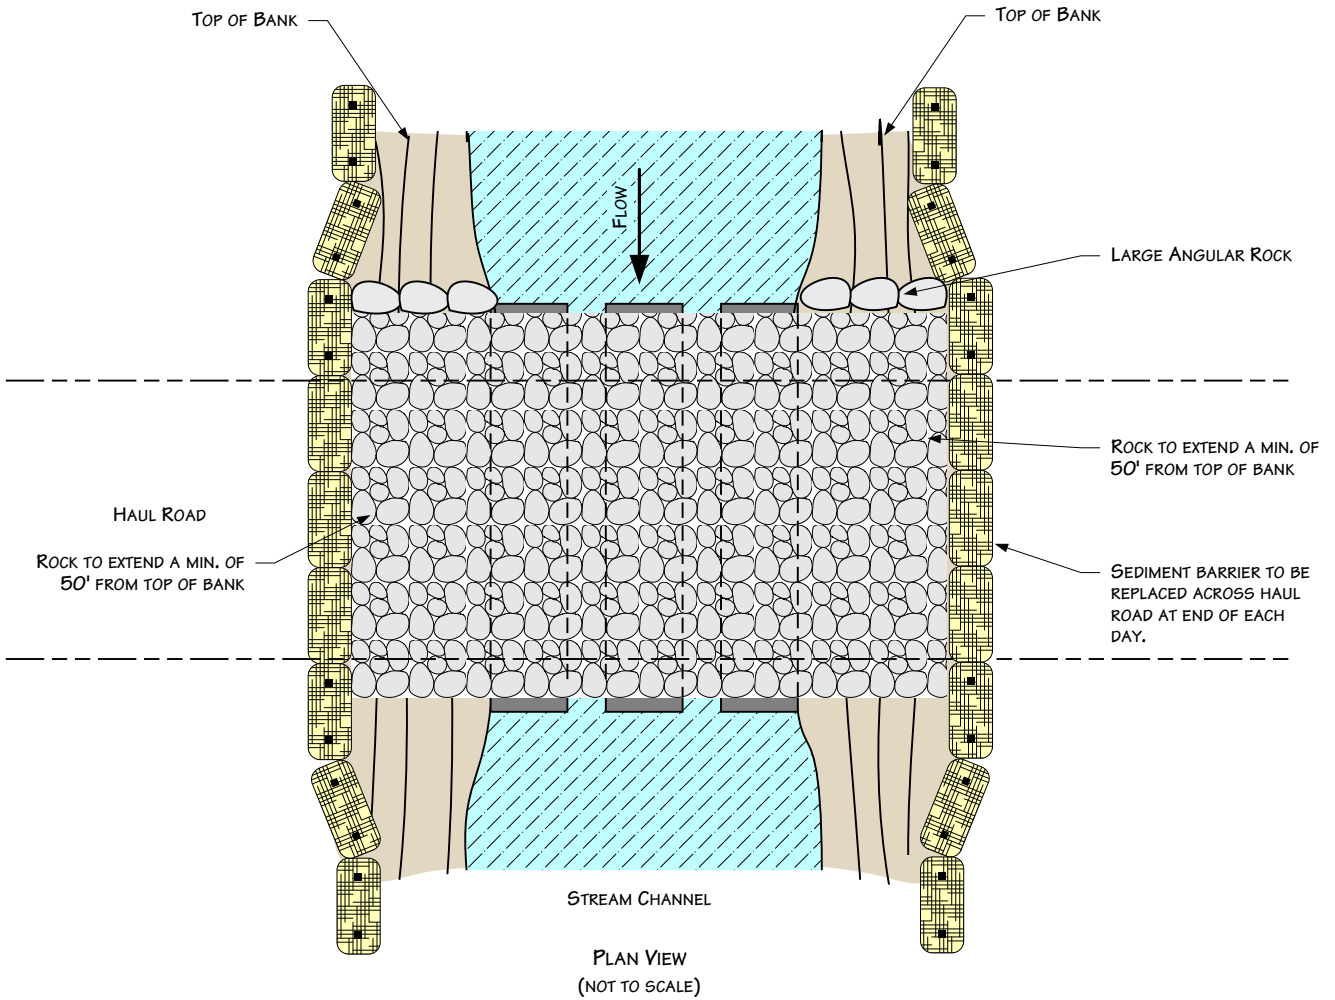

NOTES:

1. STEEL FLUME PIPE(S) SIZED TO ALLOW FOR STREAM FLOW AND EQUIPMENT LOAD.
2. STRAW BALES SHALL BE PLACED ACROSS BRIDGE ENTRANCE EVERY NIGHT.
3. ADDITIONAL INFORMATION INCLUDED ON OTHER DRAWINGS.

For environmental review purposes only.



Figure 20
Environmental Protection Plan
Typical Rock Flume Bridge

DATE: 5/25/2001

REVISED: 3/15/11

SCALE: NTS

DRAWN BY: KMKENDALL


K:\CLIENT PROJECTS\ID-PEEL\2011-019\FIG_20_ROCK_FLUME_BRIDGE.VSD




DEWATERING DISCHARGE IN WELL VEGETATED UPLANDS

NOTES:

1. PUMP INTAKE HOSE MUST BE SECURED AT LEAST ONE FOOT ABOVE THE TRENCH BOTTOM.
2. DEWATER INTO GEOTEXTILE FILTER BAG OR STRAW BALE DEWATERING STRUCTURE.

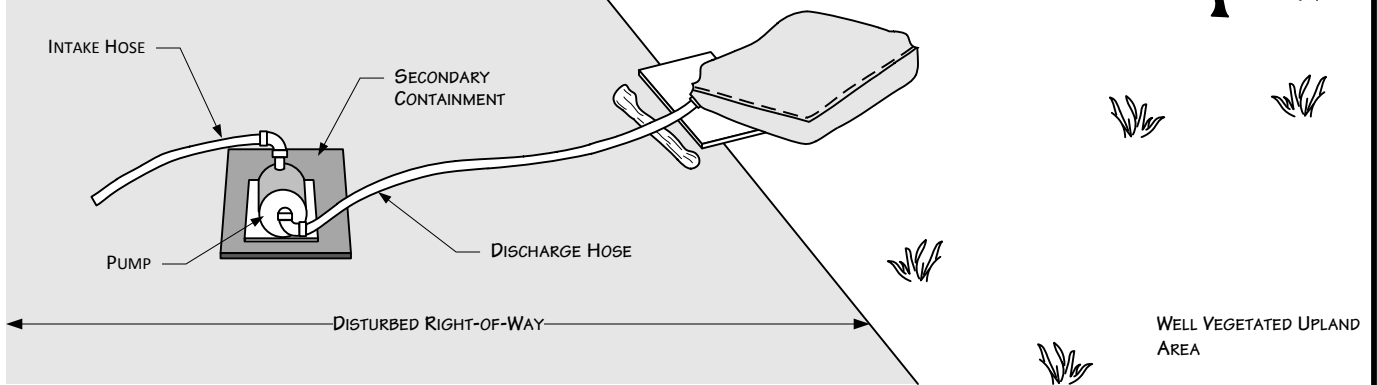

GEOTEXTILE FILTER BAG

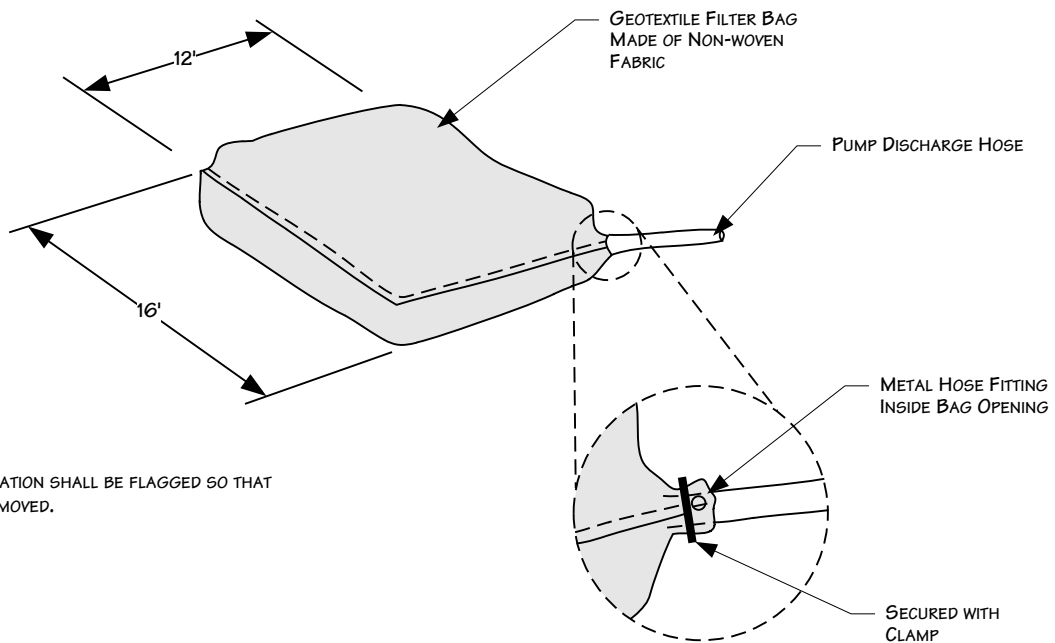

NOTE:

1. FILTER BAG LOCATION SHALL BE FLAGGED SO THAT BAG CAN BE REMOVED.

For environmental review purposes only.



Figure 21
Environmental Protection Plan
Typical Dewatering Measures

DATE: 5/25/2001


REVISED: 3/15/11

SCALE: NTS

DRAWN BY: KMKENDALL


K:\CLIENT_PROJECTS\SD-FEEL\2011-019\FIG_21_DEWATERING_MEASURES.VSD



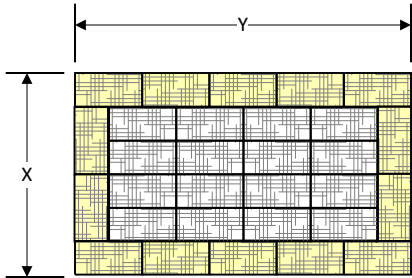


NOTES


1. ARRANGE THE STRAW BALES TO THE X AND Y DIMENSIONS AS SPECIFIED BELOW.
2. IF BOTTOM OF STRUCTURE IS NOT LINED WITH STRAW BALES (OPTION 1), LINE ENTIRE STRUCTURE WITH GEOTEXTILE FILTER FABRIC.

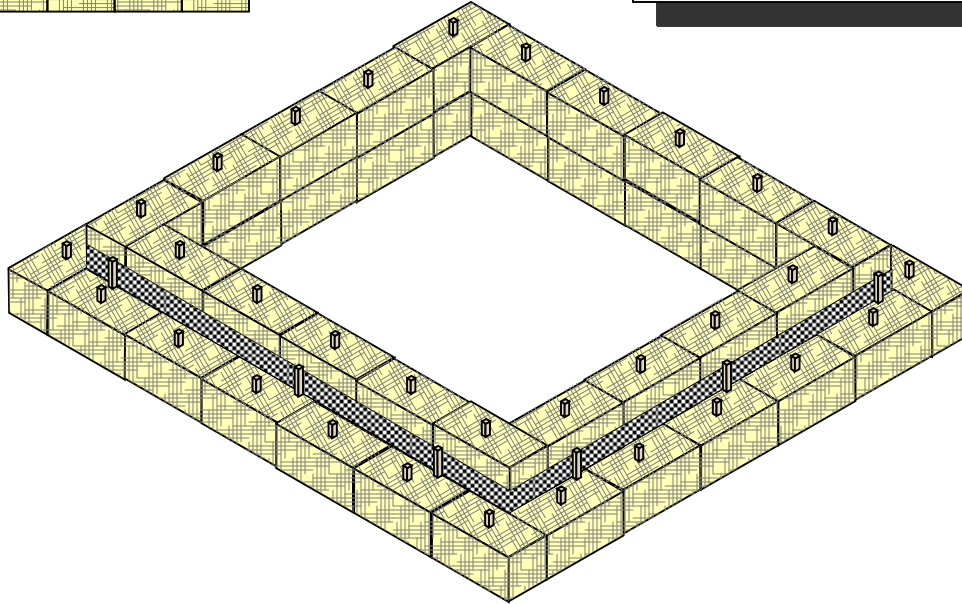

PERSPECTIVE VIEW

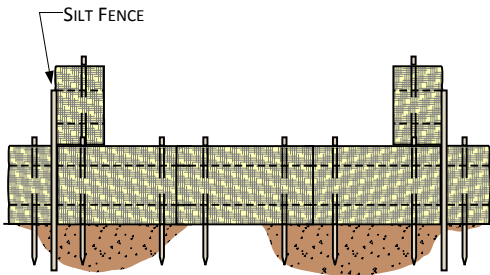

OPTION 1

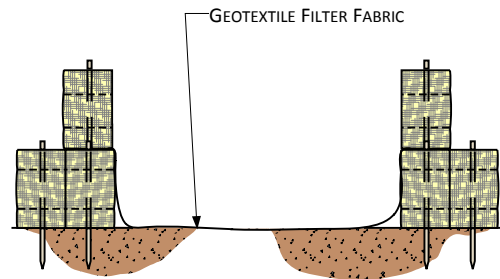

OPTION 2


TYPICAL MINIMUM SUMP DIMENSIONS (FEET)		MAXIMUM PUMPING RATE GALLONS PER MINUTE
X	Y	
10	20	300
15	20	350
20	20	400
20	25	450
25	25	500
25	30	550
30	30	660

For environmental review purposes only.



Figure 22A
Environmental Protection Plan
Straw Bale Dewatering Structure



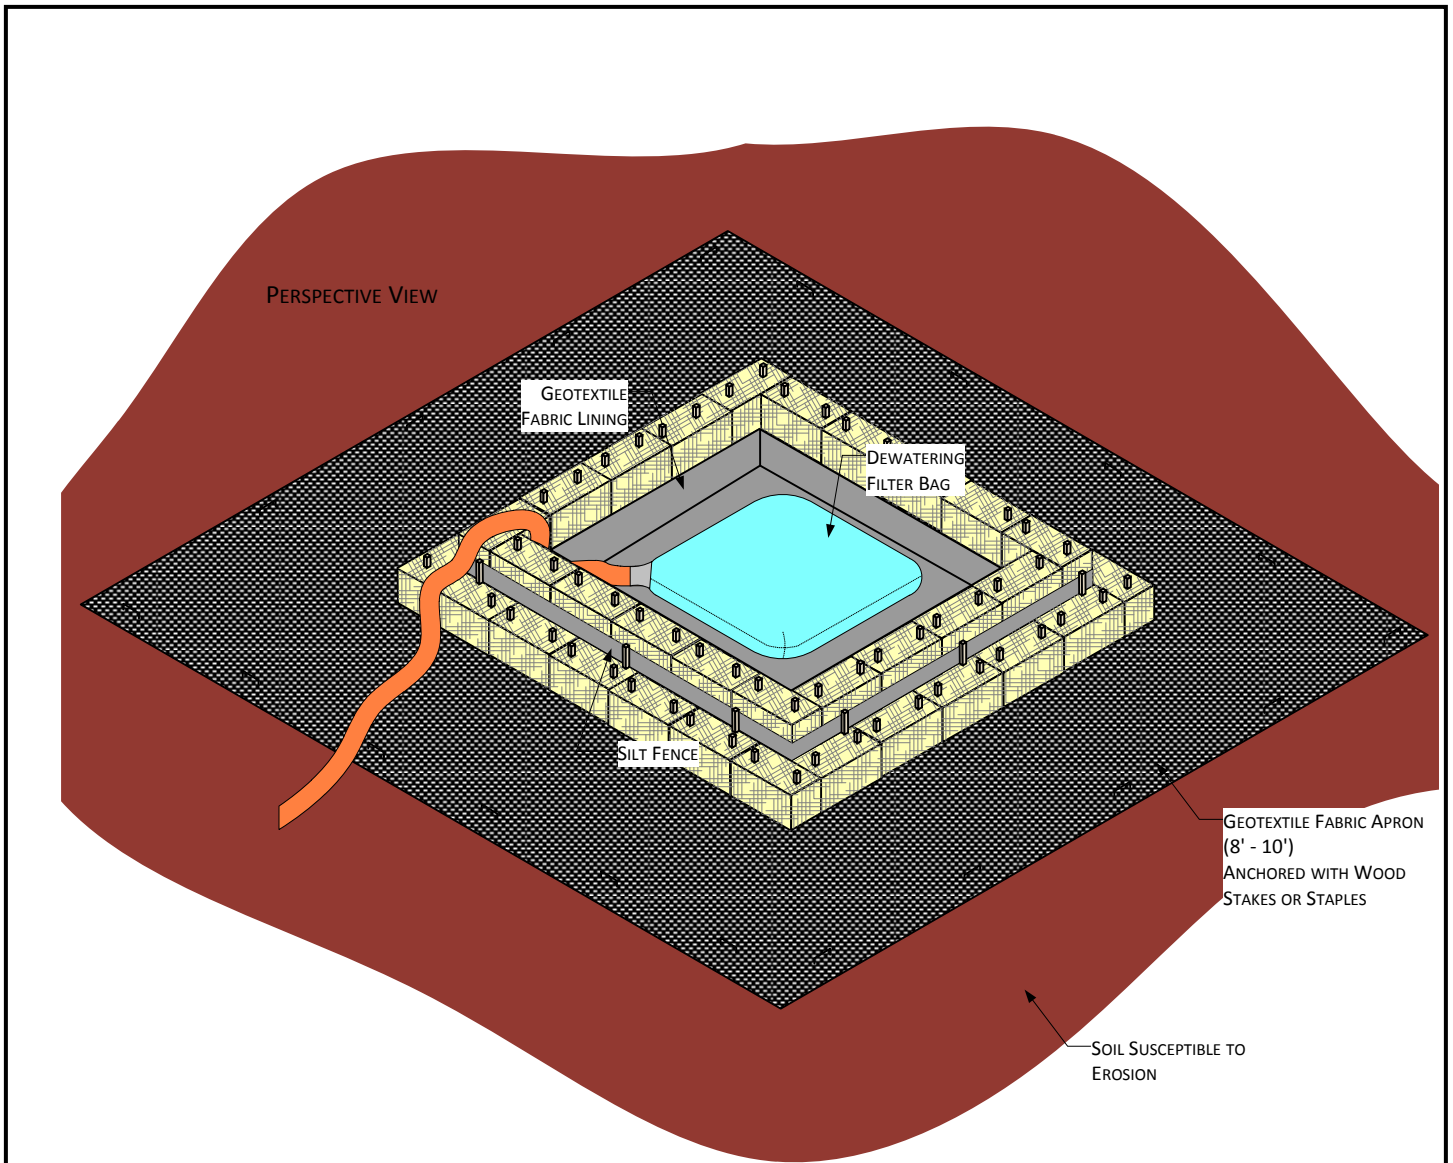

CONSTRUCT DEWATERING STRUCTURE TO ACCOMMODATE ANTICIPATED PUMPING RATES. SEE EXAMPLE BELOW.

EXAMPLE PUMPING RATE = 200 G.P.M.

STORAGE VOLUME (C.F.) = 16 X 200 G.P.M. = 3200 C.F.

HEIGHT OF STRAW BALE STRUCTURE = 3 FEET (2 BALES STACKED) (BASED ON HEIGHT OF BALES, NOT SILT FENCE)

INSIDE DIMENSIONS OF STRUCTURE = 33 X 33 FEET SQUARE

NOTES:




1. SILT FENCE ENDS MUST BE WRAPPED TO JOIN TWO SECTIONS.
2. INSTALL SILT FENCE 2 INCHES ABOVE TOP OF STRAW BALES, AND ANCHOR A MINIMUM OF 8 INCHES STRAIGHT DOWN.
3. SILT FENCE POST STAKING MUST BE 4 FEET OR LESS.
4. DEWATERING INTAKE HOSE SUPPORTED AT LEAST 1 FOOT FROM BOTTOM OF TRENCH BEING DEWATERED.
5. EROSION AND SEDIMENTATION CONTROL MEASURES SHALL BE INSPECTED AND MAINTAINED IN ACCORDANCE WITH THE COMPANY'S UPLAND EROSION CONTROL, REVEGETATION, AND MAINTENANCE PLAN.

For environmental review purposes only.

Figure 22B
Environmental Protection Plan
Straw Bale Dewatering Structure



PERSPECTIVE VIEW

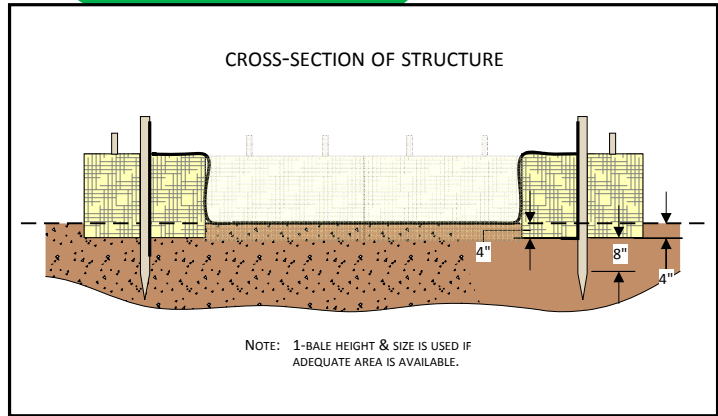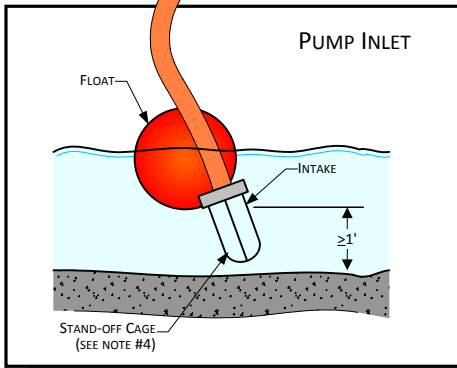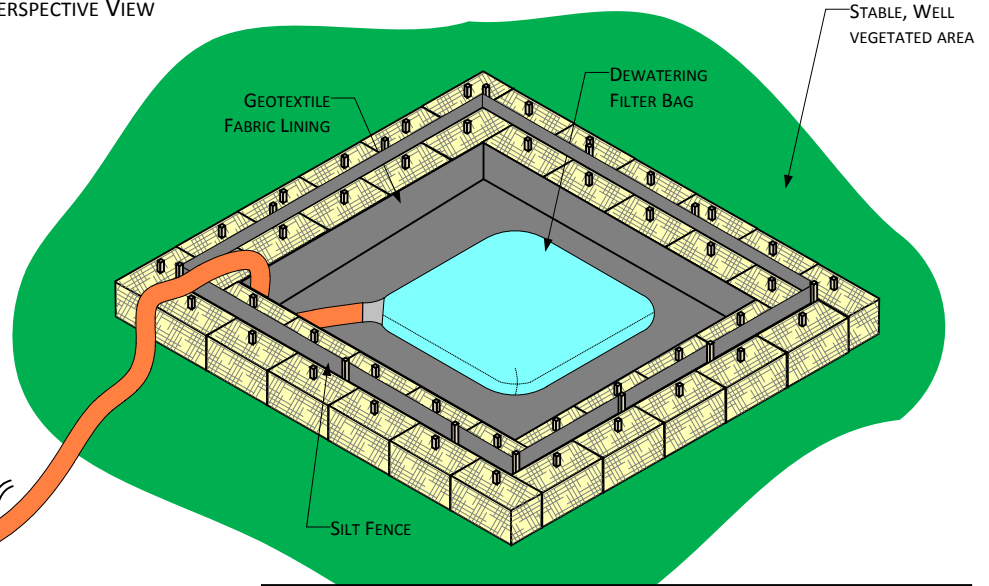

CONSTRUCT DEWATERING STRUCTURE TO ACCOMMODATE ANTICIPATED PUMPING RATES. SEE EXAMPLE BELOW.

EXAMPLE PUMPING RATE = 200 G.P.M.
 STORAGE VOLUME (C.F.) = 16 x 200 G.P.M. = 3200 C.F.
 HEIGHT OF STRAW BALE STRUCTURE = 1.5 FEET (1 BALE) (BASED ON HEIGHT OF BALES, NOT SILT FENCE)
 INSIDE DIMENSIONS OF STRUCTURE = 46 x 46 FEET SQUARE

NOTES:

1. SILT FENCE ENDS MUST BE WRAPPED TO JOIN TWO SECTIONS.
2. INSTALL SILT FENCE 2 INCHES ABOVE TOP OF STRAW BALE, AND ANCHOR A MINIMUM OF 8 INCHES STRAIGHT DOWN.
3. SILT FENCE POST STAKING MUST BE 4 FEET OR LESS.
4. DEWATERING INTAKE HOSE SUPPORTED AT LEAST 1 FOOT FROM BOTTOM OF TRENCH BEING DEWATERED.
5. USE A FILTER BAG AT THE DISCHARGE HOSE END.
6. EROSION AND SEDIMENTATION CONTROL MEASURES SHALL BE INSPECTED AND MAINTAINED IN ACCORDANCE WITH THE COMPANY'S UPLAND EROSION CONTROL, REVEGETATION, AND MAINTENANCE PLAN.


For environmental review purposes only.



Figure 22C
Environmental Protection Plan
Straw Bale Dewatering Structure



NOTE: PLACE JUTE BLANKET A MINIMUM OF ONE (1) FOOT UNDER RIP RAP. EXTEND JUTE BLANKET FROM MEAN HIGH WATER LEVEL TO SEVERAL FEET BEHIND HIGH BANK.

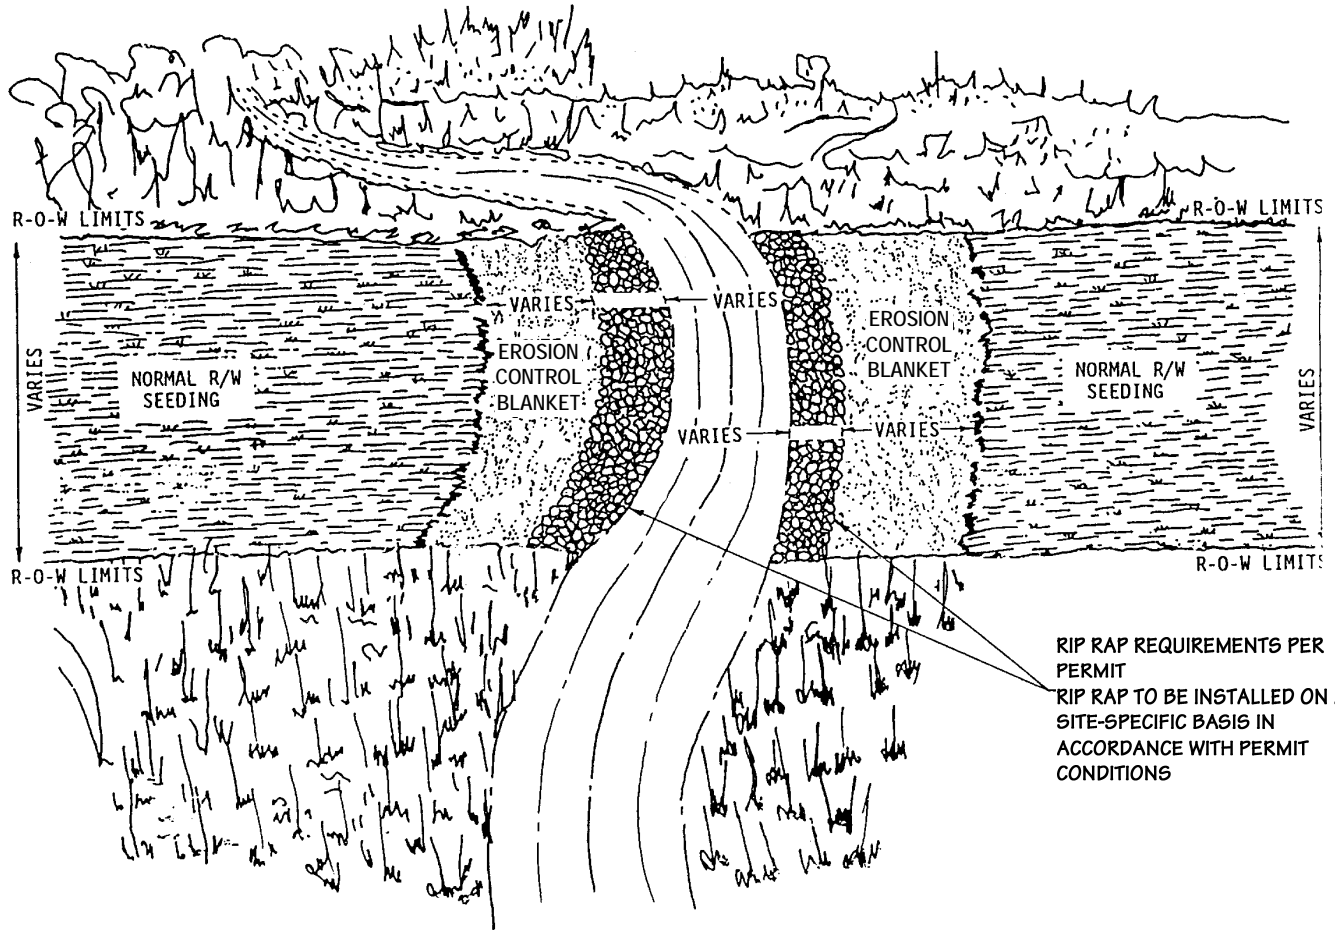


For environmental review purposes only.



Figure 23
Environmental Protection Plan
 Typical Final Stream Bank Stabilization
 Rip Rap & Erosion Control

DATE: 7/19/2000
 REVISED: 3/14/11
 SCALE: NTS
 DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\SD-FEEL\2011-019\FIG_23_STREAM_BANK_STABILIZATION.VSD



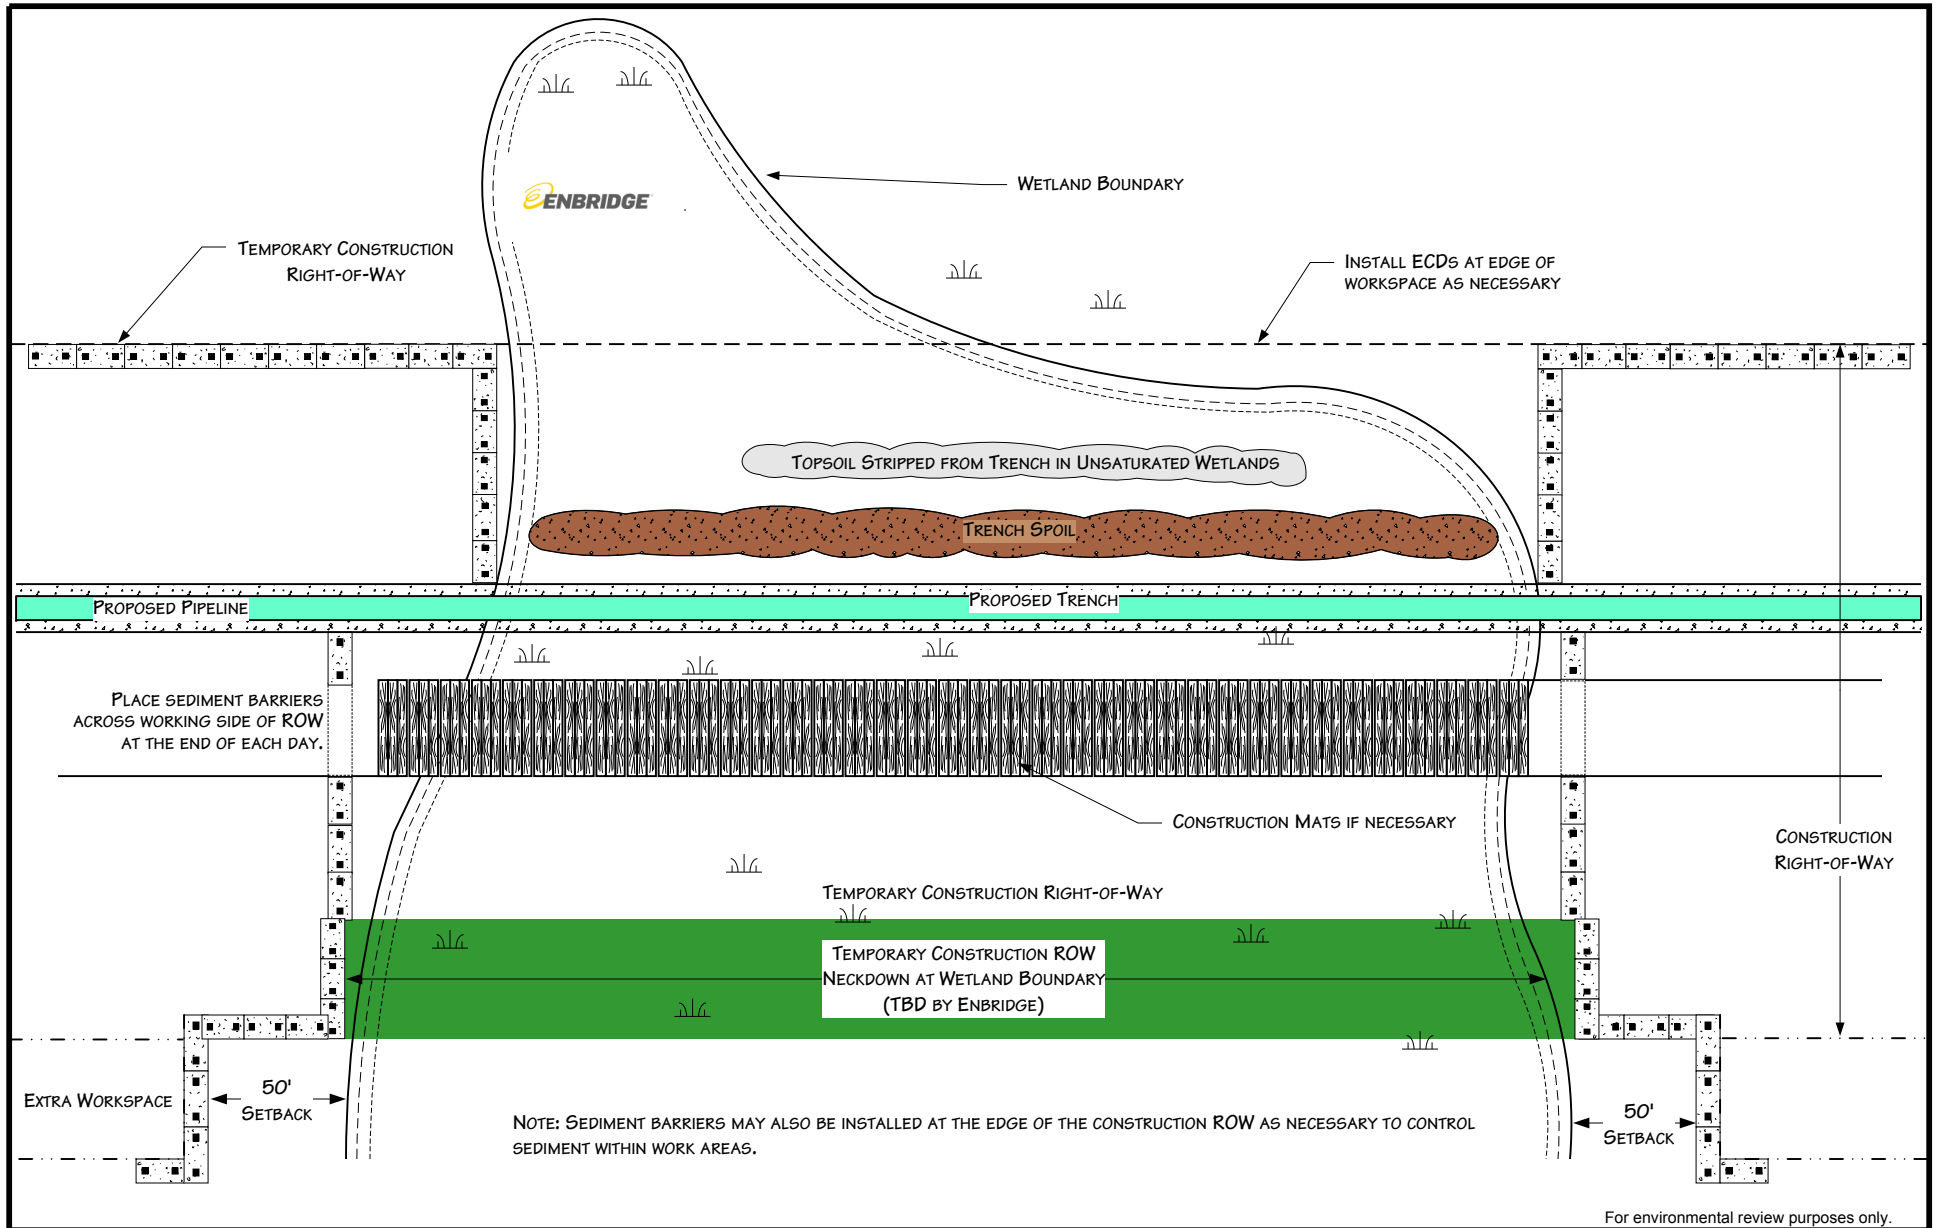


Figure 24
Environmental Protection Plan
 Typical Wetland Crossing Method

DATE: 5/25/2001


REVISED: 3/14/11

SCALE: NTS

DRAWN BY: KMKENDALL

K:\CLIENT PROJECTS\ID-FEEL\2011-019\FIG_24_WETLAND_CROSSING_METHOD.VSD



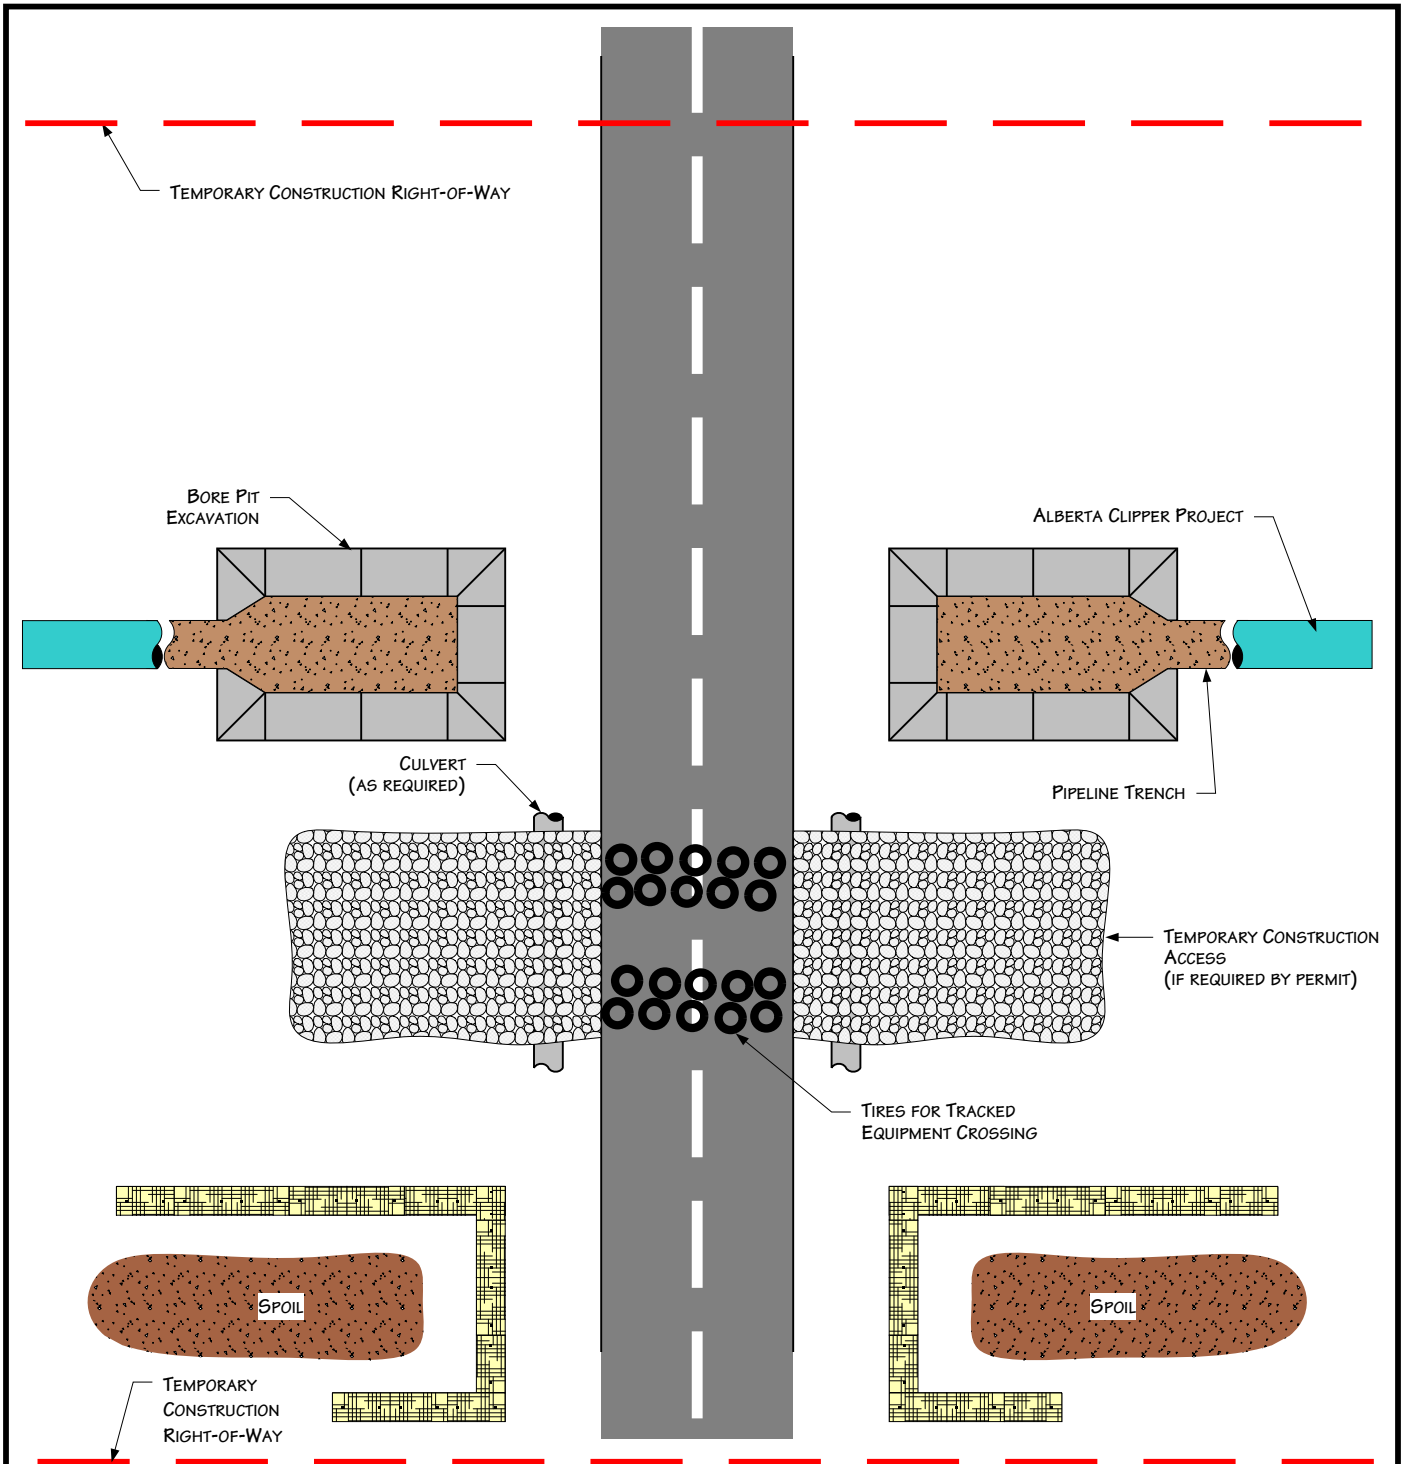

PLAN VIEW

NOTES

1. PROCEDURES SHOWN IN THIS DRAWING APPLY TO IMPROVED ROADS.
2. ROADS MUST BE CLEANED AFTER EQUIPMENT CROSSES AND DIRT PLACED IN SPOIL CONTAINMENT AREAS.
3. TEMPORARY ACCESS MATERIALS MUST BE REMOVED UPON PROJECT COMPLETION.
4. ADDITIONAL INFORMATION INCLUDED ON OTHER DRAWINGS OR PERMITS.
5. CONSTRUCTION AREAS LOCATED OUTSIDE ROAD ROW.

For environmental review purposes only.



Figure 25
Environmental Protection Plan
 Typical Improved Road Crossing
 Directional Bore Method

DATE: 7/13/1999

REVISED: 3/14/11


SCALE: NTS

DRAWN BY: KMKENDALL


K:\CLIENT_PROJECTS\D-PIEEL\2011-019\FIG_25_IMPROVED_ROAD_BORE_CROSSING.VSD




TYPICAL CROSS SECTION – BIOLOG

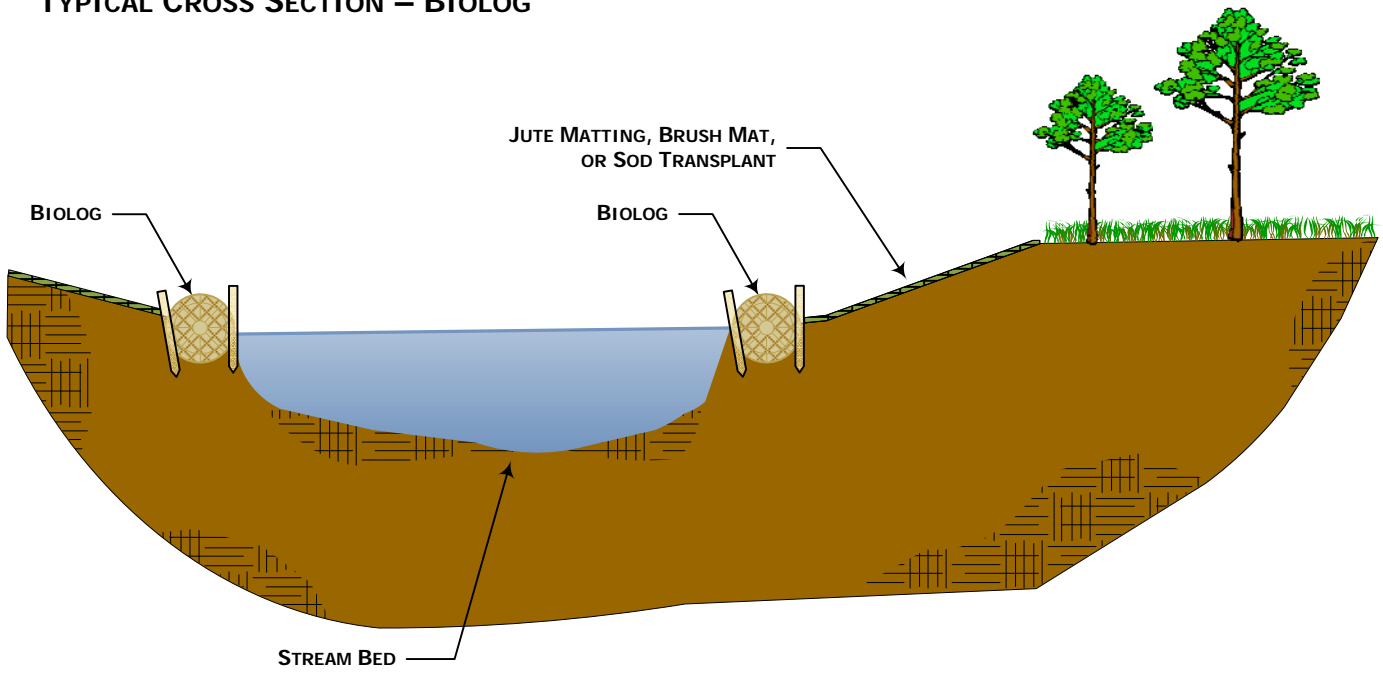


TYPICAL PLAN VIEW – BIOLOG

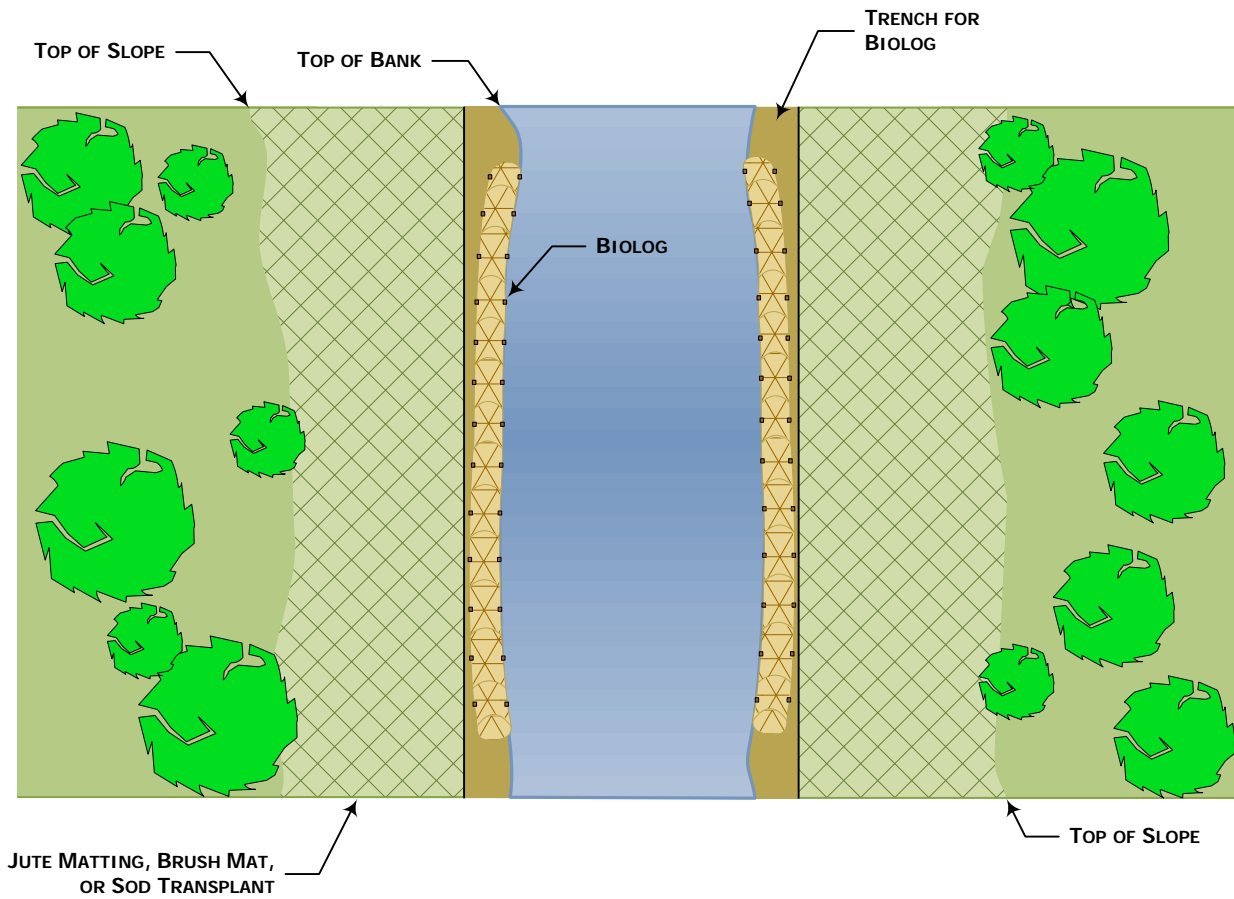


TYPICAL CROSS SECTION – SOD TRANSPLANT

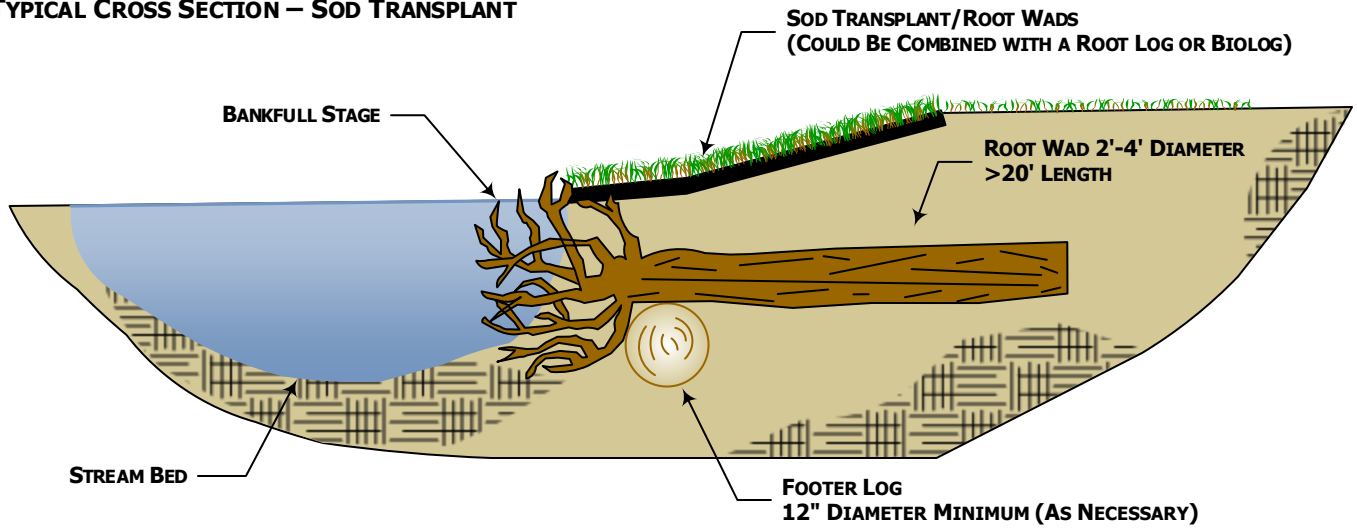


TYPICAL CROSS SECTION – JUTE MAT

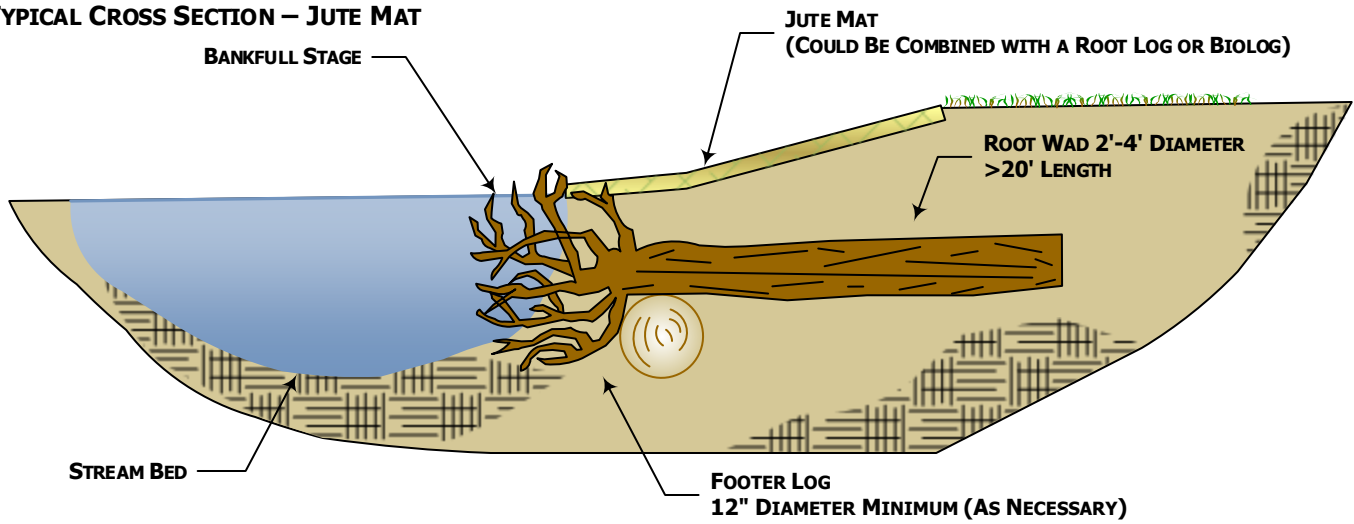

TYPICAL CROSS SECTION – BRUSH MAT

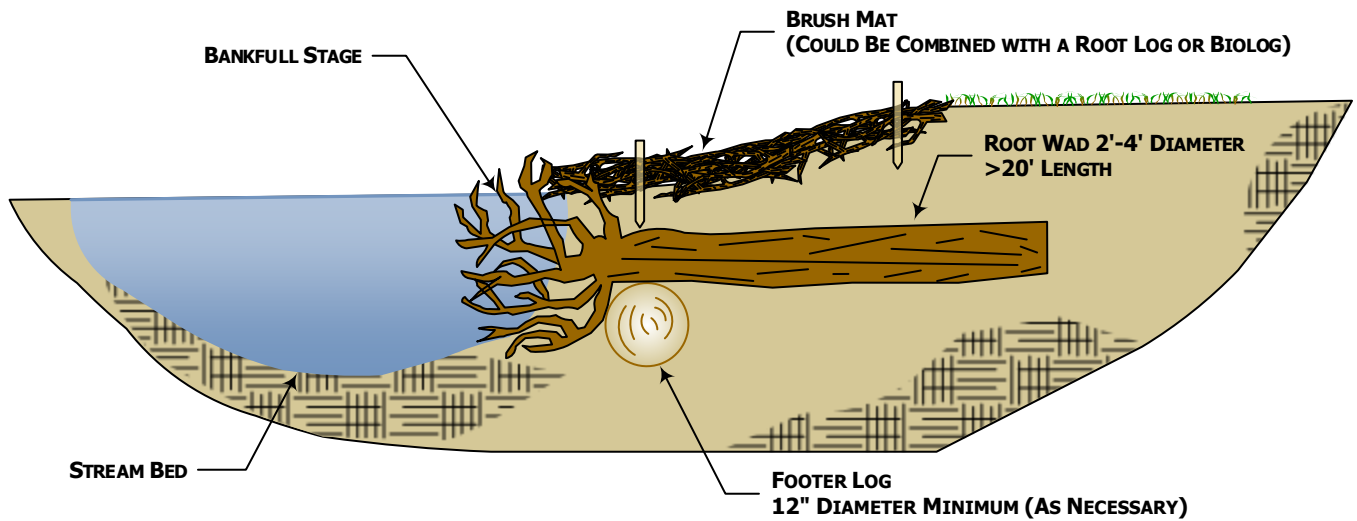

TYPICAL PLAN VIEW – NATURAL MATERIAL REVETMENT

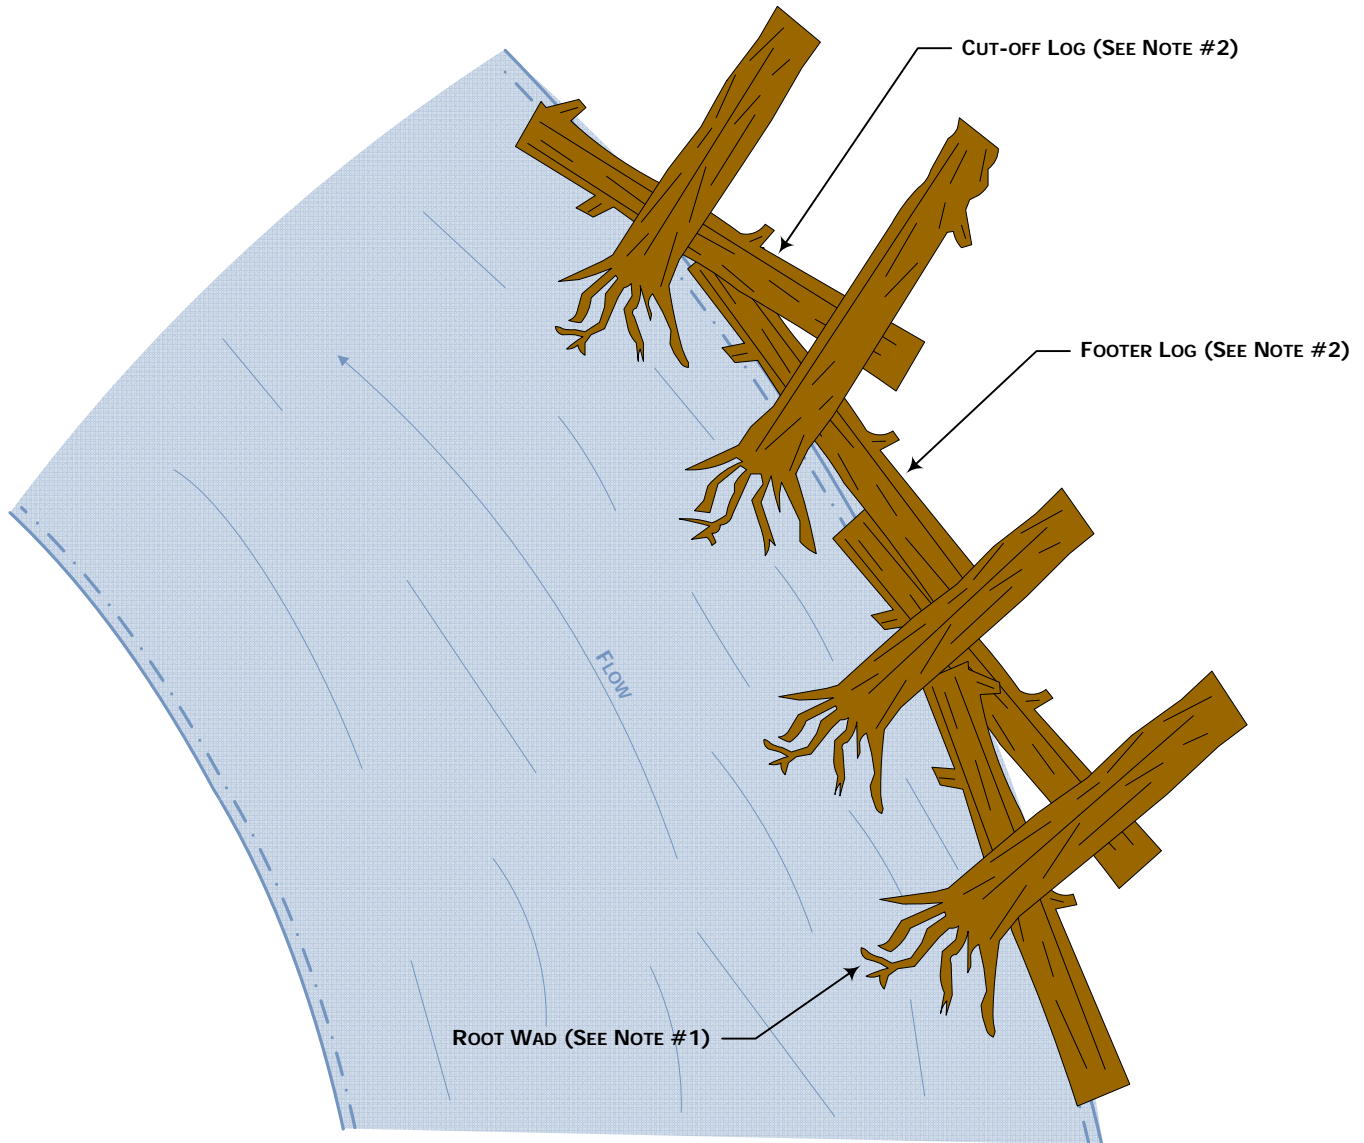

Notes:

#1 – Root wad logs to be used on steep banks or based on agency recommendations.

#2 - Root wad logs to be anchored appropriately based on site-specific conditions or agency recommendations.

This page intentionally left blank

Appendix A
Noxious and Invasive Weed Species

This page intentionally left blank

NOXIOUS AND INVASIVE SPECIES REGULATIONS

<i>Region</i>	<i>Regulatory Category</i>	<i>Agency¹</i>	<i>Reference</i>
Federal	Federal Noxious Weeds (aquatic and terrestrial plants)	USDA-APHIS	https://plants.usda.gov/java/noxious?rptType=Federal
	Federal Plant Pest Protection Act	USDA-APHIS	https://www.aphis.usda.gov/aphis/ourfocus/planthealth/plant-pest-and-disease-programs/pests-and-diseases
	Interstate Regulations: Pest movement restriction	USDA-APHIS	https://www.aphis.usda.gov/aphis/ourfocus/planthealth/plant-pest-and-disease-programs
North Dakota	State Aquatic Nuisance Species	NDGFD	https://gf.nd.gov/ans/species
	State Noxious Weeds	NDDA	https://www.nd.gov/ndda/plant-industries/noxious-weeds
	County/City Noxious Weeds	Defining County/City	https://www.nd.gov/ndda/sites/default/files/resource/2018%20Feb%20-%20City%20County%20Noxious%20Weeds%20List.pdf
Minnesota	State Prohibited, Regulated, Unregulated Nonnative, and Unlisted Nonnative Invasive Species (wild animals and aquatic plants)	MDNR	https://www.dnr.state.mn.us/invasives/laws.html
	State Prohibited, Restricted, and Specially Regulated Noxious Weeds (terrestrial plants)	MDA	http://www.mda.state.mn.us/plants/pestmanagement/weedcontrol/noxiouslist.aspx
	State Plant Pest Act (insects and terrestrial plants)	MDA	http://www.mda.state.mn.us/plants/pestmanagement/invasivesunit/pestindex.aspx
	State ballast water regulations (aquatic organisms)	MPCA	https://www.pca.state.mn.us/water/vessel-discharge
Wisconsin	State Regulated - Aquatic	WDNR	https://dnr.wi.gov/topic/Invasives/species.asp?filterBy=Aquatic&filterVal=Y
	State Regulated - Terrestrial	WDNR	https://dnr.wi.gov/topic/Invasives/species.asp?filterBy=Terrestrial&filterVal=Y
	State Regulated - Wetland	WDNR	https://dnr.wi.gov/topic/Invasives/species.asp?filterBy=Wetland&filterVal=Y
¹ APHIS: Animal Plant Health Inspection Service MDA: Minnesota Department of Agriculture MDNR: Minnesota Department of Natural Resources MPCA: Minnesota Pollution Control Agency NDDA: North Dakota Department of Agriculture NDGFD: North Dakota Game and Fish Department USDA: United States Department of Agriculture WDNR: Wisconsin Department of Natural Resources			

This page intentionally left blank

Appendix B
Equipment Cleaning Log

This page intentionally left blank



Equipment Cleaning Log

Form Completed By: _____

Date: _____ Time: _____

Location of Equipment (tract & milepost): _____

Equipment Type: _____

Equipment ID (e.g., company, unique ID number): _____

Cleaning Method: (check all that apply)

- Scrape Down
- Steam Wash Blow Down (compressed air)
- Power/Pressure Wash (water)
- Other (Describe): _____

Comments: _____

This page intentionally left blank

Appendix C


Seed Mixes

This page intentionally left blank

MINNESOTA SEED MIXES

Based on average annual precipitation and temperatures and soil types, Enbridge divided seeding in Minnesota into two regions. These regions have different seed mixes for specific areas.

- Region 1 is between the North Dakota state line and approximately Highway 71; and
- Region 2 is between Highway 71 and the Wisconsin state line.

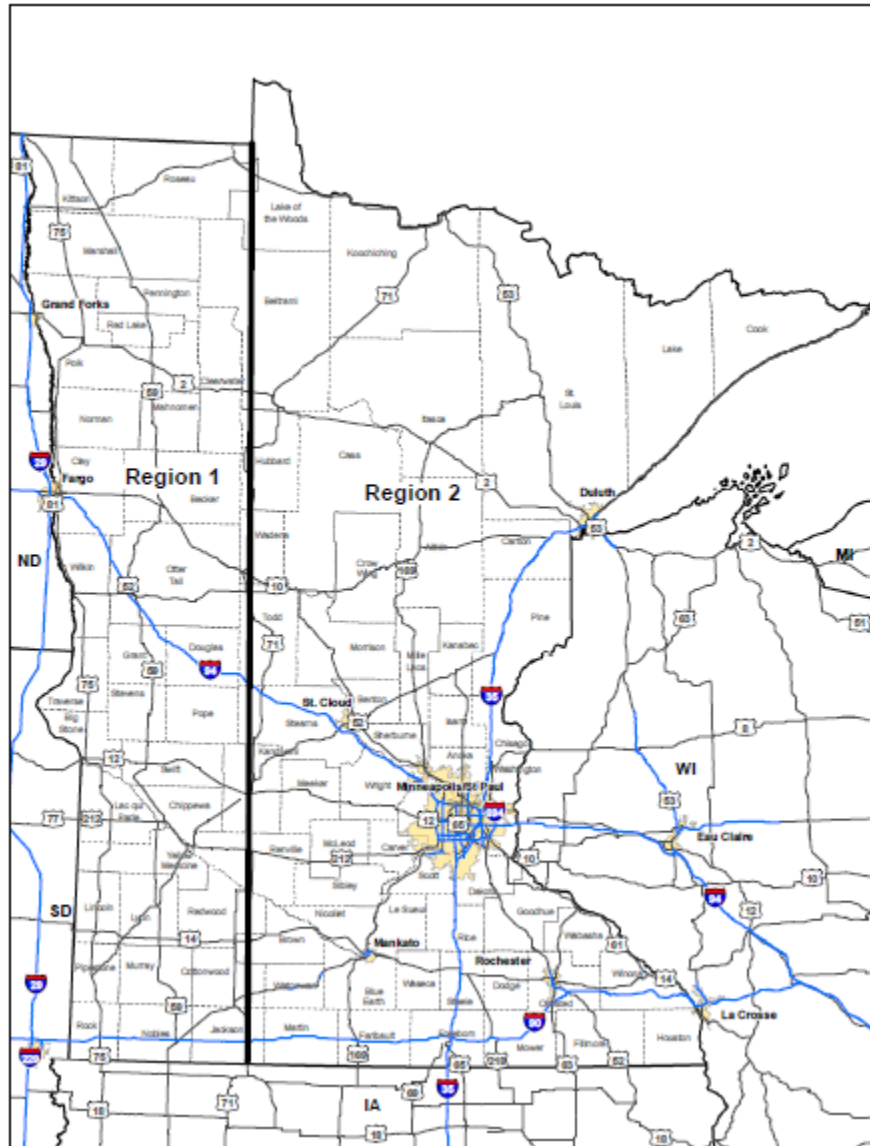

MINNESOTA STATEWIDE SEED MIXES

Table 15 MN Seed Mix 1 – Minnesota Default CRP Seed Mix		
<p><u>Use:</u> Minnesota state-wide on tracts enrolled in the CRP</p> <p><u>Seeding Rate:</u> 12.0 pounds/acre PLS drilled or 24.0 PLS pounds/acre broadcast without the companion crop Double the rate of the companion crop when broadcast seeding</p> <p><u>Notes:</u> <i>No species substitutions allowed</i></p>		
Species: Preferred Variety (if available)	Pounds/Acre PLS	Percent of Mix
Big Bluestem: Bison, Bonilla	4.0	33.3
Western Wheatgrass: Rodan	0.5	4.2
Slender Wheatgrass; Revenue	0.9	7.5
Sideoats Grama: Bad River	1.6	13.3
Switchgrass:Dacotah, Forestburg, Sunburst, Nebraska	0.2	1.7
Indiangrass: Tomahawk, Holte	0.5	4.2
Rough Dropseed: Common	0.3	2.5
Yarrow: Common	0.1	0.8
Purple Prairie Clover: Common	2.0	16.7
Ox-eye Sunflower: Common	1.0	8.3
Prairie Cinquefoil: Common	0.1	0.8
Black-eyed Susan Common	0.8	6.7
Total	12.0	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.0	100.0
Total Seed	22.0	100.0¹
¹ May not equal 100 percent due to rounding		

Table 16
MN Seed Mix 2 – Minnesota Protected and Other Waters Seed Mix

Use: Minnesota state-wide on the outer fringe of Public Water Inventory (“PWI”) waterbodies and wetlands
and all other waterbody banks

Seeding Rate: 8.255 pounds/acre PLS drilled or 16.510 pounds/acre PLS broadcast without the companion crop
Double the rate of the companion crop when broadcast seeding

Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
American slough grass: Common	1.500	18.2
Blue-joint grass: Common	0.100	1.2
Reed manna grass: Common	0.200	2.4
Fowl manna grass: Common	0.100	1.2
Fowl bluegrass: Common	1.800	21.8
Rice cut-grass: Common	0.250	3.0
Annual ryegrass: Common	0.900	10.9
Tussock sedge: Common	0.100	1.2
Fox sedge: Common	0.300	3.6
Green bulrush: Common	0.100	1.2
Wool grass: Common	0.005	0.1
River bulrush: Common	0.250	3.0
Soft-stem bulrush: Common	0.100	1.2
March milkweed: Common	0.100	1.2
Flat-topped aster: Common	0.300	3.6
Joe-pye weed: Common	0.300	3.6
Boneset: Common	0.250	3.0
Sneezeweed: Common	0.250	3.0
Spotted touch-me-not: Common	0.100	1.2
Great blue lobelia: Common	0.100	1.2
Monkey flower: Common	0.100	1.2
Mountain mint: Common	0.100	1.2
Giant goldenrod: Common	0.250	3.0
Blue vervain: Common	0.350	4.2
Ironweed: Common	0.350	4.2
Total	8.255	100.0¹
Companion Crop		
Slender wheatgrass: Adanac, Pryor, Revenue, Primar, First Strike	3.000	100.0
Total Seed	11.255	100.0¹
¹ May not equal 100 percent due to rounding		

Table 17
MN Seed Mix 3 – Minnesota Unsaturated Wetlands Seed Mix

Use: Minnesota state-wide in unsaturated wetland areas
Seeding Rate: 17.0 pounds/acre PLS drilled or 34.0 pounds/acre PLS broadcast
Notes: *No species substitutions allowed*

Species: Preferred Variety (if available)	Pounds/Acre PLS	Percent of Mix
American slough grass: Common	6.0	35.3
Annual ryegrass: Common	8.0	47.1
Flow bluegrass: Common	3.0	17.6
Total Seed	17.0	100.0¹

¹ May not equal 100 percent due to rounding

MINNESOTA REGION 1 SEED MIXES

Table 18
MN Seed Mix 4 – Native Prairie Seed Mix

Use: Minnesota Region 1 on private and public land where native or degraded prairie are currently managed as range or hay land

Seeding Rate: 13.0 pounds/acre PLS drilled or 26.0 pounds/acre PLS broadcast without the companion crop

Double the rate of the companion crop when broadcast seeding

Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
Big bluestem: Sunnyview, Bison, Bonilla, Bounty	1.25	9.6
Side-oats grama: Killdeer, Pierre, Butte	1.00	7.7
Fringed brome grass: Common	1.40	10.8
Canadian wild rye: Mandan	2.00	15.4
Slender wheatgrass: Adanac, Pryor, Revenue, Primar, First Strike	2.50	19.2
Virginia wild rye: Common	2.00	15.4
Switchgrass: Dacotah, Forestburg, Sunburst, Summer	0.75	5.8
Fowl bluegrass: Common	0.60	4.6
Indian grass: Tomahawk	1.00	7.7
Black-eyed Susan: Common	0.10	0.8
Wild bergamont: Common	0.05	0.4
Hoary vervain: Common	0.05	0.4
Partridge pea: Common	0.30	2.3
Total	13.00	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.00	100.0
Total Seed	23.00	100.0¹

¹ May not equal 100 percent due to rounding

Table 19
MN Seed Mix 5 – Mixed Hay Land (Converted Prairie) and Open-Cut Road Ditches Seed Mix

Use: Minnesota Region 1 on private mixed hay land and for re-establishing road bank/ditch vegetation
Seeding Rate: 15.0 pounds/acre PLS drilled or 30.0 pounds/acre PLS broadcast without the companion crop

Double the rate of the companion crop when broadcast seeding

Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
Meadow brome grass: Fleet, Paddock, Regar, Montana, MacBeth, Cache	3.75	25.0
Intermediate wheatgrass: Reliant, Clarke, Slate, Chief, Oahe, Haymaker, Beefmaker, Manifest	3.75	25.0
Crested wheatgrass: Nordan, RoadCrest, Summit	3.75	25.0
Tetraploid ryegrass: Common	1.50	10.0
Alfalfa: Any with Zone 2 hardiness	2.25	15.0
Total	15.00	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.00	100.0
Total Seed	25.00	100.0¹

¹ May not equal 100 percent due to rounding

Table 20
MN Seed Mix 6 – Tame Pasture Reclamation Seed Mix

Use: Minnesota Region 1 on private land tame (improved) pasture planting
Seeding Rate: 20.0 pounds/acre PLS drilled or 40.0 pounds/acre PLS broadcast without the companion crop
 Double the rate of the companion crop when broadcast seeding
Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
Alfalfa: Any with Zone 2 hardiness	6.0	30.0
Red clover: Arlington, Astred, Cinnamon , Concord or Marathon	4.0	20.0
Timothy: Climax or Claire	2.0	10.0
Orchard grass: Orion, Hawkeye, Duke, Condor, Albert	3.0	15.0
Smooth brome grass: Alpha, Badger, Bounty , York	5.0	25.0
Total	20.0	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.0	100.0
Total Seed	30.0	100.0¹
¹ May not equal 100 percent due to rounding		

MINNESOTA REGION 2 SEED MIXES

Table 21
MN Seed Mix 7 – Native Prairie Seed Mix

Use: Minnesota Region 2 on private and public land where native or degraded prairie are currently managed as range or hay land

Seeding Rate: 8.20 pounds/acre PLS drilled or 16.40 pounds/acre PLS broadcast without the companion crop

Double the rate of the companion crop when broadcast seeding

Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
Fringed brome grass: Common	2.00	24.4
Bluejoint grass: Common	0.15	1.8
Poverty grass: Common	0.50	6.1
Canadian (Nodding) wild rye: Manda	1.25	15.2
Slender wheatgrass: Adanac, Pryor, Revenue, Primar, First Strike	2.00	24.4
Fowl Bluegrass: Common	0.85	10.4
False melic grass: Common	0.25	3.0
Stiff golden rod: Common	0.15	1.8
Smooth wild rose: Common	0.15	1.8
Black-eyed susan: Common	0.25	3.0
Smooth aster: Common	0.15	1.8
American vetch: Common	0.50	6.1
Total	8.20	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.00	100.0
Total Seed	18.20	100.0¹
¹ May not equal 100 percent due to rounding		

Table 22
MN Seed Mix 8 – Mixed Hay Land and Open-Cut Road Ditches Seed Mix

Use: Minnesota Region 2 on private mixed hay land and for re-establishing road bank/ditch vegetation
Seeding Rate: 45.00 pounds/acre PLS drilled or 90.00 pounds/acre PLS broadcast without the companion crop
 Double the rate of the companion crop when broadcast seeding
Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
Fowl Bluegrass: Common	6.00	13.3
Smooth Bromegrass: Alpha, Badger, Bounty , York	7.75	17.2
Slender Wheatgrass: Adanac, Pryor, Revenue, Primar, First Strike	2.00	4.4
Perennial Rye: Citadel, Mongita, Madera, Pagent, Achiever, SR-4000, Vivid, Linn Perennial Ryegrass, Windstar, and Festulolium hybrid	13.50	30.0
Switchgrass: Kanlow, Blackwell, Shelter, Carthage	1.50	3.3
Timothy: Climax or Claire	1.75	3.9
Alfalfa: Any with Zone 2 hardiness	12.50	27.8
Total	45.00	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.00	100.0
Total Seed	55.00	100.0¹
¹ May not equal 100 percent due to rounding		

Table 23
MN Seed Mix 9 – Tame Pasture Reclamation Seed Mix

Use: Minnesota Region 2 on private land tame (improved) pasture planting
Seeding Rate: 20.0 pounds/acre PLS drilled or 40.0 pounds/acre PLS broadcast without the companion crop
 Double the rate of the companion crop when broadcast seeding
Notes: *Enbridge Environment must approve substitutions in advance*

Species: Preferred Varieties (if available)	Pounds/Acre PLS	Percent of Mix
Alfalfa: Any with Zone 2 hardiness	6.0	30.0
Red clover: Arlington, Astred, Cinnamon , Concord or Marathon	4.0	20.0
Timothy: Climax or Claire	2.0	10.0
Orchard grass: Orion, Hawkeye, Duke, Condor, Albert	3.0	15.0
Smooth brome grass: Alpha, Badger, Bounty , York	5.0	25.0
Total	20.0	100.0¹
Companion Crop		
Oats (or see Table 4 in Seed Standards and Specifications)	10.0	100.0
Total Seed	30.0	100.0¹
¹ May not equal 100 percent due to rounding		

Appendix D
Enbridge Environment Hydrotest Discharge
Authorization and Documentation

This page intentionally left blank

Enbridge Environment Hydrotest Discharge Authorization & Documentation - *Instructions*

The purpose of this form is to document and insure that appropriate planning occurs prior to hydrostatic test discharge activities as well as the proper recording of necessary information during the actual discharge event. If the discharge permit specifies the need for a Certified Operator, he/she is responsible for the final section of the form. Otherwise, an Environmental Inspector will be responsible for completion of this form.

Part 1: Basic Discharge Information: All information must be completed. Coordination with Enbridge Engineering is necessary to obtain the exact test section length and volume of water to be discharged. The estimated duration of the discharge must be calculated using the maximum permitted rate (or the anticipated rate, if lower than the permitted rate) and the total volume of water to be discharged. This is critical information and will ensure that any required sampling is conducted at the appropriate frequency specified in the permit.

Part 2: Pre-Discharge Planning Checklist: A pre-discharge planning meeting must be held with the Certified Operator (if required), Contractor, Craft Inspection, Environmental Inspection, and Construction Management staff to review items included in the checklist and any other pertinent information deemed necessary. A full copy of the permit and discharge plan must be provided to all participants. Upon completion of this meeting, all participants must sign the form to indicate that they understand all steps of the discharge process. **Note: In order to proceed with discharge activities, the Enbridge Construction Manager and Environment Staff assigned to the project, or their designees, must review the information and provide their authorization by signing and dating the form.**

Part 3: Discharge Monitoring: A copy of the permit, discharge plan, and parts one and two of the form must be on-site at all times during the discharge event. In addition to the items specified on the form, the following photographs are required:

- Receiving water before, during, and after the discharge (minimum 3 photos/day)
- Discharge structure/device before and during the discharge (minimum 3 photos/day)

As noted, upon completion of the discharge event, the Certified Operator or Environmental Inspector, Craft Inspector, Contractor Foreman, and Enbridge Construction Manager must sign and date the form. **The completed form, along with the supplemental photographs, and a copy of the chain of custody for any samples submitted for laboratory analysis must be submitted to the Enbridge Environment Project Manager/Lead within 12 hours of ending the discharge. Any permit violations will be reported to the applicable agencies by the Enbridge Environment Project Manager/Lead within the timeframes specified in the discharge permit.**

Flow meter manufacturer and model:

Flow meter date of last calibration :

pH/Dissolved Oxygen instrument manufacturer and model:

pH/Dissolved Oxygen instrument date of last calibration:

Date and Time discharge start: _____ Date and Time discharge complete: _____

Equipment, Discharge, and Receiving Water Inspection Notes (minimum 3 entries per day):

Outfall Observations & Photo Documentation Notes (note presence or absence of any unusual characteristics such as unnatural turbidity, color, oil film, floating solids, foams, settleable solids, suspended solids, or deposits - minimum 3 entries per day) :

Certified Operator or Environmental Inspector Signature: _____

Enbridge Craft Inspector Signature: _____

Contractor Foreman Signature: _____

Enbridge Construction Manager Signature: _____

Appendix E
Emergency Response Contractors/Disposal and
Treatment Facilities

This page intentionally left blank

Emergency Response Contractors

The Contractor will dispose of all wastes according to applicable federal, state, and local requirements. A listing of potential Emergency Spill Response Contractors and is provided below, and waste disposal facilities by state are provided in the pages that follow. This list was developed from state-wide databases. This list represents firms operating at the time the database was produced. The Contractor is responsible for verifying if a contractor or facility is currently operating under appropriate permits or licenses. The Contractor is responsible for ensuring wastes are disposed of properly.


Spill Response Contractors		
Company	City/State	Phone Number
North Dakota		
Clean Harbors Environmental	Williston, ND	(701) 774-2201 (800) 645-8265
Garner Environmental Services	Williston, ND	(701) 577-1200 (855) 774-1200
Absorbent & Safety Solutions	Watford City, ND	(701) 838-4558
Minnesota Limited	Berthold, ND	(701) 453-3700
Bobs Oilfield Service Inc	Belfield, ND	(701) 575-4666
Keitu Engineers & Consultants, Inc.	Mandan, ND	(701) 667-1800
Minnesota		
Bay West Environmental	St. Paul, MN	(800) 279-0456 (651) 291-0456
West Central Environmental Consultants Inc.	Morris, MN	(800) 422-8356 (888) 923-2778
Minnesota Limited	Bemidji, MN	(218) 755-9595
OSI Environmental	Bemidji, MN	(800) 585-8838
OSI Environmental	Eveleth, MN	(800) 777-8542
Bay West Environmental	Duluth, MN	(800) 279-0456 (218) 740-0110
Wisconsin - <i>The Contractor should consult with the WDNR Northern Regional Spill Coordinator (John Sager: phone (715) 365-8959) for assistance when selecting a spill response contractor.</i>		

This page intentionally left blank

F:\Enbridge Disposal\maps\g25enbdisposal01k.mxd, 5/13/2016, 10:58:30 AM, NAD 1983 UTM Zone 15N Source: Aerial imagery from ArcGIS Online.

Facility ID	Facility (Minnesota)
Hazardous Waste Facilities	
1	Clean Harbors, Cannon Falls
2	Safety-Kleen, Inc.
Waste Water Treatment Plant Facilities (WWTP)	
1	Aitkin Sewage Treatment Plant
2	GRPUC Wastewater Treatment Facility
3	Crookston Wastewater Treatment Facility
4	Hibbing Waste Treatment Plant
5	Virginia Wastewater Treatment
6	WLSSD
Non-Hazardous Waste Facilities	
1	Pinebend Landfill (Republic Services)
2	Burnsville Sanitary Landfill (WM)
3	Spruce Ridge Landfill (WM)
4	Elk River Landfill (WM)
5	Canyon (Voyageur) (WM)
6	SKB - Rosemount
7	SKB - Environmental Landfill
8	SKB - Shamrock Landfill

*For North Dakota and Wisconsin - see state map for facility information

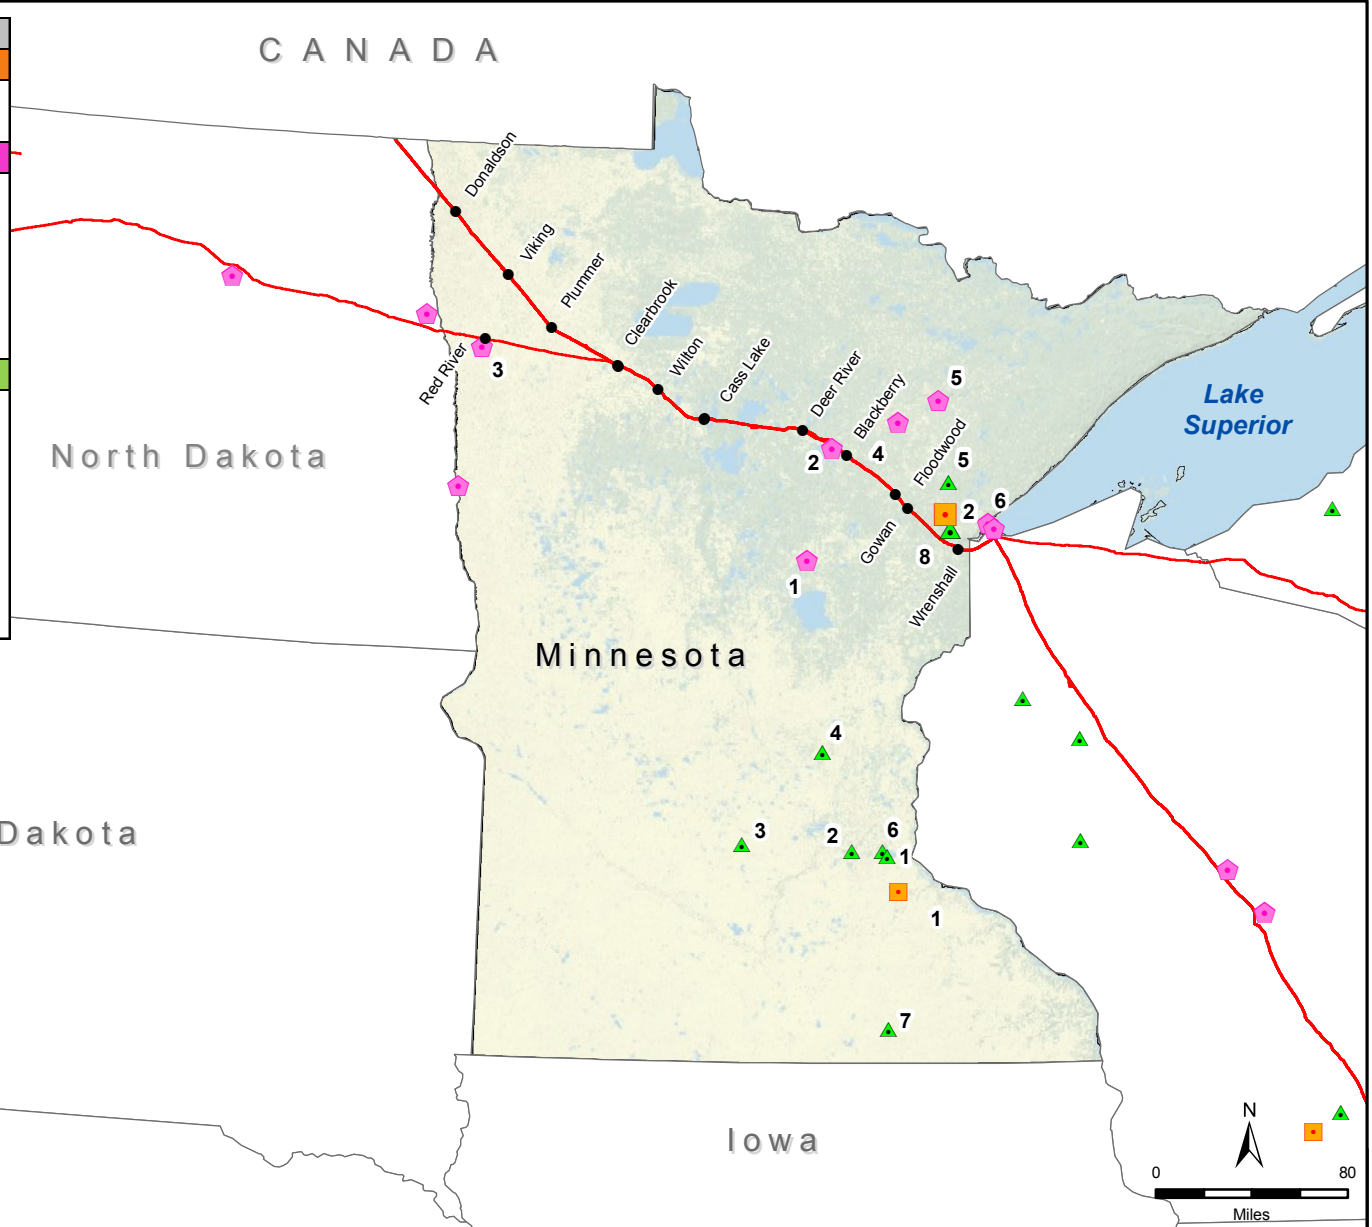

Drawn: LBG 5/13/2016
Approved: LBG 5/13/2016
Project #: Disposal



Legend

- Hazardous Waste Facility
- Waste Water Treatment Plant (WWTP)
- Non-Hazardous Waste Facility
- Enbridge Pipeline

WASTE FACILITIES - MINNESOTA

Uncontrolled Copy if Printed



Waste Facilities – Minnesota

Facility ID	Facility (Minnesota)	Waste Type	Address	City	State	Zip	County	Contact Phone
Hazardous Waste Facilities								
1	Clean Harbors, Cannon Falls	Solid & Liquid - Haz	211 Holiday Avenue	Cannon Falls	MN	55009	Goodhue	(507) 263-0252
2	Safety-Kleen, Inc.	Solid & Liquid - Haz	1302 18th Street	Cloquet	MN	55720	Goodhue	(218) 879-2164
Waste Water Treatment Plant Facilities (WWTP)								
1	Aitkin Sewage Treatment Plant	Liquid -WWTP	120 1st Street Northwest	Aitkin	MN	56431	Aitkin	(218) 927-3406
2	GRPUC Wastewater Treatment Facility	Liquid -WWTP	1105 SE 23rd Avenue	Grand Rapids	MN	55744	Itasca	(218) 326-7024
3	Crookston Wastewater Treatment Facility	Liquid -WWTP	County Road 233	Crookston	MN	56716	Polk	(218) 281-5711
4	Hibbing Waste Treatment Plant	Liquid -WWTP	11669 Town Line Road	Hibbing	MN	55746	St. Louis	(218) 362-5999
5	Virginia Wastewater Treatment	Liquid -WWTP	1204 Southern Drive	Virginia	MN	55792	St. Louis	(218) 748-7519
6	WLSSD	Liquid -WWTP	2626 Courtland Street	Duluth	MN	55806	St. Louis	(218) 722-3336
Non-Hazardous Waste Facilities								
1	Pinebend Landfill (Republic Services)	Solid - NonHaz	2495 East 117th Street	Inver Grove Heights	MN	55077	Dakota	(651) 450-2155
2	Burnsville Sanitary Landfill (WM)	Solid - NonHaz	2650 West Cliff Road	Burnsville	MN	55337	Dakota	(952) 890-3248
3	Spruce Ridge Landfill (WM)	Solid - NonHaz	12755 137th Street	Glencoe	MN	55336	McLeod	(320) 864-5503
4	Elk River Landfill (WM)	Solid - NonHaz	22460 Highway 169	Elk River	MN	55330	Sherburne	(763) 441-2464
5	Canyon (Voyageur) (WM)	Solid - NonHaz	6830 Highway 53	Canyon	MN	55717	St. Louis	(218) 345-6302
6	SKB - Rosemount	Solid - NonHaz	13425 Courthouse Blvd	Rosemount	MN	55060	Dakota	(651) 438-1500
7	SKB - Environmental Landfill	Solid - NonHaz	52563 243rd Street	Austin	MN	55912	Mower	(507) 433-8131
8	SKB - Shamrock Landfill	Solid - NonHaz	761 MN Highway 45	Cloquet	MN	55720	Carlton	(218) 878-0112

Uncontrolled Copy if Printed

Appendix F
Spill Report Form

This page intentionally left blank



Spill Report Form

(The Contractor Spill Coordinator must complete this for any spill, regardless of size, and submit the form to the Enbridge Representative within 24 hours of the occurrence)

Date of Spill: _____ Date of Spill Discovery: _____

Time of Spill: _____ Time of Spill Discovery: _____

Name and Title of Discoverer: _____

Type of material spilled and manufacturer's name: _____

Legal Description of spill location to the quarter section: _____

Directions from nearest community: _____

Estimated volume of spill: _____

Weather conditions: _____

Topography and surface conditions of spill site: _____

Spill medium (pavement, sandy soil, water, etc.): _____

Proximity of spill to surface waters: _____

Did the spill reach a waterbody? _____ Yes _____ No

If so, was a sheen present? _____ Yes _____ No

Describe the causes and circumstances resulting in the spill: _____

Describe the extent of observed contamination, both horizontal and vertical (i.e., spill-stained soil in a 5-foot radius to a depth of 1 inch): _____

Describe immediate spill control and/or cleanup methods used and implementation schedule: _____

Current status of cleanup actions: _____

Name and Company for the following:

Construction Superintendent: _____

Spill Coordinator: _____

Enbridge Representative: _____

Person Who Reported the Spill: _____

Environmental Inspector: _____

Form completed by: _____ Date: _____

This page intentionally left blank

Appendix G
Spill Reporting-Agency Contacts

This page intentionally left blank

Spill Reporting Contacts						
Agency	Water	Soil	Notification Period	24-Hour Reporting Hotline	Regulation/Code	Comments
Federal Contacts						
National Response Center	Any quantity of discharged oil that violates state water quality standards, causes a film or sheen on water's surface or leaves sludge or emulsion beneath the surface	Release of a hazardous substance in an amount equal to or greater than its reportable quantity under CERCLA	Immediately	1-800-424-8802	40 CFR 302 – Designation, Reportable Quantities, and Notification	
Environmental Protection Agency Region V (MN / WI)	Any quantity of discharged oil that violates state water quality standards, causes a film or sheen on water's surface or leaves sludge or emulsion beneath the surface		Immediately	1-312-353-2000	40 CFR 117 – Determination of Reportable Quantities for Hazardous Substances Clean Water Act § 311 – Oil and Hazardous Substance Liability	

Spill Reporting Contacts						
Agency	Water	Soil	Notification Period	24-Hour Reporting Hotline	Regulation/Code	Comments
Environmental Protection Agency Region VIII (ND)	Any quantity of discharged oil that violates state water quality standards, causes a film or sheen on water's surface or leaves sludge or emulsion beneath the surface		Immediately	1-303-312-6312	40 CFR 117 – Determination of Reportable Quantities for Hazardous Substances Clean Water Act § 311 – Oil and Hazardous Substance Liability	
State Contacts						
Minnesota Pollution Control Agency	Visible Sheen or Emulsion	No minimum quantity for crude oil. Any spill >5 gallons of refined petroleum product. Spills of any quantity of all other chemicals or materials should be reported.	Immediately upon discovery.	Minnesota State Duty Officer 1-800-422-0798 (In State) or (651) 649-5451	Minnesota Statute 115.061	Follow up report established after initial response.

Spill Reporting Contacts						
Agency	Water	Soil	Notification Period	24-Hour Reporting Hotline	Regulation/Code	Comments
North Dakota Department of Health	Visible Sheen or Emulsion	No minimum requirement. All spills that impact or threaten groundwater or surface water or may potentially have adverse effects on human health or the environment are reportable.	Immediately upon discovery.	North Dakota Department of Health 1-701-328-5210 North Dakota Hazardous Materials Emergency Assistance and Spill Reporting 1-800-472-2121 (In State) 1-701-328-5210 (Out of State)	North Dakota Administrative Code NDAC 33-16-02.1-1	Follow up report established after initial response.

Spill Reporting Contacts						
Agency	Water	Soil	Notification Period	24-Hour Reporting Hotline	Regulation/Code	Comments
Wisconsin Department of Natural Resources	Visible Sheen or Emulsion	All spills are reportable unless they meet the following criteria: 1) spill is contained on an impervious surface; 2) <5 gallons of petroleum products on a pervious surface; 3) <1 gallon of gasoline on a pervious surface.	Immediately of any discharge not exempted by the statute.	24-hour WI DNR reporting number 1-800-943-0003	Chapter 292.11 of the Wisconsin Statutes, Chapter NR 706 Wisconsin Administrative Code	Follow up report established after initial response.
County Contacts – Minnesota						
Kittson County Emergency Management	As Needed			Scot Olson (218) 843-2113	Kittson County 2015 Hazard Management Plan	
Marshall County Emergency Services	As Needed			Josh Johnston (218) 745-5841	Marshall County, MN Hazard Mitigation Plan 2016 Update	
Pennington County Emergency Management	As Needed			Erik Beitel (218) 683-7087		
Wadena County Emergency Management	As Needed			Tyler Wheeler (218) 631-7795		

Spill Reporting Contacts						
Agency	Water	Soil	Notification Period	24-Hour Reporting Hotline	Regulation/Code	Comments
Polk County Emergency Management	As Needed			Jody Beauchane, Director (218) 470-8263	Polk County, MN Hazard Mitigation Plan (July 2015)	
Red Lake County Emergency Management	As Needed			Mitch Bernstein (218) 253-2996		
Clearwater County Emergency Management	As Needed		8:00 AM – 4:30 PM Monday – Friday	(218) 694-6226		
Hubbard County Emergency Management	As Needed			Brian Halbasch (218) 732-2588		
Cass County Emergency Management	As Needed			Chad Emery (218) 547-7437	Cass County Hazard Mitigation Plan	
Crow Wing County Emergency Management	As Needed			John Bowen, Director (218) 829-4749		
Aitkin County Emergency Management	As Needed			Dispatch (non-emergency) (218) 927-7400		
Carlton County Emergency Management	As Needed			Steve VanKekerix, Director (218) 384-9539		

Spill Reporting Contacts						
Agency	Water	Soil	Notification Period	24-Hour Reporting Hotline	Regulation/Code	Comments
St Louis County Emergency Management	As Needed			Sheriff's Office Emergency Management Division (218) 336-4340		
County Contacts – North Dakota						
Pembina County Emergency Management	As Needed			Andrew Kirking (701) 265-4849		
County Contacts – Wisconsin						
Douglas County Emergency Management	As Needed		8:00 AM – 4:30 PM Monday – Friday	Keith Kesler, Director (715) 395-1636		

Minnesota

This page intentionally left blank

MINNESOTA SPILL NOTIFICATION REQUIREMENTS

The Minnesota Department of Public Safety, Division of Emergency Management (DEM) operates a 24-hour State Duty Officer service establishing a one call system for all state reporting requirements. The Duty Officers record all pertinent information and then make the appropriate notifications to the county and state agencies. The 24-Hour spills and leaks hotline can be reached via one of the following telephone numbers:

1-800-422-0798 (In State)

1-651-649-5451 (Out of State)

The Minnesota Pollution Control Agency (MPCA) requires immediate notification upon discovery of any spill of any quantity of crude oil. This includes historical contamination found during environmental investigations.

Every person who has “any substance or material under its control” is required to report. This includes:

- Property owners who discover contamination – Individuals, partnerships, companies, corporations;
- Governmental subdivisions, including officers of these entities;
- Owners of substances being stored or transported by another company; and
- Contractors that are in physical control of a discharged substance.

In addition to MPCA notification, local regulations may require additional notifications.

Additionally, reporting of releases of non-petroleum materials greater than the Reportable Quantity (RQ) is required if the material exceeds the quantity listed in **Table 3** (located at the beginning of this document).

This page intentionally left blank

**Minnesota Reporting of Petroleum Releases Guidance
Documents**

This page intentionally left blank

Reporting leaks and spills

Minn. Stat. §115.061, which has been in effect since 1969, describes the duty of people to notify the Minnesota Pollution Control Agency (MPCA) when spills and leaks occur:

115.061 — Duty to Notify and Avoid Water Pollution

- a) Except as provided in paragraph (b), it is the duty of every person to notify the agency immediately of the discharge, accidental or otherwise, of any substance or material under its control which, if not recovered, may cause pollution of waters of the state, and the responsible person shall recover as rapidly and thoroughly as possible such substance or material and take immediately such other action as may be reasonably possible to minimize or abate pollution of waters of the state caused thereby.
- b) Notification is not required under paragraph (a) for a discharge of five gallons or less of petroleum, as defined in section 115C.02, subdivision 10. This paragraph does not affect the other requirements of paragraph (a).

The law provides penalties of up to \$10,000 per day for violations.

The Minnesota Department of Public Safety, Bureau of Criminal Apprehension, operates a 24 hour service, establishing a one call system for all state reporting requirements.

Reportable spills should be directed to the Minnesota Duty Officer by calling 651-649-5451 or 800-422-0798.

The duty officer will record all pertinent information and then make the appropriate notifications to the state agencies.

Spills that must be reported

Report spills that may cause pollution, such as spills of toxic, flammable, corrosive and dangerous industrial chemicals. Also report spills of environmentally damaging materials, including milk, coal, animal parts, batteries, etc.

Reportable quantities

Minnesota has a reporting threshold of greater than five-gallons for petroleum spills. Spills of any quantity of all other chemicals or materials should be reported. If in doubt, report.

Anyone who spills is required to report

EVERY person who has “any substance or material under its control” must report spills and leaks. This includes:

- property owners who discover contamination;
- individuals, partnerships, companies and corporations;
- governmental subdivisions, including officers of these entities;
- owners of substances being stored or transported by another company; and
- contractors who are in physical control of a discharged substance.

Sometimes a fire department, police agency or other local or state agency that responds to a spill or leak chooses to report the incident to the MPCA. In some circumstances, the entity may be required to report the

spill. However, in no case does a report from someone else stand in lieu of your responsibility to report to the MPCA by calling the Minnesota Duty Officer if a substance is under your control.

Be aware that there may be other reporting requirements imposed by local ordinances, state or federal law, or permits. Understanding all reporting requirements is the responsibility of those who handle substances which can pollute.

It is the responsibility of the spiller to ensure an effective cleanup and proper management of all wastes generated. With the exception of used oil, waste generated from petroleum spills that have been reported and cleaned up immediately are exempt from Minnesota's Hazardous Waste Rules. Waste from used oil spills must be sent to a facility for energy recovery.

For more information

For more information on spill prevention, cleanup or disposal, call the MPCA at 651-296-6300 or 800-657-3864 and ask for a member of the Emergency Management Unit or go to <https://www.pca.state.mn.us/waste/emergency-response>.

More information is also on the U.S. Environmental Protection Agency website at <https://www.epa.gov/oilspill/>.



Crude oil and unrefined petroleum wastes

Crude oil and related unrefined petroleum wastes present risks to human health and the environment if improperly managed. This fact sheet will discuss the hazardous waste requirements for these wastes administered by the Minnesota Pollution Control Agency (MPCA) and the Metropolitan Counties of Anoka, Carver, Dakota, Hennepin, Ramsey, Scott, and Washington (Metro Counties).

What are crude oil and unrefined petroleum wastes?

Crude oil wastes include:

- Spilled crude oil or unrefined petroleum from pipelines, trains, trucks, tanks, and other sources.
- Absorbents, cleanup materials, soil, and water contaminated with crude oil or unrefined petroleum.

Crude oil and unrefined petroleum wastes almost always contain enough benzene and related organic compounds to make them a characteristic hazardous waste. They may also contain hazardous concentrations of heavy metals, including arsenic, cadmium, chromium, lead, mercury, and selenium.

Assume untested crude oil, unrefined petroleum, and any related wastes that will be disposed or burned are hazardous wastes until you evaluate them and document that they are non-hazardous. See MPCA fact sheet #w-hw1-01, Evaluate Waste, at <https://www.pca.state.mn.us/sites/default/files/w-hw1-01.pdf>.

What are *not* crude oil or unrefined petroleum wastes?

Other wastes may be confused with crude oil and unrefined petroleum wastes, including:

- Manufactured or refined petroleum-based and other-based fuels, such as fuel oil, gasoline, and diesel. Manage these fuel-related wastes as discussed in MPCA fact sheet #w-hw4-19, Fuel-related Wastes, at <https://www.pca.state.mn.us/sites/default/files/w-hw4-19.pdf>.
- Used oils and related wastes, including lubricating, hydraulic, and cutting oils. Manage these used oil wastes as discussed in MPCA fact sheet #w-hw4-30, Used Oil and Related Wastes, at <https://www.pca.state.mn.us/sites/default/files/w-hw4-30.pdf>.
- Recovered crude oil or unrefined petroleum that will be managed by refining along with normal process streams at a petroleum refining facility. This material is considered a commodity instead of a regulated waste.

What must I do if crude oil or unrefined petroleum is spilled?

Immediately report all spills of crude oil or unrefined petroleum to the Minnesota Duty Officer. See [More information](#) on the page 3. If needed, call 911 to summon emergency responders first.

Note: The five-gallon exemption in Minnesota's spill reporting law applies only to refined petroleum fuel products, not crude oil or unrefined petroleum-contaminated wastes. All spills of crude oil or unrefined petroleum, regardless of volume, must be reported.

Next, take all reasonable steps to contain the spill and begin to recover as much of the spilled material as possible. Follow any directions given to you by MPCA Emergency Management Unit (EMU) staff.

Finally, document your spill response actions. Submit a written report of transport-related spills to the U.S. Department of Transportation (DOT) within 30 days.

How must crude oil and unrefined petroleum wastes be managed?

- Manage untested wastes and wastes that are not eligible for any of the other options below as fully regulated hazardous wastes. See MPCA fact sheet #w-hw1-06, Treat or Dispose of Hazardous Waste, at <https://www.pca.state.mn.us/sites/default/files/w-hw1-06.pdf>.
- In certain situations, MPCA EMU staff may allow specific management of crude oil or unrefined petroleum wastes that is different than explained in this fact sheet. If the EMU staff issue a specific allowance, this authorization supersedes the requirements discussed here. EMU authorizations are incident-specific and cannot be used for a different spill.
- Liquids and solids that meet the criteria below may be managed equivalent to off-specification used oil and burned for energy recovery in utility or industrial furnaces and boilers. Crude oil and unrefined petroleum wastes that will be burned for energy recovery equivalent to used oil must contain:
 - 10 parts per million (ppm) or less of arsenic.
 - 0.2 ppm or less of mercury.

For guidance on management requirements for off-specification used oil, see MPCA fact sheet #w-hw4-30, Used Oil and Related Wastes, at <https://www.pca.state.mn.us/sites/default/files/w-hw4-30.pdf>.

- Contaminated soil shown to leach less arsenic, cadmium, chromium, lead, mercury, and selenium than the hazardous waste toxicity characteristic levels in MPCA fact sheet #w-hw2-04, Characteristic Hazardous Wastes, at <https://www.pca.state.mn.us/sites/default/files/w-hw2-04.pdf>, may be transported without a hazardous waste manifest in Minnesota and:
 - Landfilled if soils have been dewatered and the receiving landfill's permit and Industrial Solid Waste Management Plan allow its acceptance. The landfill must be notified prior to shipment and must agree to accept the soil. The landfill may require additional testing before accepting the waste, and may apply specific conditions or limitations to the disposal.
 - Land applied if soil application has been approved by the MPCA's Petroleum Remediation Program (PRP). For information on the PRP approval process, see MPCA fact sheet #c-prp3-03, Land Treatment of Petroleum Contaminated Soil, at <https://www.pca.state.mn.us/sites/default/files/c-prp3-03.pdf>.
- Contaminated water shown to contain less arsenic, cadmium, chromium, lead, mercury, and selenium than the hazardous waste toxicity characteristic levels in MPCA fact sheet #w-hw2-04, Characteristic Hazardous Wastes, at <https://www.pca.state.mn.us/sites/default/files/w-hw2-04.pdf>, may be transported without a hazardous waste manifest in Minnesota and:
 - Discharged to a publicly owned treatment works (POTW). The POTW must be notified prior to shipment and must agree to accept the water. The POTW may require additional testing before accepting the waste, and may apply specific conditions or limitations to the discharge.
 - Land applied if water application has been issued a National Pollutant Discharge Elimination System/State Disposal System (NPDES/SDS) Permit for Contaminated Groundwater by the MPCA. For the application process for this permit, see MPCA form #wq-wwprm7-29, Industrial Groundwater Pump-Out Application, at <https://www.pca.state.mn.us/sites/default/files/wq-wwprm7-29.doc>.

More information

Guidance in this fact sheet was compiled from Minnesota Statutes, Chapter 115, and Minnesota Rules, Chapters 7037 and 7045, and incorporates regulatory interpretation decisions made by the MPCA on April 13, 2016. To review Minnesota laws, visit the Office of the Revisor of Statutes at <https://www.revisor.mn.gov/pubs>.

For information about waste minimization, contact the Minnesota Technical Assistance Program (MnTAP). The MPCA's Small Business Environmental Assistance Program can offer free, confidential compliance assistance. Immediately report all hazardous waste spills to the Minnesota Duty Officer.

Metro County Hazardous Waste Offices

Anoka	763-422-7093
.....	https://www.anokacounty.us/
Carver	952-361-1800
.....	http://www.co.carver.mn.us/
Dakota	952-891-7557
.....	https://www.co.dakota.mn.us/
Hennepin	612-348-3777
.....	http://www.hennepin.us/
Ramsey	651-266-1199
.....	https://www.ramseycounty.us/
Scott	952-496-8475
.....	http://www.scottcountymn.gov/
Washington	651-430-6655
.....	https://www.co.washington.mn.us/

Minnesota Pollution Control Agency

Toll free (all offices)	1-800-657-3864
All offices	651-296-6300
.....	https://www.pca.state.mn.us/

Minnesota Duty Officer

Toll free	1-800-422-0798
Metro	651-649-5451

Small Business Environmental Assistance Program

Toll free	1-800-657-3938
Metro	651-282-6143
.....	https://www.pca.state.mn.us/sbeap/


Minnesota Technical Assistance Program

Toll free	1-800-247-0015
Metro	612-624-1300
.....	http://www.mntap.umn.edu

This page intentionally left blank

Minnesota Pollution Control Agency District Contacts

This page intentionally left blank

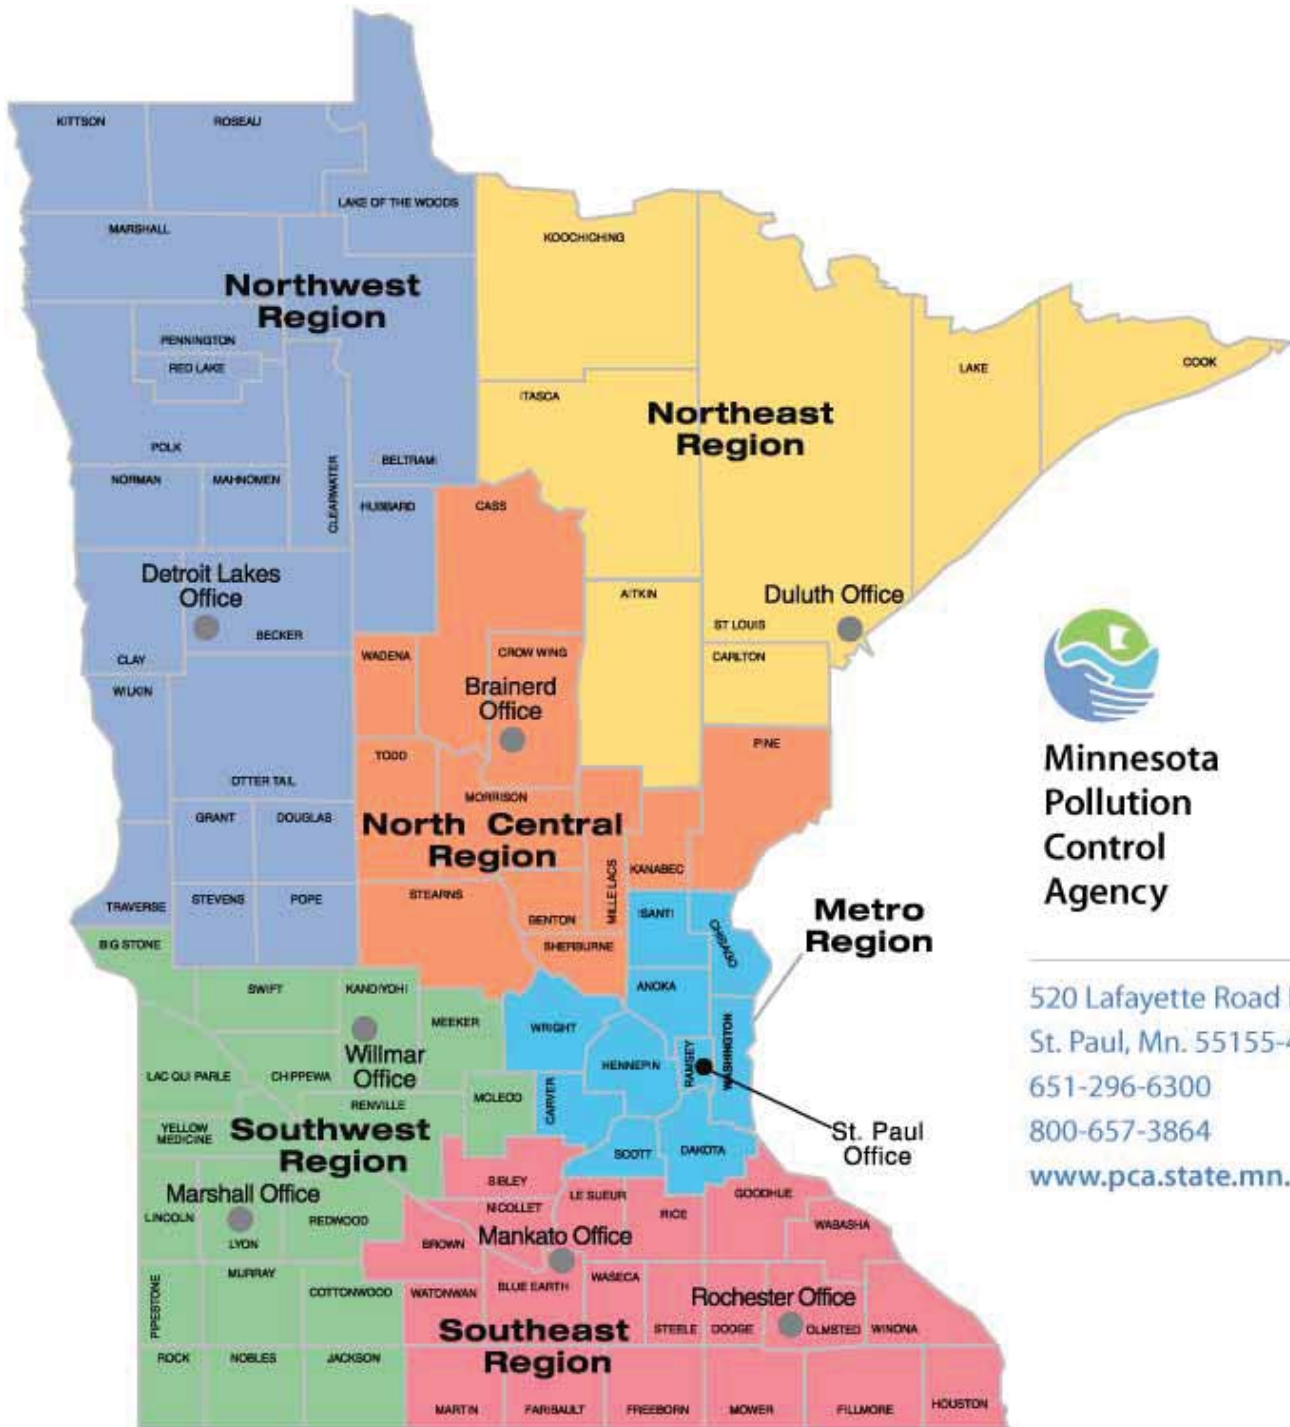

**Minnesota
Pollution
Control
Agency**

520 Lafayette Road North
 St. Paul, Mn. 55155-4194
 651-296-6300
 800-657-3864
www.pca.state.mn.us

Minnesota PCA District office contacts

Brainerd:

7678 College Road
Suite 105
Baxter, MN 56425
218-828-2492
800-657-3864
Fax: 218-828-2594

Detroit Lakes:

714 Lake Ave.
Suite 220
Detroit Lakes, MN 56501
218-847-1519
800-657-3864
Fax: 218-846-0719

Duluth:

525 Lake Ave. S.
Suite 400
Duluth, MN 55802
218-723-4660
800-657-3864
Fax: 218-723-4727

Mankato:

12 Civic Center Plaza
Suite 2165
Mankato, MN 56001
507-389-5977
800-657-3864
Fax: 507-389-5422

Marshall:

504 Fairgrounds Rd
Suite 200
Marshall, MN 56258
507 537-7146
800-657-3864
Fax: 507 537-6001

Rochester:

18 Wood Lake Drive SE
Rochester, MN 55904
507-285-7343
800-657-3864
Fax: 507-280-5513

St. Paul:

520 Lafayette Road N
St. Paul, MN 55155-4194
651-296-6300
800-657-3864,
TTY: use your preferred
telecommunications relay service.

Willmar:

1601 Highway 12 East
Suite 1
Willmar, MN 56201-6002
320-214-3786
800-657-3864
Fax: 320-214-3787

Fond du Lac Line 4 Project

Application for Pipeline Routing Permit and Partial Exemption

Minnesota Public Utilities Commission

Appendix F

Unanticipated Discoveries Plan

TABLE OF CONTENTS

1.0 INTRODUCTION..... 1
2.0 UNANTICIPATED DISCOVERY CONDITIONS 1
3.0 DISCOVERY OF HISTORIC PROPERTIES..... 2
 3.1 FEDERAL AGENCY JURISDICTION..... 3
 3.2 STATE LANDS..... 4
 3.3 PRIVATE LANDS SUBJECT TO STATE ROUTING AUTHORITY
 JURISDICTION 4
4.0 DISCOVERY OF HUMAN SKELETAL REMAINS 5
5.0 TRAINING OF CONSTRUCTION PERSONNEL..... 5

APPENDICES

- Appendix A – Contact Lists
- Appendix B – Unanticipated Discovery Flow Charts

ACRONYMS AND ABBREVIATIONS

ACHP	Advisory Council on Historic Preservation
CFR	Code of Federal Regulations
EI	Environmental Inspector
Enbridge	Enbridge Energy, Limited Partnership
MIAC	Minnesota Indian Affairs Council
Minn. Stat.	Minnesota Statute
NPS	National Park Service
NRHP	National Register of Historic Places
OSA	Office of the State Archaeologist
Project	Fond du Lac Line 4 Project
RFA	Responsible Federal Agency
SHPO	State Historic Preservation Office
TCP	Traditional Cultural Property
TCR	Traditional Cultural Resources
THPO	Tribal Historic Preservation Office
UDP	Unanticipated Discoveries Plan
USACE	United States Army Corps of Engineers

DEFINITIONS

“Consulting Tribe,” means a Tribe included in the National Historic Preservation Act Section 106 consultation for this Project.

“Enbridge Environmental Department”, means a member of the Enbridge Environmental Compliance Management Team responsible for ensuring compliance with environmental permit conditions and company commitments during construction.

“Enbridge Lead Environmental Inspector”, means the individual responsible for implementing the various environmental requirements within the given construction area.

“Traditional Cultural Properties” (“TCPs”), means a subtype of historic properties recognized as eligible for listing on the Minnesota State and/or NRHP, as further defined in National Register Bulletin #38, “Guidelines for Evaluating and Documenting Traditional Cultural Properties” and other federal guidance.

“Traditional Cultural Landscapes,” means a subtype of historic properties recognized as eligible for listing on the Minnesota State and/or NRHP, as further defined by National Park Service Preservation Brief 36, “Protecting Cultural Landscapes: Planning, Treatment and Management of Historic Landscapes” and other federal guidance.

“Traditional Cultural Resources Survey” (“TCR”) Survey, which will be conducted in accordance with existing state and federal guidance and requirements, is intended to comply with the Enbridge’s federal, state, and contracted obligations to conduct a survey of tribal historic properties and other cultural resources that may be affected by the Project, and must include: field surveys to identify Tribal Sites along the entire length of any approved route that identify (preserving confidentiality of sites) (sic); literature review; the results of Tribal consultation; and other matters.

“Cultural Resources,” is an umbrella term to refer to all historic properties of importance to tribes (including but not limited to both TCPs and Traditional Cultural Landscapes) and any other cultural resources of importance to tribes.

“Third Party Cultural Resource Monitor,” means a monitor the Permittee hires to address concerns related to observed or suspected Archeological and Cultural Resources or human remains.

“Tribe,” means a federally recognized Indian tribe.

1.0 INTRODUCTION

Enbridge Energy, Limited Partnership (“Enbridge”) is proposing to construct the Fond du Lac Line 4 Project, a project that would relocate approximately 10 miles of Line 4 pipeline within the Fond du Lac Reservation in St. Louis and Carlton Counties, Minnesota (“the Project”).

This Unanticipated Discoveries Plan (“UDP”) sets forth the guidelines to be used in the event archaeological resources (includes both prehistoric and historical resources) or human skeletal remains are discovered during construction activities. These measures were developed by Enbridge in accordance with applicable state and federal guidelines. Early and frequent communications are essential in meeting both the spirit and law of those guidelines; therefore, Appendix A shows the most current list of relevant contacts in the event of an unanticipated discovery during construction.

2.0 UNANTICIPATED DISCOVERY CONDITIONS

Pipeline construction excavations have the potential to uncover previously unknown archaeological sites and human skeletal remains, as well as many other cultural and natural elements such as modern refuse and faunal remains. While extensive environmental surveys can effectively eliminate most discoveries during construction, Enbridge is aware that project planning should anticipate even the remote possibility of a discovery.

Third Party Cultural Resource Monitors required by Fond du Lac for work on the Reservation (“Monitor”) and the Enbridge Lead Environmental Inspector (“Lead EI”) will have the primary responsibility of initially distinguishing discoveries of significant archaeological and cultural resource sites or human skeletal remains from those that are neither. The unanticipated discovery of significant archaeological and cultural resource sites and human skeletal remains would require ceasing construction activities at the find location followed by a coordinated consultation effort among Enbridge, permitting agencies, landowners, and the Fond du Lac tribe. In the event that a suspected discovery is determined not to involve a significant archaeological or cultural resource site or human skeletal remains, construction would resume and there would be no need of the consultation process as outlined above; however, documentation of the event must be made and can include notes, photographs, and drawings as appropriate.

When possible archaeological and cultural materials or suspected human skeletal remains are identified during ground disturbing activities within the construction corridor, the Monitor and the Lead EI will be notified immediately of the discovery.

1. Immediately following notification of the discovery, the Lead EI shall:
 - (a) Establish and delineate a 25-foot buffer around the edge of the discovery (using flagging and/or fencing), advise the on-site construction manager to halt all ground-disturbing activities within the buffered area until otherwise notified by Enbridge Environment, and implement measures to protect the discovery from looting and vandalism, including a 24-hour watch, if necessary; and
 - (b) Contact a qualified Professional Archaeologist (possible archaeological materials) meeting the Professional Qualification Standards of the Secretary of Interior as stated in Title 48 Federal Regulation 44716 (“48 FR 44716”) and/or Physical Anthropologist (suspected human skeletal remains) with a graduate degree in said

- discipline and a recognized body of work in the professional community, to conduct an assessment of the discovery. The Professional Archaeologist should meet the qualification standards outlined in 36 Code of Federal Regulations (“CFR”) Part 61 in order to conduct the assessment. The Physical Anthropologist must be acknowledged as competent to positively identify human skeletal remains during the initial event of their discovery. As indicated below, this individual will work closely with the OSA who has the statutory responsibility to authenticate human burials in Minnesota.
2. When contacted by the Lead EI, the Professional Archaeologist shall gather additional information from the discovery area and assess the potential significance and condition and integrity of the discovery according to the guidelines established by the National Park Service (“NPS”) in Bulletin 15 and its amendments:
 - (a) The Professional Archaeologist will determine whether-or-not the discovery is an archaeological site or cultural resource over 45 years of age. If the discovery is an archaeological site or cultural resource greater than 45 years of age, the Professional Archaeologist will record as much information as possible to secure a Smithsonian Trinomial Number from the appropriate state agency. The Lead EI would then notify Enbridge Environment to initiate the process outlined in Section 3.0 below.
 - (b) If the discovery is not an archaeological site or cultural resource greater than 45 years of age, the Professional Archaeologist will document the discovery for the record and Enbridge’s lead EI will advise the on-site construction manager to restart ground-disturbing activities.
 3. When contacted by the Lead EI, the Physical Anthropologist shall investigate the site to make an assessment of the likely nature of the remains:
 - (a) If the remains are likely human, then the Lead EI would notify the Enbridge Environmental Department (“Enbridge Environment”) to initiate the process outlined in Section 4.0 below as they have access to multiple forms of communication to quickly follow the procedures outlined in this plan.
 - (b) If the discovery does not represent human skeletal remains, the Physical Anthropologist will document the discovery for the record and Enbridge’s Lead EI will advise the on-site construction manager to restart ground-disturbing activities.

3.0 DISCOVERY OF HISTORIC PROPERTIES

Upon the discovery of an archaeological site or cultural resource greater than 45 years of age, the Professional Archaeologist will advise Enbridge Environment of the proper agency notification procedure and recommend a plan of action for the discovery area.

- (a) If the discovery area is under the jurisdiction of a federal permit and/or approval, or otherwise subject to federally mandated conditions, Enbridge Environment will advise the Responsible Federal Agency (“RFA”) of the resource and provide information regarding its significance and condition and integrity (see Section 3.1 below).

- (b) If the discovery is on state land, Enbridge Environment will first advise the land-managing agency of the resource and provide information regarding its significance, condition and integrity and, if directed by the land-managing agency, advise the appropriate State Archaeologist or Tribal Archaeologist (see Section 3.2 below).
- (c) If the discovery is on private land, its disposition will still be subject to the authority of the appropriate state routing agency. Enbridge Environment will advise the state routing agency of the resource and provide information regarding its significance, condition and integrity (see Section 3.3 below).

3.1 FEDERAL AGENCY JURISDICTION

- (a) Enbridge Environment will notify the RFA of the resource and provide information regarding its significance and condition and integrity.
- (b) Within 24 hours of notification, the RFA shall provide notice of the discovery to other parties who may wish to participate in consultation, including but not limited to the appropriate Fond du Lac tribal official (Tribal Historic Preservation Office [“THPO”]), state routing authority, state agencies (such as the MPUC), land-managing agencies, or private landowner(s), as applicable. After 24 hours, consultation for eligibility and effect with continue in order for avoidance and mitigation options to be developed.
- (c) The RFA shall have 5 calendar days following notification to determine the discovery’s eligibility for listing on the National Register of Historic Places (“NRHP”) in consultation with the appropriate THPO and other consulting parties. The RFA may extend the review period by an additional 7 calendar days by providing written notice to consulting parties prior to the expiration of the 5-day calendar period. The RFA shall provide Enbridge Environment with avoidance or mitigation treatment options by the end of the 5-day period.
- (d) For properties determined eligible for listing on the NRHP pursuant to (c) above, Enbridge Environment shall notify the RFA and other consulting parties of Enbridge’s proposed treatment measures to resolve adverse effects to the discovered resource. The consulting parties shall comment on the proposed treatment measures within 48 hours. The RFA shall ensure that the recommendations of the consulting parties are considered prior to granting approval of Enbridge-proposed treatment measures. Once approval has been granted by the RFA, Enbridge Environment shall carry out the approved treatment measures and, after doing so, Enbridge may resume construction.
- (e) In the event of any disagreements between the consulting parties regarding the NRHP eligibility of the newly discovered property or the treatment measures proposed to mitigate adverse effects to the property, the RFA shall seek and take into account the recommendations of the Advisory Council on Historic Preservation (“ACHP”). Within 48 hours of receipt of a request, ACHP shall provide the RFA with recommendations on how to resolve the dispute.
- (f) If, after consultation, the RFA determines that the discovery does not represent an NRHP-eligible resource, the RFA will direct Enbridge Environment to resume ground-disturbing activities at the discovery location at its discretion.

3.2 STATE LANDS

- (a) Enbridge Environment will notify the land-managing agency of the resource and provide information regarding its significance and integrity. If directed by the land-managing agency to do so, Enbridge Environment will advise the appropriate State Archaeologist and/or Tribal Archaeologist. The State/Tribal Archaeologist has the discretion to notify Native American tribal officials, state routing authority, and other state agencies as appropriate.
- (b) The land-managing agency will have 5 calendar days following notification to consult with the appropriate state archaeologist and other consulting parties, as necessary, about the assessment of the discovery to determine its eligibility, avoidance, and/or mitigation measures. NPS criteria of eligibility for listing on the NRHP may be considered as a guideline to determine the significance of the find and SHPO may be consulted during the assessment, but the state agency is not obliged to apply NPS standards in making its decision. The land-managing agency may assume the resource is eligible for listing on the NRHP while consultation occurs and may require avoidance, impact minimization, or mitigation. The land-managing agency shall provide Enbridge Environment with avoidance or mitigation treatment options by the end of the 5-day period.
- (c) For properties determined eligible for listing on the NRHP, Enbridge Environment shall notify the land-managing agency and other consulting parties of the treatment measures it proposes for resolving adverse effects to the resource. The consulting parties shall provide their views on the proposed treatment measures to Enbridge Environment, the land-managing agency and other consulting parties within 48 hours. The land-managing agency shall ensure that the recommendations of the consulting parties are considered prior to granting approval of Enbridge's proposed treatment measures. Once approval has been granted by the land-managing agency, Enbridge Environment shall carry out the approved treatment measures and, after doing so, Enbridge may resume construction.
- (d) If, after consultation, the land-managing agency determines that the discovery does not represent an NRHP-eligible or otherwise important resource, the land-managing agency will direct Enbridge Environment to resume ground-disturbing activities, at its discretion, at the discovery location.

3.3 PRIVATE LANDS SUBJECT TO STATE ROUTING AUTHORITY JURISDICTION

- (a) Enbridge Environmental Department will notify the state routing authority of the resource and provide information regarding its significance and integrity.
- (b) Within 24 hours of notification, the state routing authority shall provide notice of the resource to other parties, including, but not limited to, the appropriate THPO, the appropriate State Archaeologist, Native American tribal officials, state agencies, and private landowner(s), as applicable to comply with the permit and to notify the parties that the resource requires determinations of eligibility and effect in order to develop avoidance and/or mitigations options.
- (c) The state routing authority will have 5 calendar days following notification to consult with the appropriate SHPO and other consulting parties, as necessary, about assessing the

discovery. Criteria for eligibility for listing on the NRHP may be considered as a guideline to determine the significance of the find and THPO may be consulted during the assessment, but the state routing authority is not obliged to apply the standards in making its decision. The state routing authority may assume the resource is eligible for listing on the NRHP while consultation occurs and may require avoidance, impact minimization, or mitigation. Construction may not resume until the appropriate THPO or other consulting parties have developed avoidance or mitigation strategies and notified Enbridge Environment. The state routing authority shall provide Enbridge Environment with avoidance or mitigation treatment options by the end of the 5-day period.

- (d) For properties eligible for listing on the NRHP, Enbridge Environment shall notify the state routing authority and other consulting parties of the treatment measures it proposes to resolve impacts to the resource. The consulting parties shall provide their views on the proposed treatment measures within 48 hours. The state routing authority shall ensure that the recommendations of the consulting parties are considered prior to granting approval of Enbridge's proposed treatment measures. Once approval has been granted by the state routing authority, Enbridge Environment shall carry out the approved treatment measures and, after doing so, Enbridge may resume construction.
- (e) If, after consultation, the state routing authority determines that the discovery does not represent an NRHP-eligible or otherwise important resource, the state routing authority will direct Enbridge Environment to resume ground-disturbing activities, at its discretion, at the discovery location.

4.0 DISCOVERY OF HUMAN SKELETAL REMAINS

1. When unmarked human burial or skeletal remains are encountered during construction activities, Enbridge will comply with Minnesota's "Private Cemeteries Act" (Minnesota Statute ["Minn. Stat."] §307.08).
2. In the event a human burial or skeletal remains are encountered during ground-disturbing construction activity, all construction shall immediately cease in the vicinity, and Enbridge Environment will implement the State-mandated notification procedure in Minnesota by notifying the local law enforcement agency (county sheriff). As required by Minn. Stat. §307.08 Enbridge Environment will also notify the Office of the State Archaeologist ("OSA") and Tribal Archaeologist of the find.
3. Enbridge Environment also shall promptly notify the RFA, land-managing agency, or state routing authority of the find and consult regarding the appropriate measures to handle the discovery.

After permission to resume construction has been issued by the RFA, land-managing agency, or state routing authority, Enbridge's Lead EI will advise the on-site construction manager to restart ground-disturbing activities.

5.0 TRAINING OF CONSTRUCTION PERSONNEL

Prior to construction, Enbridge will train workers about the need to avoid archaeological, historic and cultural properties, how to identify archaeological, historic, and cultural properties, and procedures to follow if undocumented archaeological, historic and cultural properties, including human burials and gravesites, are found during construction.


Appendix A
Contacts List

Contact List		
State/County/Agency	Contact	Address/Telephone
FEDERAL		
U.S. Army Corps of Engineers	Brad Johnson, St. Paul District Archaeologist	Contact info U.S. Army Corps of Engineers Centre 180 5 th Street East St. Paul, MN 55101-1638 Telephone: (651) 290-5201 E-mail: brad.a.johnson@usace.army.mil
U.S. Army Corps of Engineers	Nancy Komulainen-Dillenburg, St. Paul District Archaeologist	Contact info U.S. Army Corps of Engineers Centre 180 5 th Street East St. Paul, MN 55101-1638 Telephone: (651) 290-5201 E-mail: Nancy.S.Komulainen-Dillenburg@usace.army.mil
Bureau of Indian Affairs	Richard Berg, Midwest Regional Office Archaeologist	Contact info 5600 American Blvd W, Ste 500 Bloomington, MN 55437 Telephone: (612) 713-4400, ext. 1145 E-mail: richard.berg@bia.gov
Fond du Lac Band of Lake Superior Chippewa Reservation Business Committee ("RBC")	Kevin DuPuis, Chairman	1720 Big Lake Road, Cloquet, MN 55720 Telephone: (218) 879-4593 Fax: (218) 879-4146 E-mail: kevindupuis@fdlrez.com
Fond du Lac Band of Lake Superior Chippewa Tribal Historic Preservation Officer ("THPO")	Jill Hoppe, THPO	1720 Big Lake Road, Cloquet, MN 55720 Telephone: (218) 878-7124 E-mail: JillHoppe@fdlrez.com
Minnesota Indian Affairs Council	Melissa Cerda, Cultural Resource Director	161 St. Anthony Ave, Suite 919 St. Paul, MN 55103 Telephone: (651) 276-2797 E-mail: melissa.cerda@state.mn.us
MINNESOTA		
Enbridge	TBD, Lead Environmental Inspectors	Cellphone: TBD E-mail: TBD
Minnesota State Historic Preservation Office	Amy Spong, Deputy SHPO	Minnesota State Historic Preservation Office Minnesota Historical Society 345 Kellogg Boulevard West St. Paul, MN 55102-1903 Telephone: (651) 259-3466 E-mail: amy.spong@mnhs.org
Office of the State Archaeologist	Amanda Gronhovd, Minnesota State Archaeologist	Office of the State Archaeologist Fort Snelling History Center 200 Tower Avenue St. Paul, MN 55111 Telephone: (612) 725-2411 E-mail: Amanda.Gronhovd@state.mn.us
Minnesota Geological Survey	Harvey Thorleifson, Director	Minnesota Geological Survey 2642 University Ave. St. Paul, MN 55114-1057 Telephone: (612) 627-4780, ext. 224
Minnesota Department of Natural Resources	TBD	500 Lafayette Rd., St. Paul, MN 55155 Telephone: E-mail:
Minnesota Public Utilities Commission	TBD	121 7th Place E, Suite 350 Saint Paul, MN 55101 Telephone: E-mail:


Contact List		
State/County/Agency	Contact	Address/Telephone
St. Louis	Ross Litman, County Sheriff	100 N 5th Avenue W Room 103 Duluth, MN 55802 Telephone: (218) 726-2340
Carlton	Kelly Lake, County Sheriff	317 Walnut Avenue Carlton, MN 55718 Telephone: (218) 384-3236

Appendix B
Unanticipated Discovery Flow Charts

Discovery of Historic Properties Flow Chart

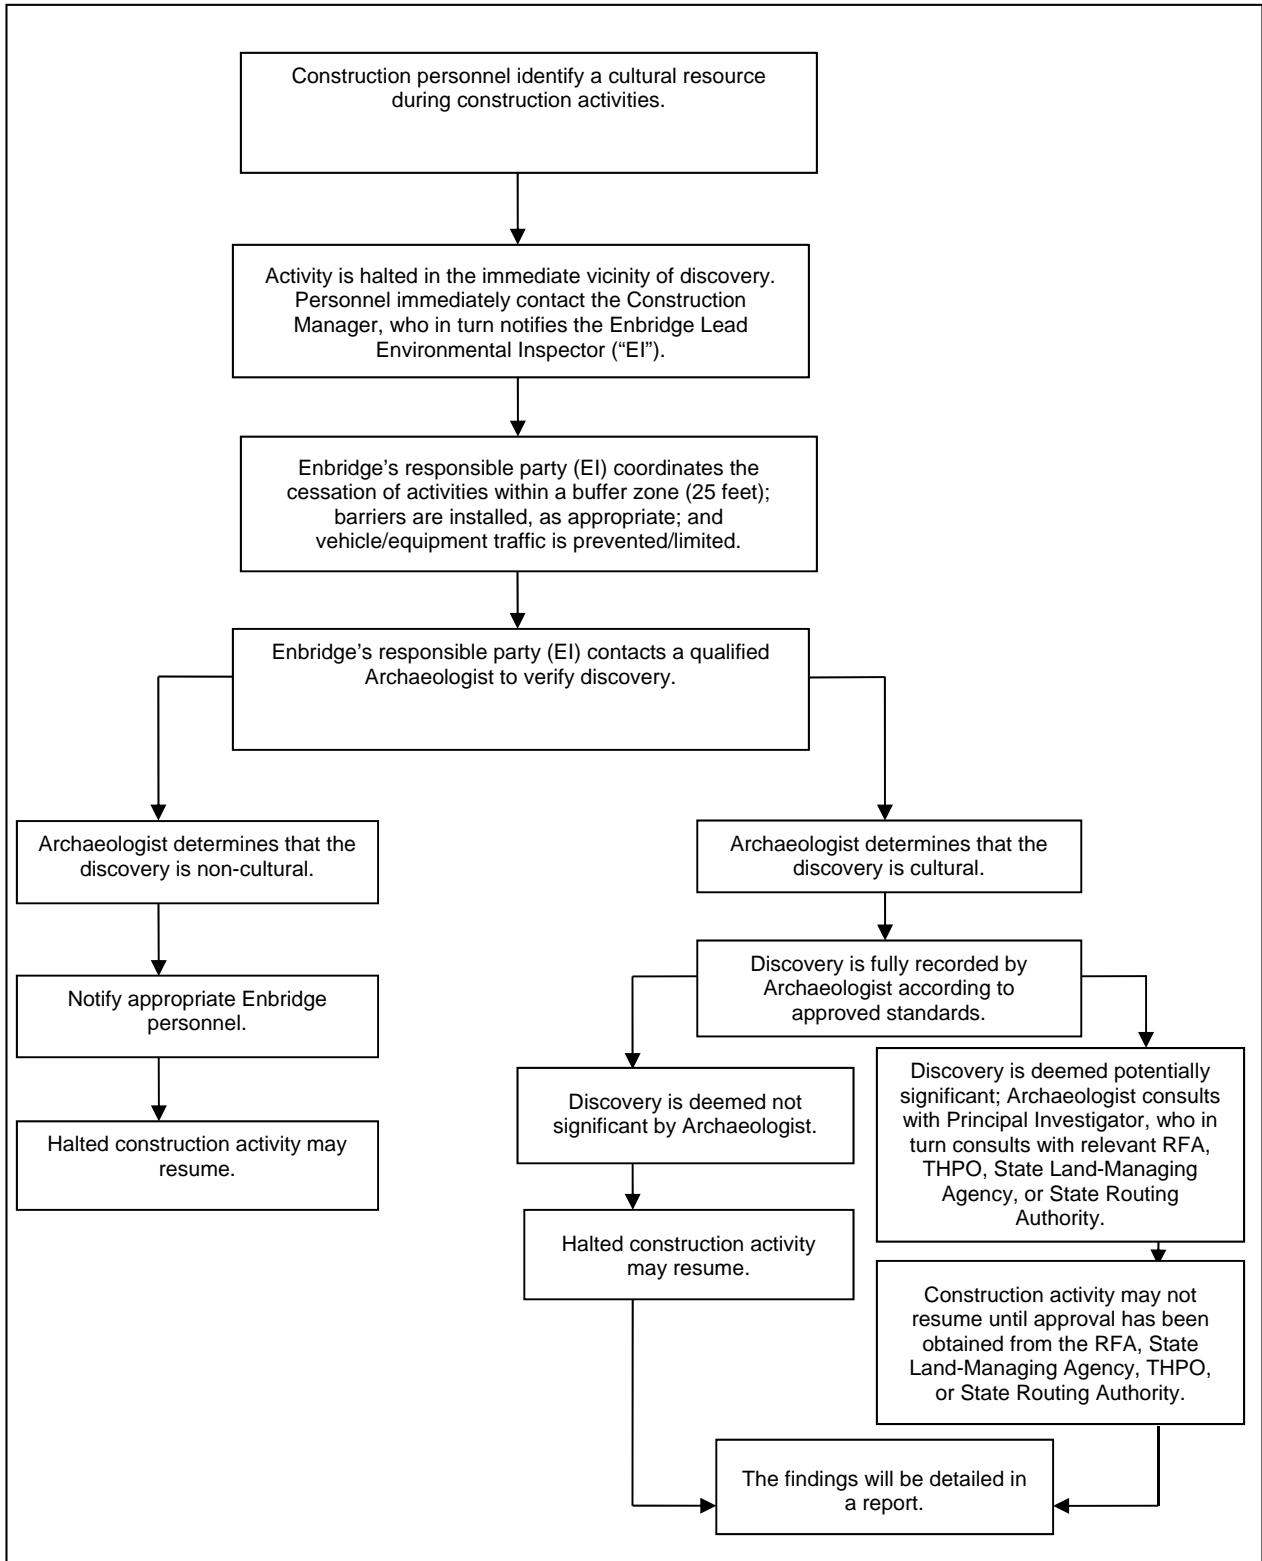

Unanticipated Discovery of Human Remains Flow Chart

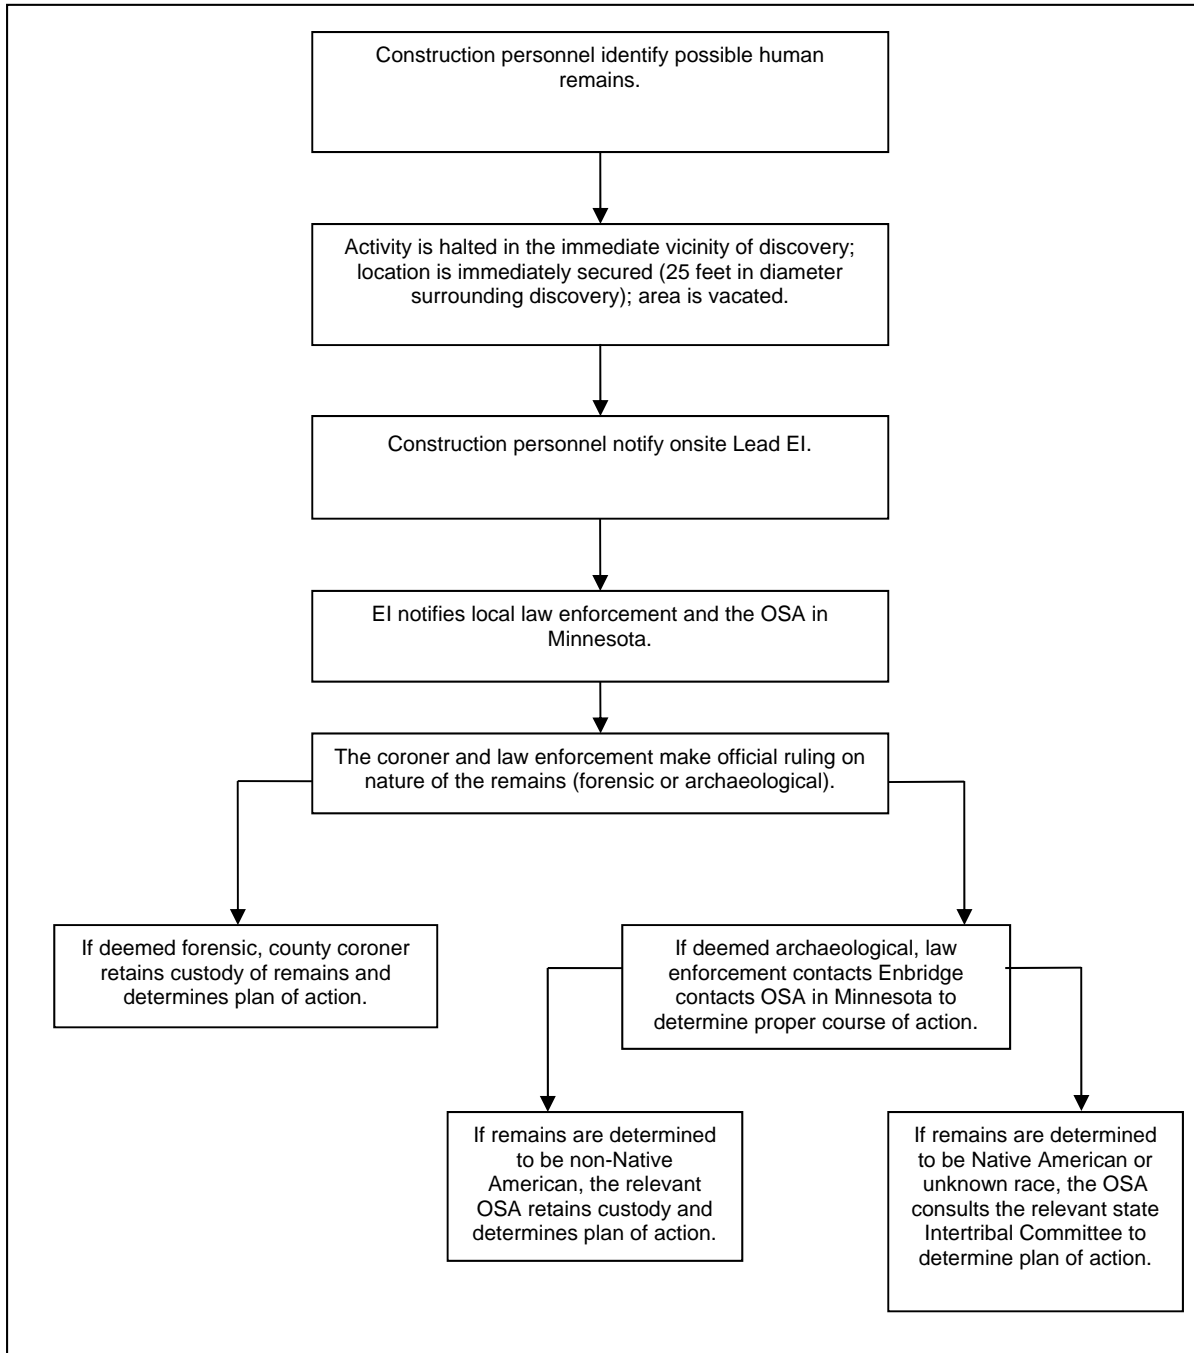

Fond du Lac Line 4 Project

Application for Pipeline Routing Permit and Partial Exemption

Minnesota Public Utilities Commission

Appendix H

Contaminated Sites Management Plan



Contaminated Sites Management Plan

Enbridge Energy, Limited Partnership • Fond du Lac Line 4 Project

TABLE OF CONTENTS

1.0 INTRODUCTION..... 1
2.0 APPLICABILITY 1
 2.1 CONTAMINATED MATERIAL..... 1
 2.1.1 Known..... 1
 2.1.2 Unknown..... 2
 2.2 OTHER MATERIAL..... 2
 2.3 PROJECT RELATED SPILLS..... 2
3.0 ROLES AND RESPONSIBILITIES..... 2
 3.1 PROJECT TEAM..... 2
 3.1.1 Enbridge Major Projects Environmental Staff 3
 3.1.2 Environmental Inspector..... 3
 3.1.3 Enbridge Liquid Pipelines Environmental Staff..... 3
 3.1.4 Chief Inspector..... 4
 3.1.5 Project Contractor..... 4
4.0 PROJECT CONTRACTOR RESPONSE ACTIONS..... 4

List of Tables

Table 1 Known Potential Contaminated Sites (to be completed prior to construction)
Table 2 Contaminated Material Disposal Facilities (to be completed prior to construction)

List of Figures

Figure 1 Route Overview
Figure 2 Known Potential Contaminated Sites (to be developed prior to construction)

APPENDICES

Appendix A – Contact List
Appendix B – Environmental Inspector Contaminated Site Response Form
Appendix C – Site Investigation Field Sampling and Screening Log
Appendix D – Contaminated Materials Management Flowchart

1.0 INTRODUCTION

This Contaminated Sites Management Plan (“CSMP”) has been prepared by Enbridge Energy, Limited Partnership (“Enbridge”) for the Fond du Lac Line 4 Project (“Project”) that will take place within the Fond du Lac Reservation in Minnesota. The proposed Project Preferred Route is shown on Figure 1. The purpose of the CSMP is to present guidance to Contractors for managing contaminated soil, water, debris or other materials which may be encountered during Project work based on the applicability described below. This CSMP does not address potential contractor safety requirements that may apply when managing contaminated materials.

2.0 APPLICABILITY

This CSMP applies to contaminated material that may be encountered along the Project Preferred Route as a result of activities or events that occurred prior to the Project commencing (i.e., historical). Contamination may be caused by petroleum products, agricultural chemicals, asbestos, or other industrial byproducts that are present as a result of historical activities or events whether known or unknown.

2.1 CONTAMINATED MATERIAL

For the purpose of this CSMP, “contaminated material” has one or more of the following characteristics:

- Petroleum odors in soil or water
- Petroleum staining in soil or on vegetation
- Petroleum free product or sheen (e.g., rainbow or bluish colors) on water, soil, or debris surfaces
- Evidence of improper waste disposal such as industrial garbage, scrap materials, used containers, or other by-product type wastes
- Evidence of man-made earthen features (hills, depressions, waste piles, etc.)
- Evidence of dumping or other waste disposal
- Vegetation that is stressed or dead
- Soil that is discolored compared to adjacent or nearby soils
- Evidence of present or past chemical storage or use, including tanks, drums or containers
- Buildings or structures that suggest current or past industrial activity
- Evidence of land use associated with potential contamination (landfills, waste treatment plants, agricultural pesticide storage facilities, storage ponds, septic fields, drains, culverts, etc.)

2.1.1 Known

Enbridge will conduct a review of data and information to identify sites with the potential to encounter contaminated material within 1,200 feet of the Project Preferred Route. If any sites with historical documentation of contaminated material are identified, they will be listed in Table 1, and locations will be shown on Figure 2.

2.1.2 Unknown

It is possible that contaminated material may be encountered unexpectedly at locations along the Preferred Route where no historical information was available. Such locations will be considered previously unknown sites this CSMP will apply to such sites.

2.2 OTHER MATERIAL

Material such as debris (e.g., common household waste, construction debris, old appliances, etc.) with no apparent signs of contamination may be encountered during the Project. The material will not be considered contaminated and will not be managed as part of this CSMP.

In addition, natural organic (i.e., biogenic) sheens where the Project route crosses wetlands, ditches, or other water-saturated surfaces may be encountered. A biogenic sheen can often be identified by breaking up the sheen with a stick and observing the sheen behavior. If the sheen remains broken into platelets and fails to re-coalesce quickly, it may be considered natural and not a source of hydrocarbon contamination. If the sheen quickly reforms or exhibits a typical rainbow petroleum-type sheen on the surface of the water, then the material will be considered contaminated.

Additional assessment will be conducted as explained in Section 4 if there is any doubt as to whether material encountered is contaminated.

2.3 PROJECT RELATED SPILLS

Contaminated material that is generated during the Project as a result spills that occur during construction (e.g., equipment releases) will be managed in accordance with Enbridge's Environmental Protection Plan which has been developed separate from this CSMP.

3.0 ROLES AND RESPONSIBILITIES

The following section provides a summary of roles and responsibilities as they pertain to contaminated site management during the Project. Enbridge is committed to achieving a high standard of environmental protection and is committed to the proper management of unanticipated environmental conditions, including contamination.

Enbridge's expectations for work during the Project include conducting all work activities safely and effectively while complying with regulations.

3.1 PROJECT TEAM

Multiple parties will be working together to ensure the Project is executed according to scope. The parties expected to have a major role in maintaining environmental compliance and proper management of contaminated materials are Enbridge, its Contractors, and other stakeholders. Contact information for key personnel is included in the attached Contact List (Appendix A).

3.1.1 Enbridge Major Projects Environmental Staff

The responsibilities of Enbridge Major Projects Environmental Staff associated with this project include:

- manage environmental permit compliance during the Project (does not include in-depth management of contaminated sites);
- serve as the interface between the Project Engineering staff, contractors, and the Liquid Pipelines Environmental Staff;
- oversee site-specific management and disposal of contaminated material that may be encountered during the Project; and
- track Project progress and advise Enbridge's Liquid Pipelines Environmental Staff if contamination is encountered at any given location.

3.1.2 Environmental Inspector

Environmental Inspectors on the Project are considered Enbridge Major Projects Environmental Staff and the responsibilities of the Environmental Inspectors include:

- maintain overall environmental permit compliance during the Project (does not include comprehensive management of contaminated materials);
- serve as an on-site point of contact in the field during the Project;
- provide an initial assessment and on-site guidance regarding contamination or suspected contamination; and
- complete the attached Environmental Inspector Contaminated Site Response Form (Appendix B) when contamination or suspected contamination is encountered during the Project.

3.1.3 Enbridge Liquid Pipelines Environmental Staff

The responsibilities of Enbridge Liquid Pipelines Environmental Staff associated with this project include:

- direct activities specifically associated with the CSMP for the Project;
- serve as the primary point of contact with regulators when addressing contaminated sites;
- provide advance notice to applicable regulatory agencies during the Project when excavation activities are within one day of a location of a known potentially contaminated site;
- oversee site-specific management and disposal of contaminated materials that may be encountered during the Project;
- document conditions at contaminated sites using appropriate field screening and analytical sampling methods (including completing Appendix C, Site Investigation Field Sampling and Screening Log);
- maintain a database of contaminated sites encountered during the Project;

- manage records associated with contaminated material management and disposal; and
- prepare site-specific memorandums and a final report of findings for sites addressed under the CSMP during the Project.

3.1.4 Chief Inspector

The Chief Inspector reports directly to Enbridge and the responsibilities of the Chief Inspector include:

- notify the Enbridge Major Projects Environmental Staff when Project activities involving ground disturbance are two days out from work commencing at known potentially contaminated sites; and
- provide initial notification to the Enbridge Environmental Inspector upon discovery of any type of contamination at a site regardless of whether it is previously known or newly discovered (i.e., unknown site).

3.1.5 Project Contractor

Project Contractor reports to the Chief Inspector and the responsibilities of the Project Contractor include:

- continually evaluate project activities for unanticipated conditions including potential contamination;
- provide the initial report to the Chief Inspector and cease work if contamination is encountered during Project activities; and
- work with Enbridge Liquid Pipelines Environmental Staff to arrange for proper removal, temporary storage/containment, and transport of contaminated materials offsite.

4.0 PROJECT CONTRACTOR RESPONSE ACTIONS

In the event that contaminated soil, water, or debris is encountered, the Project Contractor will take the response actions listed below which are also summarized in the Contaminated Materials Management Flowchart (Appendix D).

1. Cease Work
 - i The Project Contractor will cease work activity in the vicinity of the contamination.
2. Address Safety
 - i The Project Contractor will refer to the Project Safety Plan and consult with Enbridge's Project Safety representatives to determine proper health and safety actions.
3. Notify Enbridge
 - i The Project Contractor will notify the Chief Inspector who will notify Enbridge's Compliance Manager and Enbridge Major Projects Environmental Staff as soon as possible after taking initial safety precautions.

- ii The Major Projects Environmental Staff will notify Enbridge Liquid Pipelines Environmental Staff.
 - iii Enbridge's on-site Environmental Inspector will complete the Environmental Inspector Contaminated Site Response Form (Appendix B) documenting response actions and estimated impacts.
 - iv Enbridge Liquid Pipelines Environmental Staff will make a determination as to whether the contamination is due to an active/ongoing release or a historical release.
4. Prevent Contaminant Migration
- i At the direction of Enbridge's Liquid Pipelines staff, the following actions may be taken:
 - Build earthen dams within the trench to isolate the contamination particularly if water is present; and/or
 - Deploy sorbent pads and booms to remove and isolate petroleum contamination that may be present on water in the trench.
5. Containerize Contaminated Material
- i At the direction of Enbridge's Liquid Pipelines staff, the Project Contractor will segregate contaminated material from clean material to the extent possible. The contaminated material will be clearly labeled with the milepost and date it was removed from the trench. The material will be stored at the job site until disposal at an offsite facility is approved.
 - Contaminated dry soil** and debris will be placed on plastic sheeting or within a roll-off dumpster or other suitable containment structure and covered with plastic sheeting.
 - Contaminated water** that needs to be dewatered from the excavation will be pumped into a frac tank or similar container.
 - The Project Contractor will make reasonable efforts to remove crude oil or other free phase petroleum product from the trench to prevent it from being mixed with containerized water.
 - Free phase petroleum product should be removed with a vac truck or sorbent pads, boom, etc. and stored or contained separately from
 - Contaminated hydrovac slurry and drilling mud** will be placed into a water tight roll-off dumpster or other suitable containment structure and covered.
 - Mud and slurry will be solidified only with approval, and, at the direction of Enbridge Liquid Pipelines Environment Staff.
 - Solidification materials may include dry saw dust wood pellets, Portland cement, bentonite, or other appropriate absorbent material that has been approved by Enbridge Liquid Pipelines Environment Staff.
6. Dispose of the Contaminated Material

- i Enbridge Liquid Pipelines Environment staff may need to collect samples from the contaminated material for waste characterization and disposal purposes.
 - ii Enbridge Liquid Pipelines Environment Staff will identify a proper disposal facility for the contaminated material and provide the Project Contractor with shipping papers for transportation to the disposal facility.
 - iii The Project Contractor will arrange for transportation of contaminated material to one of the disposal facilities listed on Table 2.
 - iv The Project Contractor will maintain records of shipping and waste disposal and provide copies them to the Enbridge Liquid Pipelines Environment Staff.
7. Assist with Environmental Documentation
- i Depending on the characteristics of the contamination encountered, Enbridge Liquid Pipelines Environment Staff may need to collect additional samples from the excavation bottom and sidewalls before backfilling occurs.
 - ii The Project Contractor will assist the Enbridge Liquid Pipelines Environment Staff in this effort.
8. Backfill the trench with clean borrow material
- i Backfill material must be approved by Enbridge Liquid Pipelines Environment Staff.
 - ii Do not backfill with contaminated material.
 - iii Document the source of the backfill material.

Table 1 (to be completed prior to construction)

Table 1

Known Potential Contaminated Sites
 Contaminated Sites Management Plan – Minnesota,
 Fond du Lac Line 4 Project

Site Number	Existing Pipeline Milepost	Site Name	Site Type	Agency Status	Distance to Site (feet)	Direction to Release	Volume (barrels)	Tier

Tier Explanation: 1 = Decent likelihood for encountering contamination during construction
 2 = Moderate likelihood for encountering contamination during construction

**Table 2 Contaminated Material Disposal Facilities (to
be completed prior to construction)**


Table 2

Contaminated Material Disposal Sites
Contaminated Sites Management Plan – Minnesota,
Fond du Lac Line 4 Project

Site Name	Site Address	Phone Number	Material Accepted

Figure 1 Route Overview

REVISED: March 15, 2019

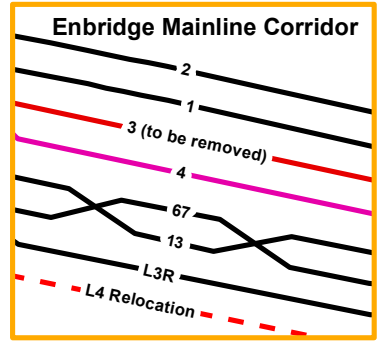


FOND DU LAC


ST. LOUIS COUNTY
CARLTON COUNTY

MP 1060.0

MP 1070.0

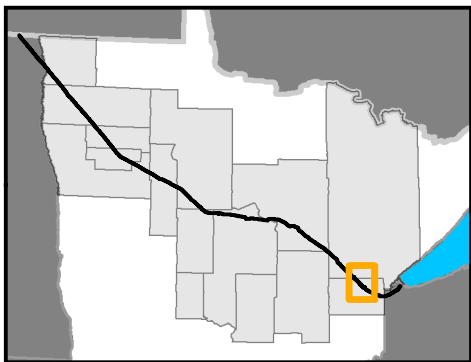

REVISED
03/14/2019



- Line 4 Relocation
- Existing Line 4
- Fond du Lac

TSW
Date: 3/14/2019

Figure 2 (To be developed prior to construction)

Appendix A

Contact List

This page intentionally left blank

**Appendix A
Contact List
Contaminated Sites Management Plan – Minnesota
Fond du Lac Line 4 Project**

Contact	Company	Role	Phone (office)	Phone (cell)	Email
Julianne Motis	Enbridge	Senior Environmental Advisor, Major Projects Environment	218-522-4652	218-409-5239	Julianne.Motis@enbridge.com
Karl Beaster	Enbridge	Senior Environmental Advisor, LP US Environment Operations	218-464-5623	715-718-1040	Karl.Beaster@enbridge.com
		Environmental Inspector TBD			
		Environmental Inspector TBD			
		Chief Inspector TBD			
		Project Contractor TBD			

This page intentionally left blank

Appendix B
Environmental Inspector Contaminated Site Response
Form

This page intentionally left blank

Appendix B
Environmental Inspector Contaminated Site Response Form
Contaminated Sites Management Plan – Minnesota
Fond du Lac Line 4 Project

Name: _____
Date: _____ **Time:** _____
Milepost: _____ **Stationing:** _____

Potential Contamination Observed (check all that apply):

- | | |
|--|--|
| <input type="checkbox"/> Petroleum odors in soil or water
<input type="checkbox"/> Visual petroleum staining in soil or on vegetation
<input type="checkbox"/> Petroleum free product or sheen (e.g., rainbow or bluish colors) on water, soil, or debris surfaces
<input type="checkbox"/> Evidence of improper waste disposal such as industrial garbage, scrap materials, used containers, or other by-product type wastes
<input type="checkbox"/> Presence of man-made hills, depressions, or waste piles or evidence of dumping or other waste disposal
<input type="checkbox"/> Stressed or dead vegetation
<input type="checkbox"/> Soil that is discolored compared to adjacent or nearby soils | <input type="checkbox"/> Evidence of present or past chemical storage or use, including tanks, drums or containers
<input type="checkbox"/> Active or closed buildings and structures that suggest current or past industrial activity
<input type="checkbox"/> Evidence of land use associated with potential contamination (landfills, waste treatment plants, agricultural pesticide storage facilities, storage ponds, septic fields, drains, culverts, etc.)
<input type="checkbox"/> Other (describe)

_____ |
|--|--|

Response Actions

Has containment cell been constructed and lined with plastic? Yes / No
Containment Cell Dimensions (feet):
Quantity of Contaminated Soil Excavated and Stockpiled (cubic yards):

Estimated Impacts

Estimated Extent of Contaminated Soil (horizontal and vertical, in feet):
Has groundwater or surface water been impacted? Yes/No
Describe water impacts (sheen, free oil, etc.):
Nearest surface waterbody (name and distance):

Describe response action activities on reverse.

Appendix B
Environmental Inspector Contaminated Site Response Form
Contaminated Sites Management Plan – Minnesota
Fond du Lac Line 4 Project

Are any impacts observed in the nearest surface water body?

Describe:

Appendix B
Environmental Inspector Contaminated Site Response Form
Contaminated Sites Management Plan – Minnesota
Fond du Lac Line 4 Project

Project Contractor Contaminated Site Response Actions:

This page intentionally left blank

Appendix C

Site Investigation Field Sampling and Screening Log

This page intentionally left blank

Appendix C

Site Investigation and Field Sampling and Screening Log Contaminated Sites Management Plan - Minnesota Fond du Lac Line 4 Project

Milepost: _____ Date: _____
Sampler: _____

Field Investigation Instrument Record: Photoionization detector with 10.6 eV bulb

Sample Nomenclature (Location - sample type - #):

R = Removed S = Sidewall B = Bottom Stockpile = Stockpile

Sample ID	Depth (FT)	Time (military)	Soil Type (USCS)	Color/ Discolor	Odor/ Sheen	Headspace Reading (ppm)
Example: Stockpile-1	4	16:30	CL	Reddish brown	Petroleum/ Rainbow	275

	Calibration	Bump Test 1	Bump Test 2
Time			
Zero reading (ppm)			
Span reading (ppm)			
Background (ppm)			


SITE SKETCH : north arrow, scale, excavation extents & depths, impacted areas, sample locations, borings, wells, structures, utilities, natural features...

This page intentionally left blank

Appendix D
Contaminated Materials Management Flowchart

This page intentionally left blank

Appendix D
Contaminated Materials Management Flowchart
Contaminated Sites Management Plan - Minnesota
Fond du Lac Line 4 Project

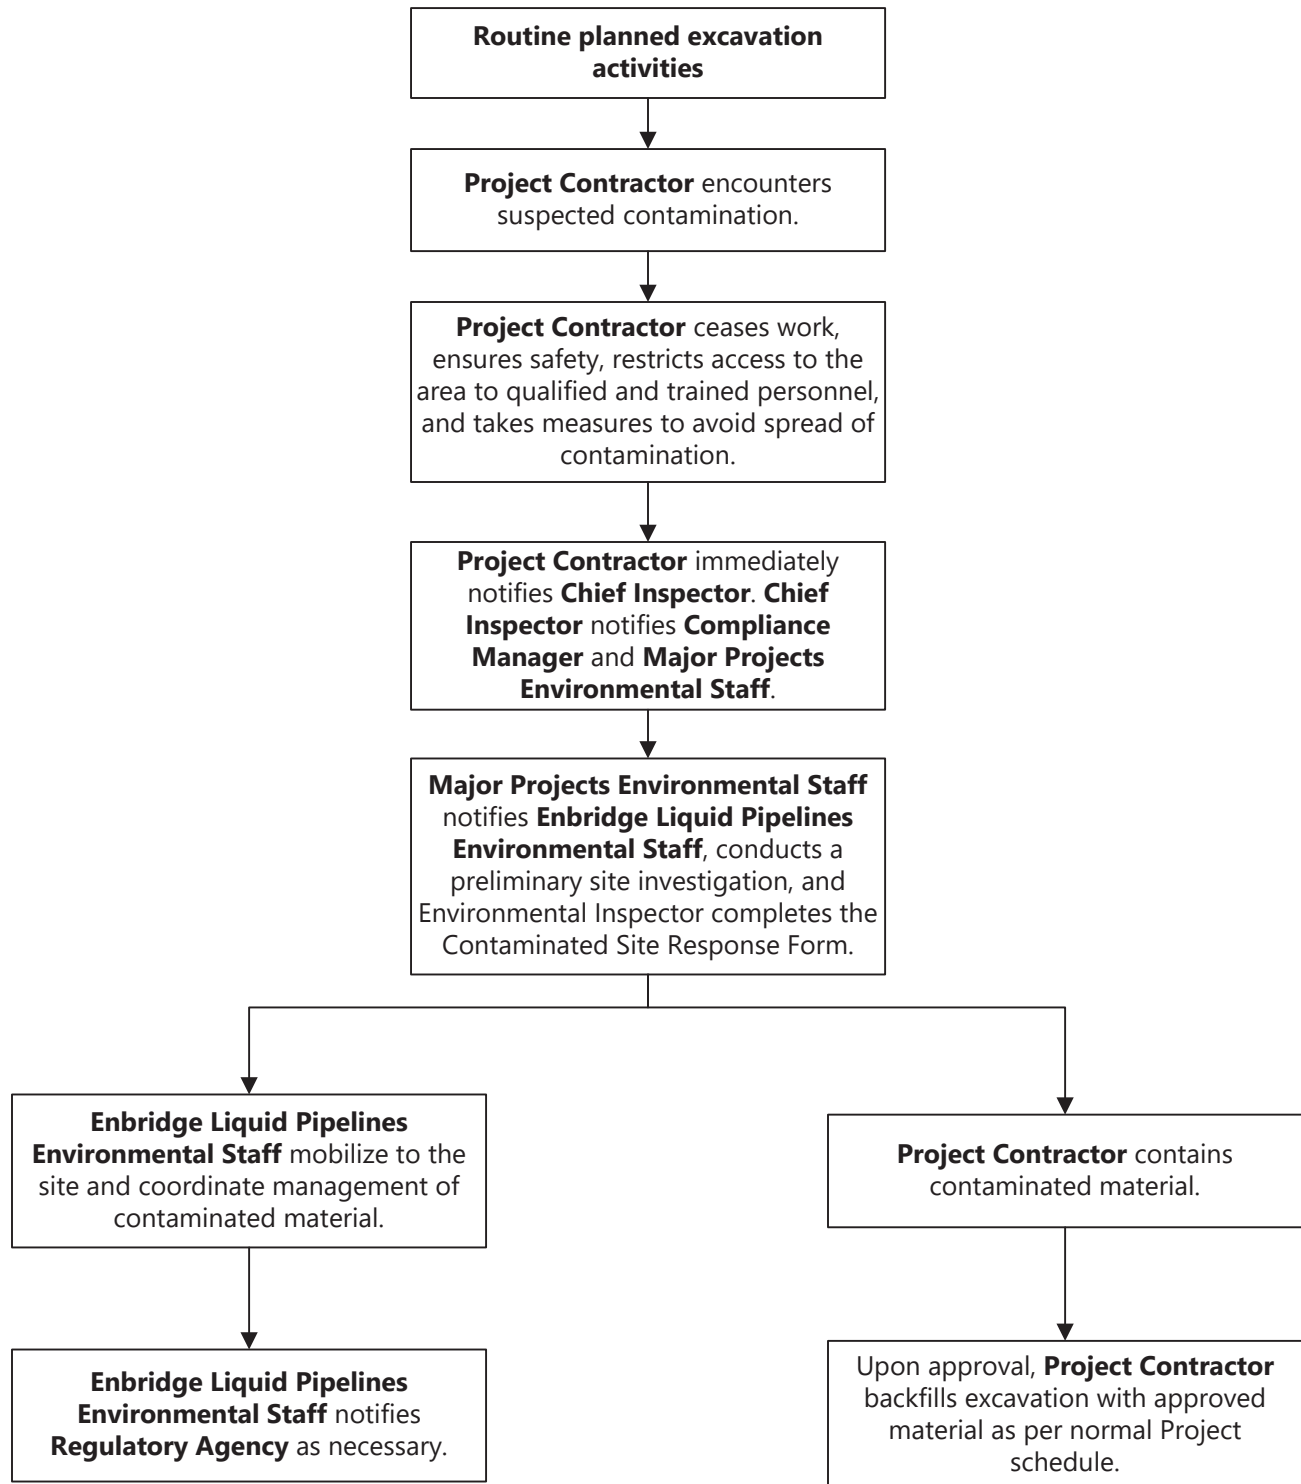

This page intentionally left blank
