



SGS MUSCOWPETUNG

ABORIGINAL CONSTRUCTION MONITORING

WEEKLY REPORT

SPREAD 3

SEPTEMBER 10TH TO SEPTEMBER 16TH, 2018

Social and Cultural Features

Field Observation	# of occurrences	Description and Mitigation Measures	Mitigation Status	Further Action Required (Yes/No)
Traditional Use Area (hunting, fishing, gathering, trapping)	0			
Rock Formations (rocks of significance, tipi rings, etc.)	0			
Artifacts	0			
Bones	0			
Potential Gravesites	0			

Environmental Features

Field Observation	# of occurrences	Description and Mitigation Measures	Mitigation Status	Further Action Required (Yes/No)
Medicinal or Cultural Plants	0			
Aquatic Life	0			
Animal Observations or Burrows	0			
Bird Nests	0			
Trees (Red Willow)	0			
Wetlands	0			
Watercourse Crossing	0			

Additional Observations and Summary of Activities or Concerns

This week we spent our time in spread four again. They are still currently doing machine clean up and spreading of top soil and working their way back towards spread three. The process of final clean is that they de-compact the sub soil with discers and graters and then they pull the second soils in and grade it evenly across the right of way. They pick the rocks and disc it again then they pull in the top soil. This process is repeated with the top soil as previously mentioned. They are also building fences where they are needed. They are also doing straw crimping in spread four as a soil erosion prevention method. All previously mentioned are still on-going this week.

Crews were rained out one day this week. Qu'Appelle Valley has been completed. They should be into spread three by the end of this week.

This week I also spent one day with an inspector checking for deficiencies throughout the right of way.




Road 76, kp 416+775, crew was backfilling.








Spreading topsoil SSKP 431+830

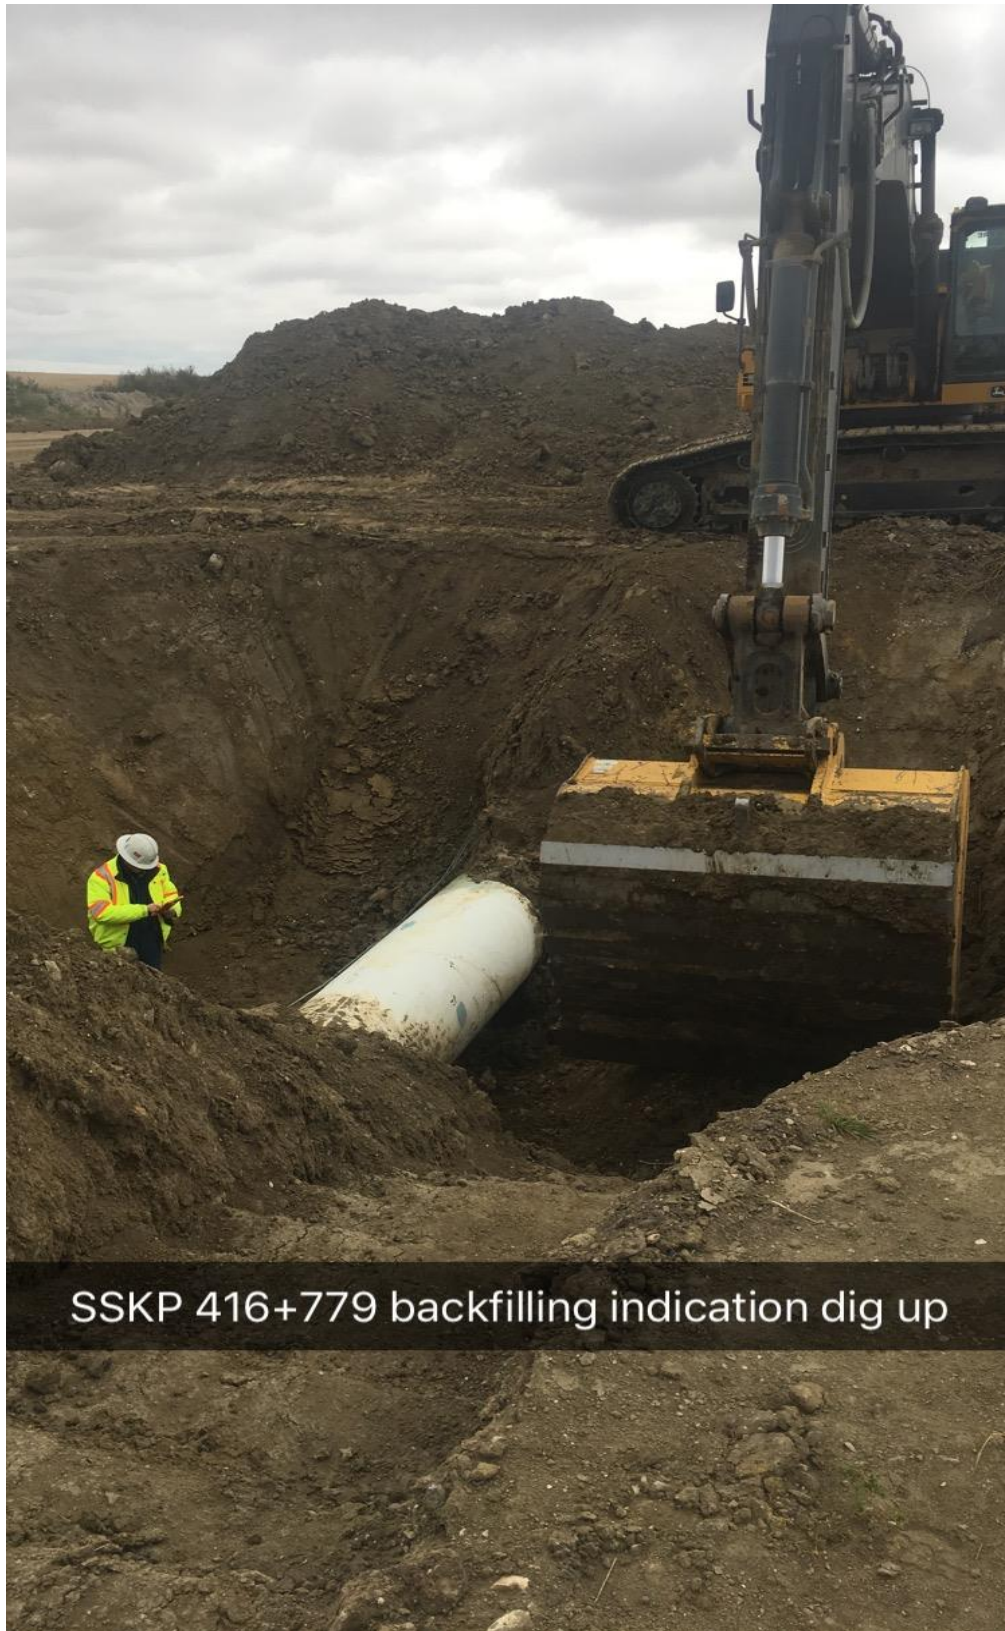

SSKP 416+779 backfilling indication dig up





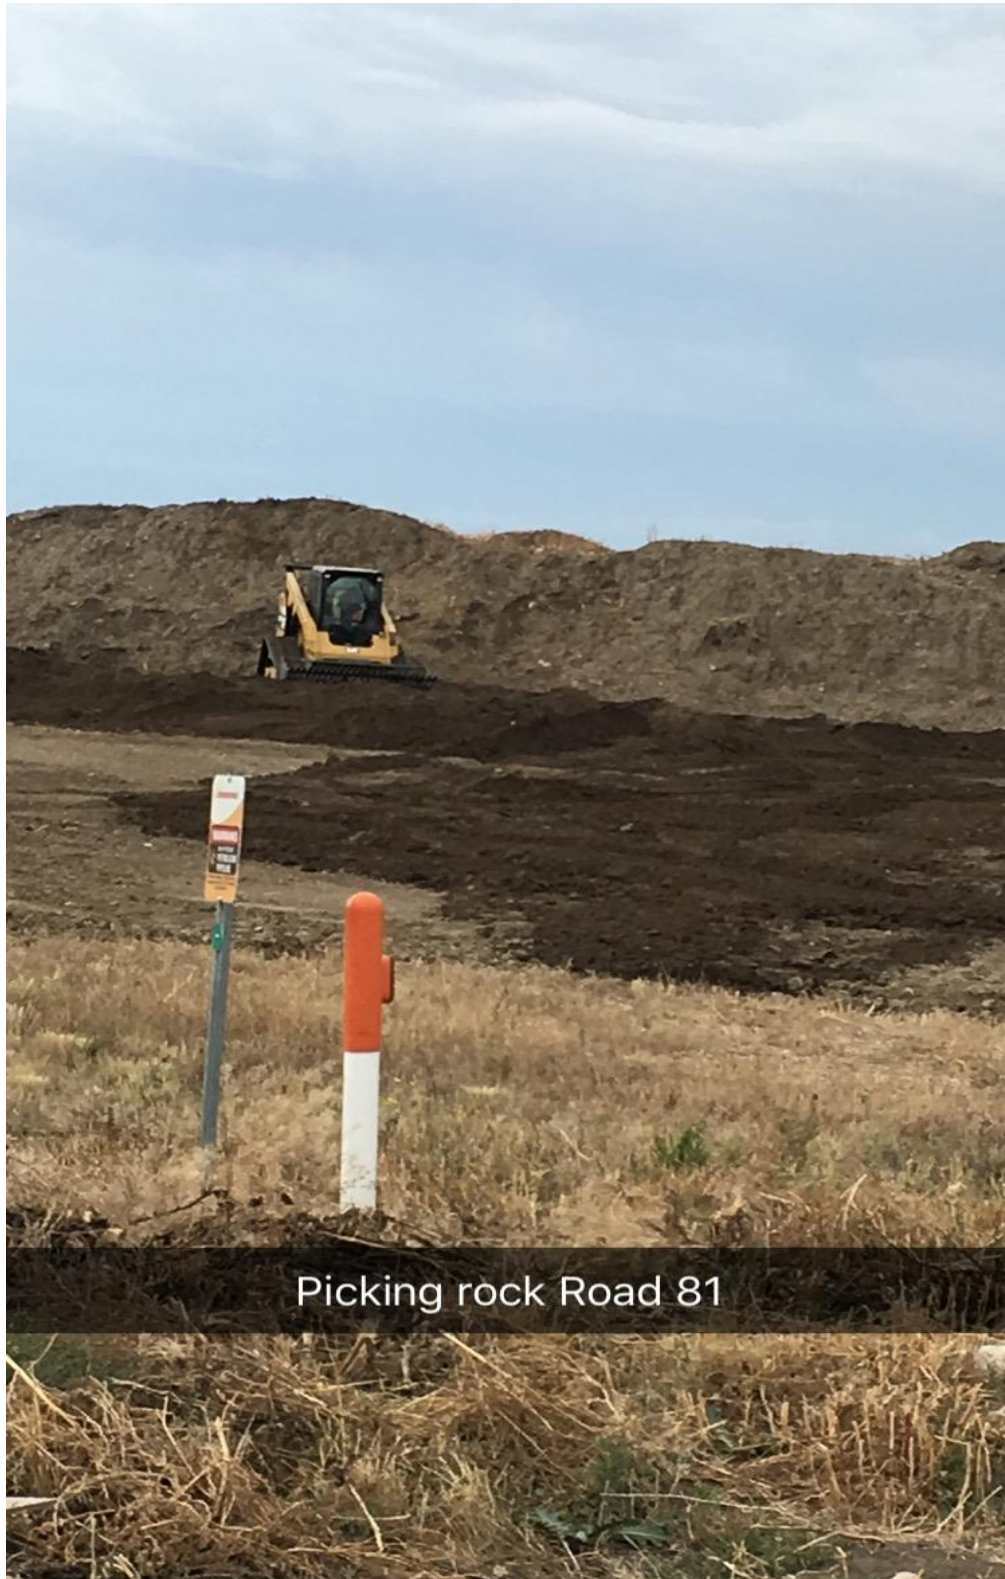



Final disc. Road 78





Loading up equipment road 81

Approvals

Prepared by



Gary Gopher
Senior Construction Monitor

September 16, 2018

Reviewed by



Joseph Roach
Project Manager

September 18, 2018

Approved by



Emmanuel Olotu, P.Eng.
Technical Manager, Geotechnical

September 18, 2018

This document is issued by the Company under its General Conditions of Service available on request and accessible at http://www.sgs.com/terms_and_conditions.htm. Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein. Any other holder of this document is advised that information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility is to its Client and this document does not exonerate parties to a transaction from exercising all their rights and obligations under the transaction documents. Any unauthorized alteration, forgery or falsification of the content of appearance of this document is unlawful and offenders may be prosecuted to the fullest extent of the law.
