



**SGS MUSCOWPETUNG**

**ABORIGINAL CONSTRUCTION MONITORING**

**WEEKLY REPORT**

**SPREAD 3**

**OCTOBER 28<sup>TH</sup> TO NOVEMBER 4<sup>TH</sup>, 2018**

### Social and Cultural Features

Field Observation	# of occurrences	Description and Mitigation Measures	Mitigation Status	Further Action Required (Yes/No)
Traditional Use Area (hunting, fishing, gathering, trapping)	0			
Rock Formations (rocks of significance, tipi rings, etc.)	0			
Artifacts	0			
Bones	0			
Potential Gravesites	0			

### Environmental Features

Field Observation	# of occurrences	Description and Mitigation Measures	Mitigation Status	Further Action Required (Yes/No)
Medicinal or Cultural Plants	0			
Aquatic Life	0			
Animal Observations or Burrows	0			
Bird Nests	0			
Trees (Red Willow)	0			
Wetlands	0			
Watercourse Crossing	0			

## Additional Observations and Summary of Activities or Concerns

This week the pellets have arrived and they began the process to cover the right of way (ROW) throughout the Elbow pasture. They have started on the west side of the river where there are native areas. The pellets consist of paper mulch which are supposed to act as erosion control. The theory is that when they are wet they expand and protect the soil from erosion. Certain areas of the native areas are classified as more susceptible to soil erosion so more pellets are spread throughout these areas for prevention and other areas don't require as much. They have calculated how much is needed per acre of the pellets. The fencing in the elbow pasture is ongoing this week building alley ways and should be completed this coming week. All access roads are officially completed.

The straw and crimping crew are near completion but equipment broke down. They will come back once they are up and running to complete the areas that are needed.


Valve number 10 is completed. They have started constructing chain linked fences at road number 11 and are currently working to construct the chain link at the lower berm station. They will also be constructing chain linked fences at valves 7, 8, 10, 11, 12, and 13 which they are currently awaiting a back order of supplies.



Spreading topsoil Road 38



Spreading pellets Road 38

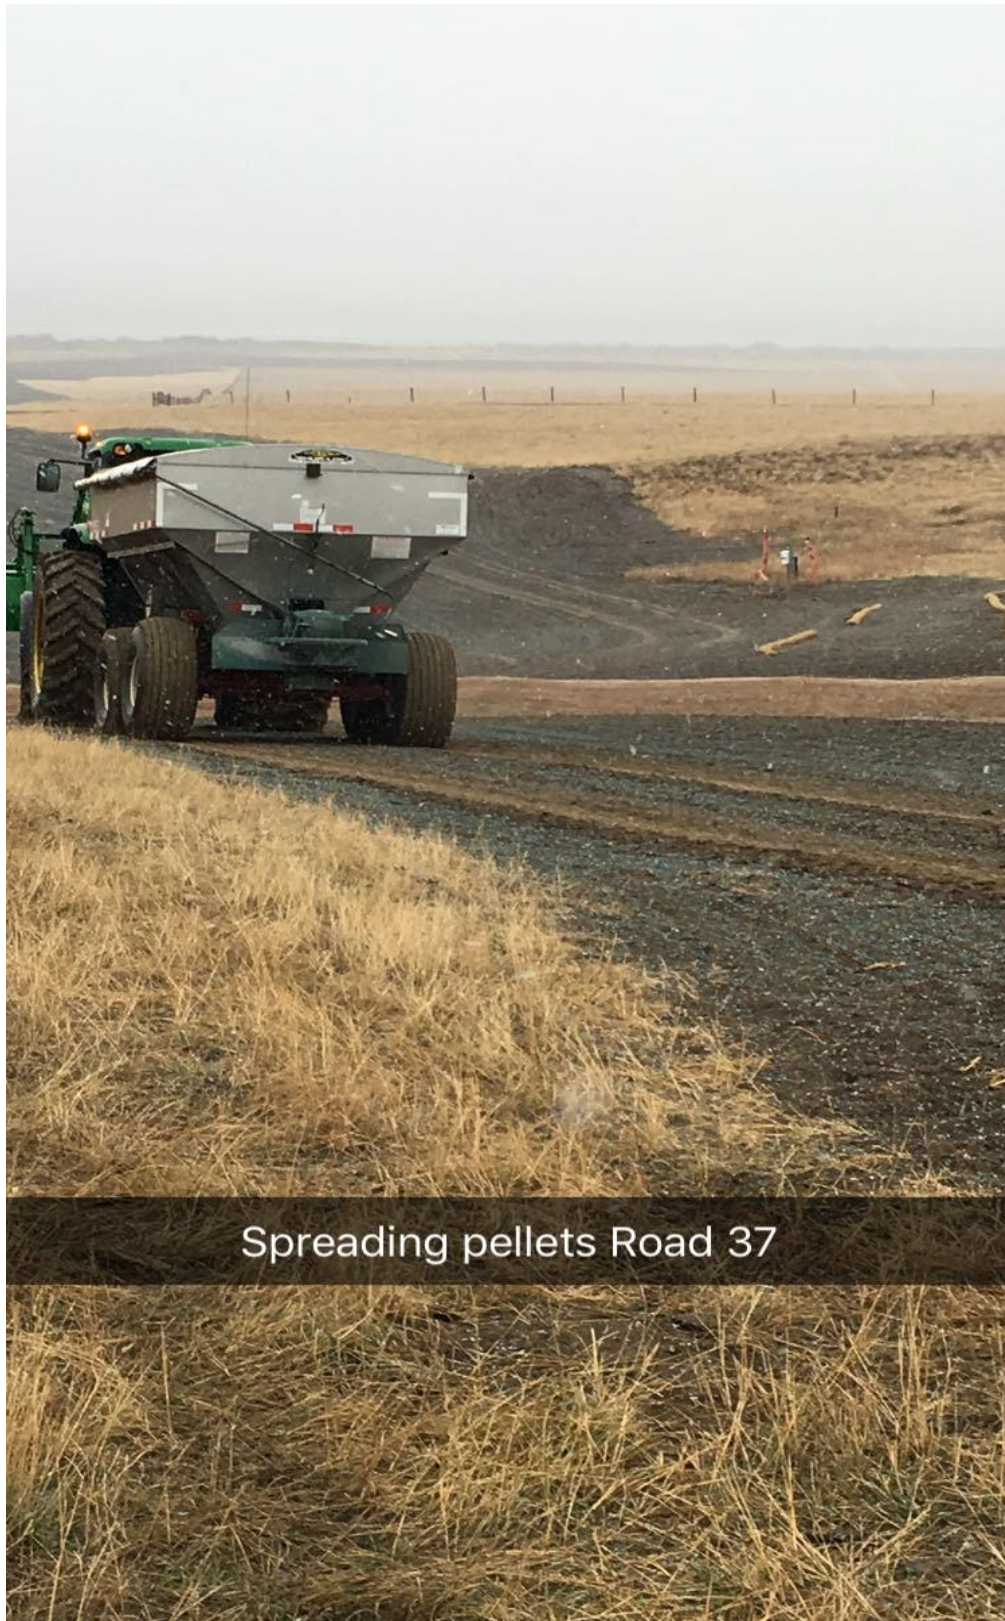



Spreading pellets SSKP 335+900







Finished valve pad Road 38



Loading pellets Road 37



Filling up seeder Road 32



Handing seeding Road 63





Constructing fence SSKP 395+023



Loading pellets Road 38

## Approvals

### Prepared by



---

Gary Gopher  
Senior Construction Monitor

---

November 4, 2018

### Reviewed by



---

Joseph Roach  
Project Manager

---

November 6th, 2018

### Approved by



---

Emmanuel Olotu, P.Eng.  
Technical Manager, Geotechnical

---

November 6th, 2018



This document is issued by the Company under its General Conditions of Service available on request and accessible at [http://www.sgs.com/terms\\_and\\_conditions.htm](http://www.sgs.com/terms_and_conditions.htm). Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein. Any other holder of this document is advised that information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility is to its Client and this document does not exonerate parties to a transaction from exercising all their rights and obligations under the transaction documents. Any unauthorized alteration, forgery or falsification of the content of appearance of this document is unlawful and offenders may be prosecuted to the fullest extent of the law.
