



SGS MUSCOWPETUNG

ABORIGINAL CONSTRUCTION MONITORING

WEEKLY REPORT

SPREAD # 3

AUGUST 20TH TO AUGUST 26TH, 2018

Social and Cultural Features

Field Observation	# of occurrences	Description and Mitigation Measures	Mitigation Status	Further Action Required (Yes/No)
Traditional Use Area (hunting, fishing, gathering, trapping)	0			
Rock Formations (rocks of significance, tipi rings, etc.)	0			
Artifacts	0			
Bones	0			
Potential Gravesites	0			

Environmental Features

Field Observation	# of occurrences	Description and Mitigation Measures	Mitigation Status	Further Action Required (Yes/No)
Medicinal or Cultural Plants	0			
Aquatic Life	0			
Animal Observations or Burrows	0			
Bird Nests	0			
Trees (Red Willow)	0			
Wetlands	0			
Watercourse Crossing	0			


Additional Observations and Summary of Activities or Concerns

This week the indication digs are completed except for one on Road 52. There was a dent underneath the pipe discovered. The engineer inspector measured the pipe and it was not to specifications, so they cut out about three metres of the pipe where the dent was located. They welded a three-metre pup (3 metre length of pipe) onto the pipe where the dent was removed. Currently awaiting to pass x-ray on the weld and coating of the pipe, then backfill will be completed.

The weed control is still ongoing and they are currently at road 37 which they had reached the river. The fencing and the reseeding of spread 3 is now completed.

Valve number 11 and 12 were completed this week with both being backfilled. Now all valves have been backfilled on spread three.



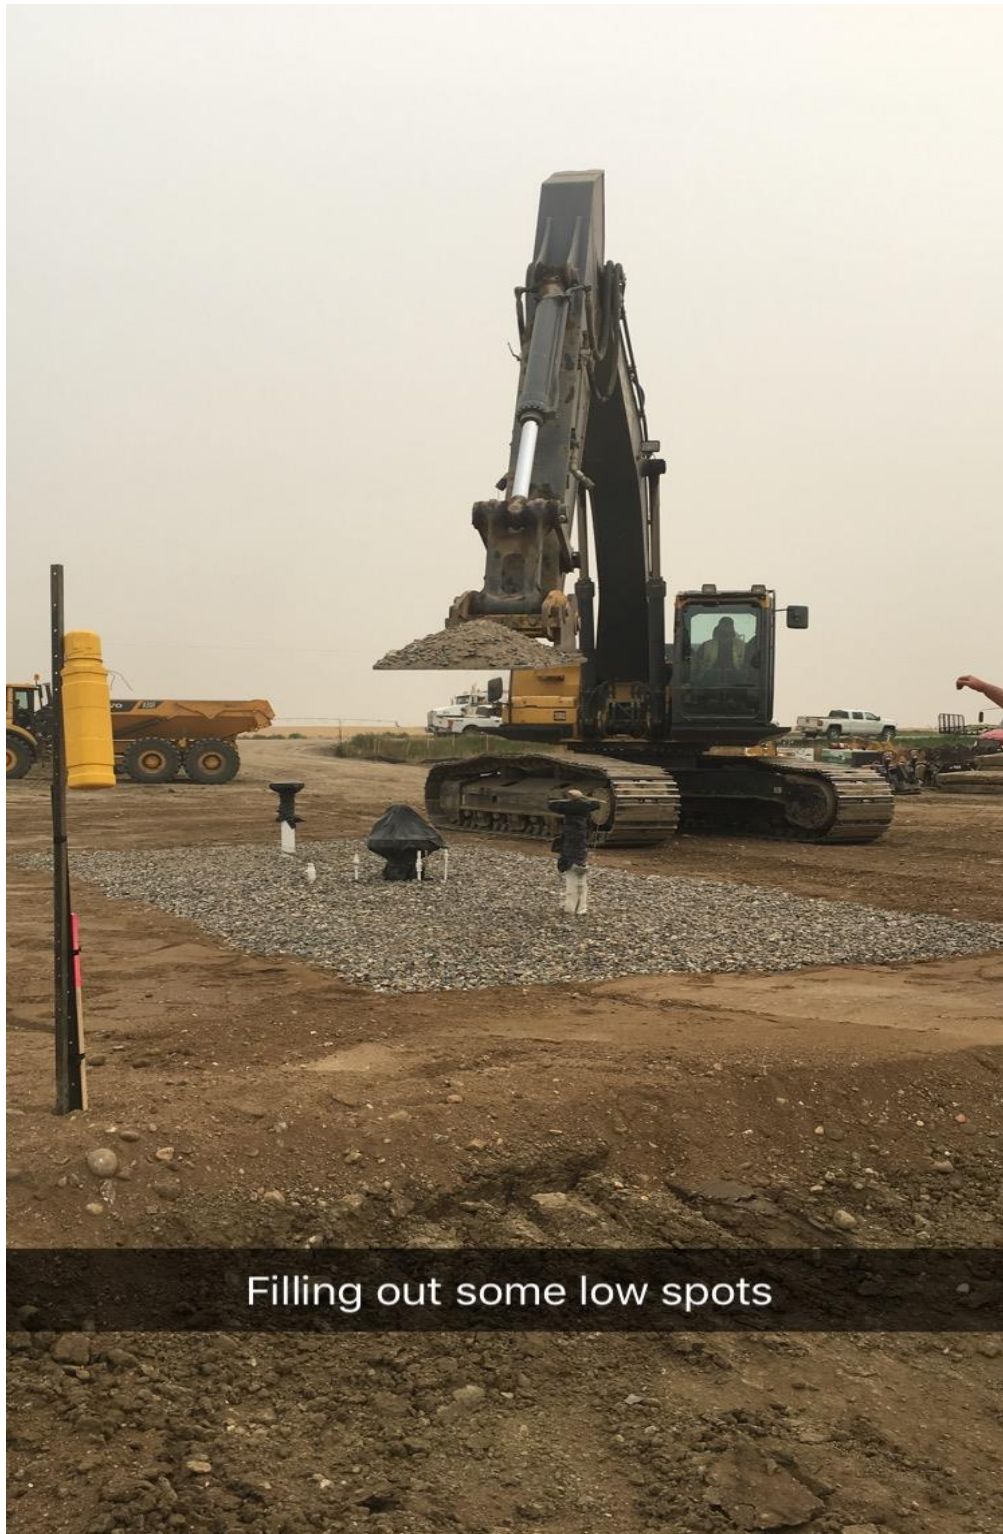

Filling out some low spots





Compacting MLBV #12



Sandblasting. SSKP 360+750



Weed control Road 36



Pounding posts. Road 64



Weed control. Road 20



Compacting crushed rock around valve



Daylighting line MLBV #9



Compacting MLBV #12

Approvals

Prepared by



Gary Gopher
Senior Construction Monitor

August 26, 2018

Reviewed by



Joseph Roach
Project Manager

August 29, 2018

Approved by



Emmanuel Olotu, P.Eng.
Technical Manager, Geotechnical

August 29, 2018

This document is issued by the Company under its General Conditions of Service available on request and accessible at http://www.sgs.com/terms_and_conditions.htm. Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein. Any other holder of this document is advised that information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility is to its Client and this document does not exonerate parties to a transaction from exercising all their rights and obligations under the transaction documents. Any unauthorized alternation, forgery or falsification of the content or appearance of this document is unlawful and offenders may be prosecuted to the fullest extent of the law.
